


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7308
TRUNK HIGHWAY 28
COUNTY Stearns
DISTRICT 3A

LIMITS: N. Jct. T.H. 71- N. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION		REMARKS	CODE N°
		TYPE	WIDTH THICKNESS		
1919	28-28-1	Grading Gravel	16' 2 1/2"	Co. Job 1908 800 C.Y./Mile.	
1922	28-28-21	Grading Gravel	24' 20' 3"	1200 C.Y./Mile.	
1928	28-28-30	Grading Gravel	32' 24' 2 3/4"	1300 C.Y./Mile.	
1928	28-28-30	Oil Tr. Gravel	24' 1"	12475 Gal./Mile. Maint. Dept.	
1933	28-28-30	Oil Tr. Gravel	24' 1"	Maint. Dept.	
1933	28-28-21	Oil Tr. Gravel	24' 1"	Maint. Dept.	
1936 A.F.E. 7 1937 A.F.E. 14		Subgrade Lift	28'	Maint. Dept.	449
1938	A.F.E. 36	Mixed Bit. Surf.	24' 1"	Maint. Dept.	449
M 1942	A.F.E. 5	Bit. Seal Coat	24'	RT-6, 2445 Gal./Mi. Agg. 78 C.Y./Mi. Maint. Dept.	449
M 1945	A.F.E. 4	Bit. Surf. Repair	24'	MC-2, 7208 Gal./Mi. Grav. 379 C.Y./Mi. Maint. Div.	449
M 1947	A.F.E. 4	Bit. Fog Seal	24'	MC-2, 3439 Gal.	449
M 1948	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'	MC-3&5C-3, 14336 Gal. Agg. 831 C.Y.	449 (Net 1.95)
M 1950	A.F.E. 4	Bit. Fog Seal	24'	KC-1, 2783 Gal. Agg. 149 C.Y.	449
M 1952	A.F.E. 4	Bit. Surf. Repair	24'	SC-3, 3682 Gal. Agg. 3136 Tons	449

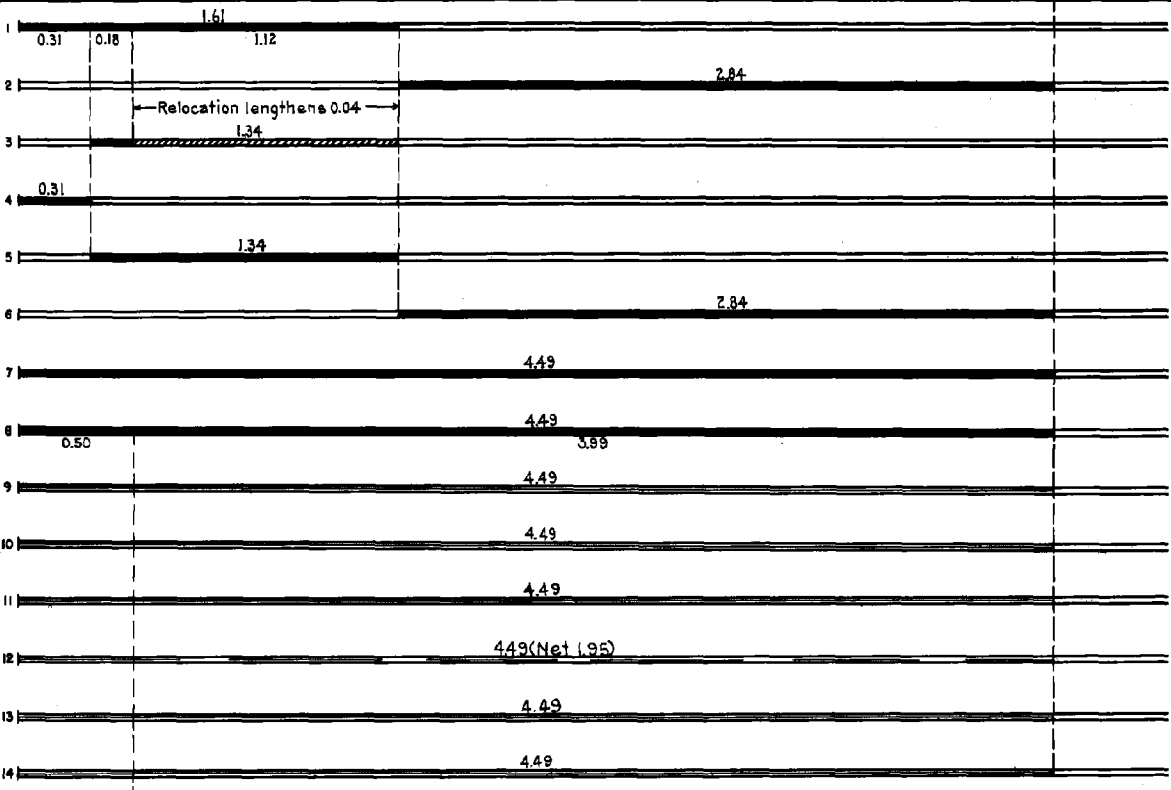

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1922	1927	4.45	4.45	0.00	0.00	0.00	4.45	0.00	0.00	0.00
1924	1956	4.49	4.49	0.00	0.00	0.00	4.49	0.00	0.00	0.00
1957		4.34	4.34	0.00	0.00	0.00	4.34	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1928

(1) This work not done under these project numbers but lies within the limits of these projects.

