


PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7326
TRUNK HIGHWAY 22
COUNTY Stearns
DISTRICT 3B

LIMITS: S.Co.Line in Eden Valley - Jct. T.H. 23 in Richmond
Ref. Pt. 157+00.139 - 167+00.063



YEAR BUILT	PROJECT NO	DESCRIPTION			
		TYPE	WIDTH	THICKNESS	REMARKS
		Mixed Bit. W10D & W46	24'-6"		No Record of Const. Added in 1959.
		Br. 7134 & Br. Gravel	22'-32"		213' B.S. & 20' B.S. No Record of Const. Added in 1959.
		W86 Culvert			
C&M	1960	Road Mix Bit. Surt. Bit. Resurfacing	24'	1 1/2"	By Maint. Dist.
C	1961	Ditch Grading Gravel Surface	22'		By Maint. 2181 Tons
C	1963	Reshaping Sub. Gravel Base Mixed Bit.	32'	6"	By Maint. Bit. Mix 8255 Tons Mc-2 Prime 35352 Gal.
M	1965	C Light Bit. Seal	24'		RS-1C, 19,258 Gal. FA-1, Seal Coat Agg. 648 C.Y.
C	1976	7326-05 Bit. Resurfacing RS 469(1)	24'-6"	2 1/4"	
M	1980	SF Bit. Surfacing	24'	1 1/2"	Spot Location
M	1983	SF Culvert Replacements			7 Culverts Contract No. 4022
M	1984	SF Spot Bit. Overlay	24'	2"	Sp. 2341 976 Tons
M	1984	SF Spot Bit. Overlay	24'	1"	Sp. 2341 1146 Tons
C	1989	7326-10 Spot Overlay		1 1/2"	Spec. 2341
M	1992	M4508 Bit. Overlay	Var.	Var.	Spec. 2331
M	1992	SF Bit. Overlay	28'	1 1/2"	Spec. 2331

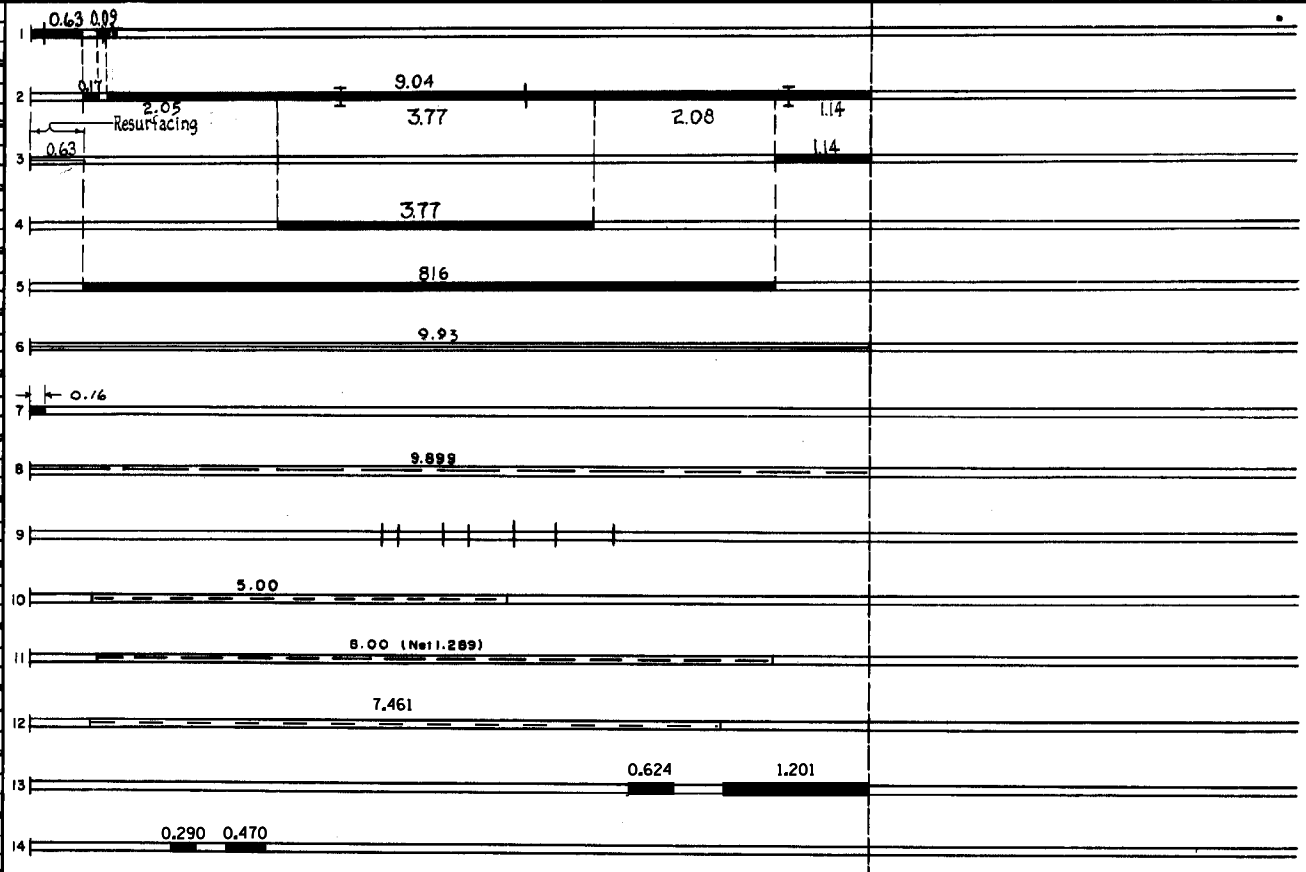

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1958	1974	9.93	9.38	0.04	0.51	0.00	9.89	0.04	0.00	0.00
1975		9.93	9.13	0.04	0.76		0.89	0.04		

REMARKS: Layout is to scale as of 1959.

