


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8215
TRUNK HIGHWAY 100
COUNTY Washington
DISTRICT 9A

LIMITS: W. End of Bridge (Miss. River) in St. Paul Park - Jct. T.H. 61
in Newport



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1938		Mixed Bit. Br. 5600	24' 17'	1 1/2"	No Record of Constr. Added in 1938. 1736 W.P.T. B.S. 26 & HT.
C	A.F.E. 28	Mixed Bit.	24'	1 1/2"	Over existing street. Maint. Dept.
M	A.F.E. 33	Bit. Retreat	24'		RT-6, 8190 Gal./Mi. Grav. 704 C.Y./Mi. Maint. Dept.
M	A.F.E. 5	Bit. Seal Coat	24'		RT-10, 2264 Gal./Mi. Sand, 82 C.Y./Mi. Maint. Dept.
M	A.F.E. 5	Bit. Seal Coat	24'		RT-10, 3508 Gal. Agg. 135 C.Y.
		Mixed Bit.	22'		No Record of Constr. Village street taken over in 1949.
C	8205-10	Grading	44'		Divided Highway
1949	8205-15	Concrete	44'	9-79	
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-3, 1888 Gal. Agg. 101 C.Y.
M	A.F.E. 4	Light Bit. Seal	24'		RT-B, 2711 Gal. Agg. 74 C.Y.
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-3, 5784 Gal. Agg. 380 C.Y.
M	A.F.E. 5	Light Bit. Seal	24'		RT-8, 2806 Gal. Agg. 87 C.Y.
M	A.F.E. 604	Spot Treat. Bit. Surf. Repair	22'		Bit. 12073 Gal. Agg. 959 Tons Fog Seal (1.95 Mi)
M	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		Bit. 6509 Gal. Agg. 627 Tons
M	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		Plant Mix 346 Tons

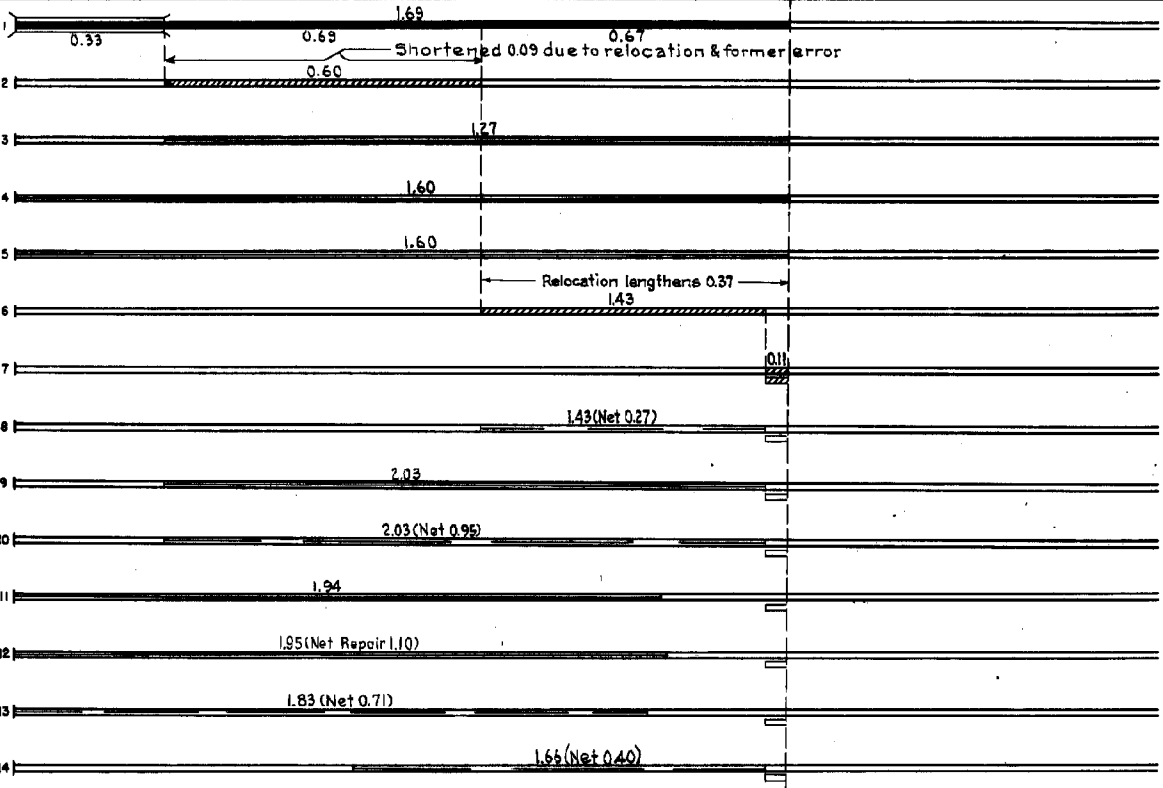

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1938	1939	1.69	0.00	0.00	1.33	0.36	1.15	0.00	0.18	0.36
1940	1946	1.60	0.00	0.00	1.27	0.33	1.09	0.00	0.18	0.33
1949	1950	2.47	0.00	0.00	2.14	0.33	1.96	0.00	0.18	0.33
1951		2.47	0.00	0.00	2.14	0.33	0.00	0.00	2.14	0.33

REMARKS: Layout is to scale as of 1938
(1) Contract not final but work substantially complete in 1949.

