


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8407
TRUNK HIGHWAY 75
COUNTY Wilkin
DISTRICT 4A

LIMITS: Jct. T.H. 9 W. of Doran - N. Jct. T.H. 210 N. of Breckenridge

YEAR BUILT	PROJECT N#	DESCRIPTION			CODE N#
		TYPE	WIDTH	THICKNESS	
C	8407-07				On old concrete
1952	8407-08	Plant Mix Bit.	22' 3 1/2"		
C	8406-06	Concrete	24'	9'-9"	0106D 22'
1959		Br. 9315			By Br. Crew No. 3
C		Replace Portals & raise lower Cross-frames on Br. 4816			
1960					
C		Construction of Roadside Park			By Maint.
1961					
M		Light Bit. Seal	23'		RS-2, 4880 Gal. Agg. 170 C.Y.
1962					
C		Concrete	20'	9'-9"	Transferred from C.S. 8408
1937					
C&M	8407-13	Pl. Mix. Bit. Surf.	22'	1 1/2"	5/8 Pl. Mix. Bit. placed on 0.67 mi.
1968		Rt. Turn Lane	12'		
		Escape Lane	12'		
M	SF	Bit. Seal	24'		MC-800, 2000 Gal. Agg. 275 C.Y.
1968					
C	-22	Agg. Base*	36'		* Pertaint to new Rdwy. only. 1/2 Pl. Div.
	RF 006-3(94)	P.C. Conc.*	48'	8"	
		Pl. Mix Bit Shldrs.			Mix Bit. on old Rdwy.
C	-18	Grading Bit. Base	24'	3"	
	HHS 006-2(55)	Pl. Mix Bit. Surf. Gr. Shldrs.	10'		
M	1975	SF	Joint Seal		6650 lbs.
1976	8407-23	Pl. Mix Bit. Seal	VAR	3/4"	Bit. Spec. 2341
1981	8407-26	Agg. Shoulders	3"		
1982	SF	Bit. Shoulders	10'	4"	SBL 686 Ton

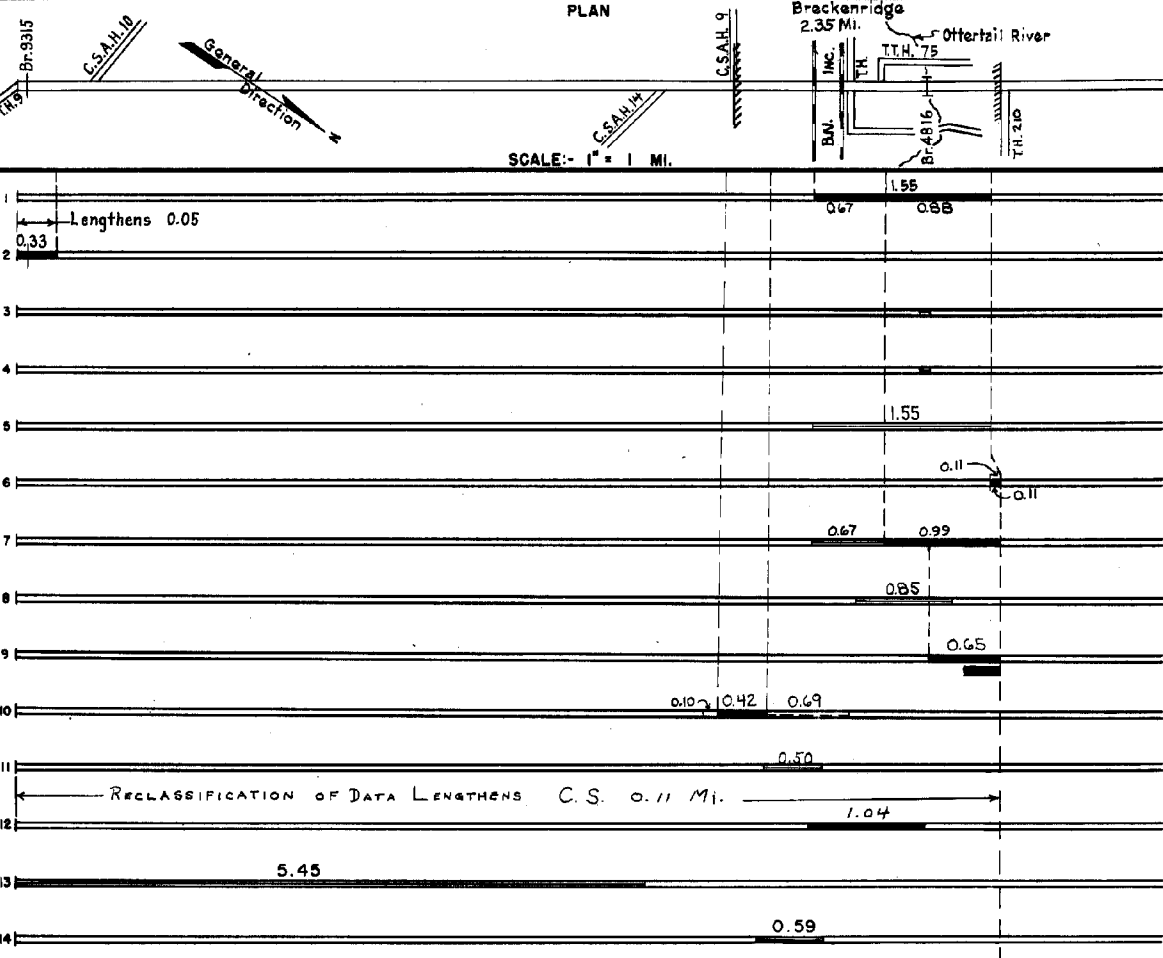

YEARS FROM	TOTAL TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS: See Sheet No. 1
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	

