



PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8704  
TRUNK HIGHWAY 59  
COUNTY Yellow Medicine  
DISTRICT 8B


LIMITS: Jct. I.H. 67 in Clarkfield - N. Co. Line

Ref. Pt. 097+00.742 - 104+00.797

Clarkfield  
0.51 Mi.

PLAN

YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION				CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	REMARKS	
C	8704-02	Grading 5" Sub. Gravel C86x40	36' 28'	2"	1200 C.Y.	
M	A.F.E. 6	Grav. Resurfacing (Spots)			2005 C.Y.	
C	A.F.E. 7	Seeding				
M	A.F.E. 6	Grav. Resurfacing (Spots)			1053 C.Y.	
C	8704-03	Gravel Base Plant Mix Bit.	30' 24'	9" 1 1/2"		
M	A.F.E. 605	Light Bit Seal	24'		AERS-2, 12334 Gal. Agg. 623 Tons	
M	A.F.E. 604	Bit. Surf. Repair	24'		SG-3, 2886 Gal. Agg. 224 Tons	
C	8704-05	Plant mix bit base Plant mix bit.	24' 24'	1 1/2" 3"		
M	C	Light Bit Seal	25'		RS-1C, 15760 Gal. Agg. 570 C.Y.	
C	8704-08	Grade Base Pl. Mix Bit Surf.	44'	2 1/2" 3"	Also B & 24 C & E	
C	8704-10 RF 017-2 (32)	Pl. Mix Bit Surf. Gravel Shldr.	24'	3" 3"		
M	5F	Crack Joint Seal			200 Ln. Ft.	
M	M97128	Spot Overlay	24'	1 1/2"	Spec. 2341	
M	8704	Agg. Seal			Fine Agg. Number 2	

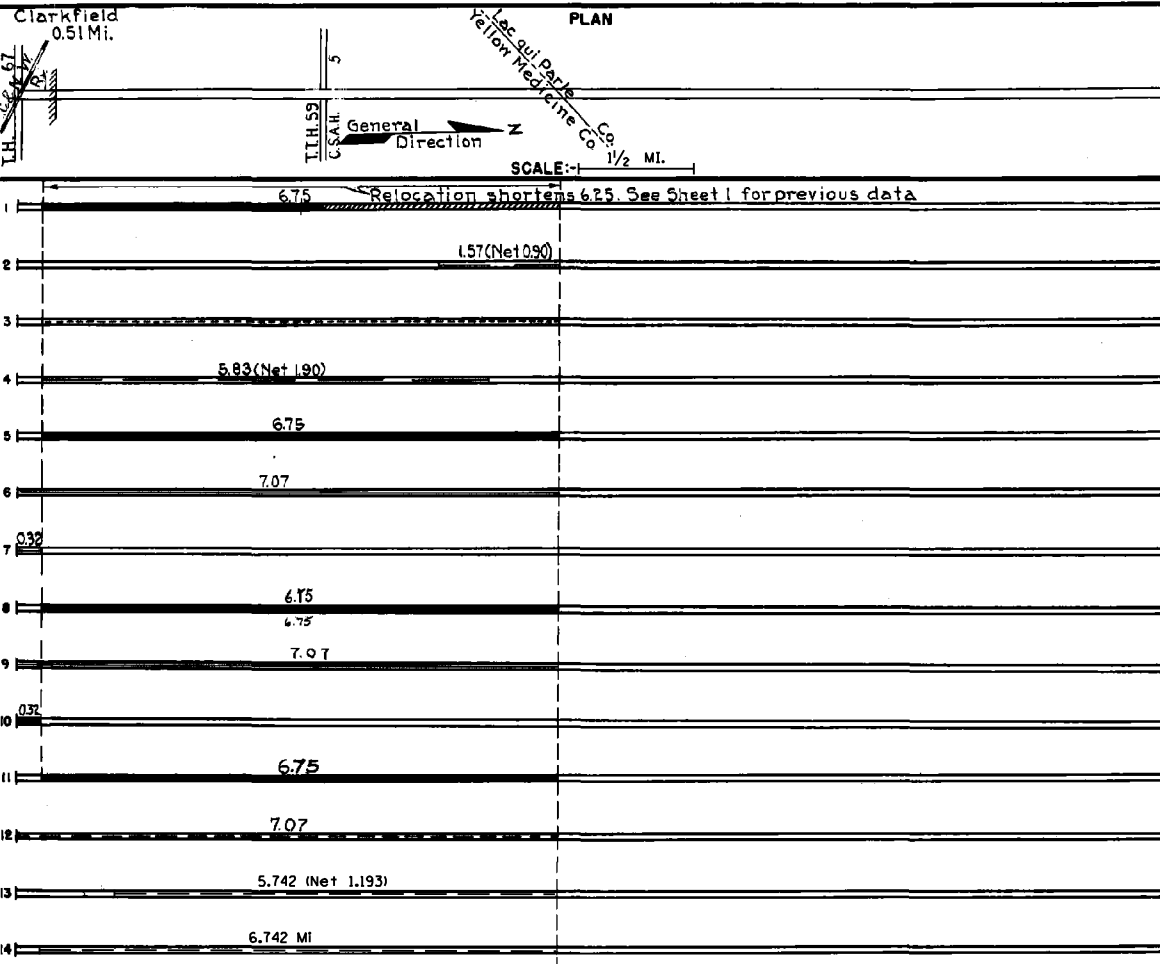

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1948	1950	7.07	6.56	0.00	0.51	0.00	7.07	0.00	0.00	0.00
1951		7.07	6.56	0.00	0.51	0.00	6.56	0.00	0.51	0.00

REMARKS: Layout is to scale as of 1948.

