

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1504
TRUNK HIGHWAY 200
COUNTY Clearwater
DISTRICT 2A

LIMITS: West Co. Line - Jct. T.H. 92

White Earth Indian Reservation PLAN

Clearwater
Kalmien
Co.

Bound.
Res.


General
Direction

T. H. 92

C.S.A.H. 7

SCALE: 1" = 1 MI.

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST.
		TYPE	WIDTH	THICKNESS	
		Gravel Br. 4386	20' 18'	1"	No Record of Constr. Added in 1934 54 W.P.T.
1938	A.F.E. 16	Grading Remove Br. 4397	30'		Maint. Dept.
1941	1504-01	Grading			W.P.A.
1942	1504-02	Br. 4396	26'		Rebuild old Br. 4396 45 W.P.T. Br. Crew & W.P.A.
1942	A.F.E. 6	Reshape & Gravel	24'		737 C.Y./Mi. Maint. Dept.
1943	A.F.E. 6	Grav. Resurface			1327 C.Y./Mi. Maint. Dept.
1954	1504-04	Grading Select Granular Matl	30'	12"	353
1954	1504-05	Mixed Bit (Bit. Sub. Base)	24'	2"	454
1956	A.F.E. 817	Bit Surfacing Mixed Bit	26'	1"	MC-3 83723 Gal. Agg. 4249 Tons Spot Base Repair
1959	A.F.E. 604	Bit Surf. Repair	24'		MC. 2200 Gal. Agg. 176 Tons
1961		Regravel Shoulders Light Bit. Seal	Var. 27'	Var.	5447 Tons (Gravel) RC-2, 16164 Gal. Agg. 580 C.Y.
1977	1504-08	P.Mix Bit Surf. GRAV. SHOULDERS	24' 3'	VAR.	1276
1968	SF	LIGHT BIT. SEAL			RC-250 15440 GAL Agg. 555 C.Y.
1972	1504-06	PLATE BEAM GUARDRAIL FOR BR. No. 4396			515 LIN. FT.

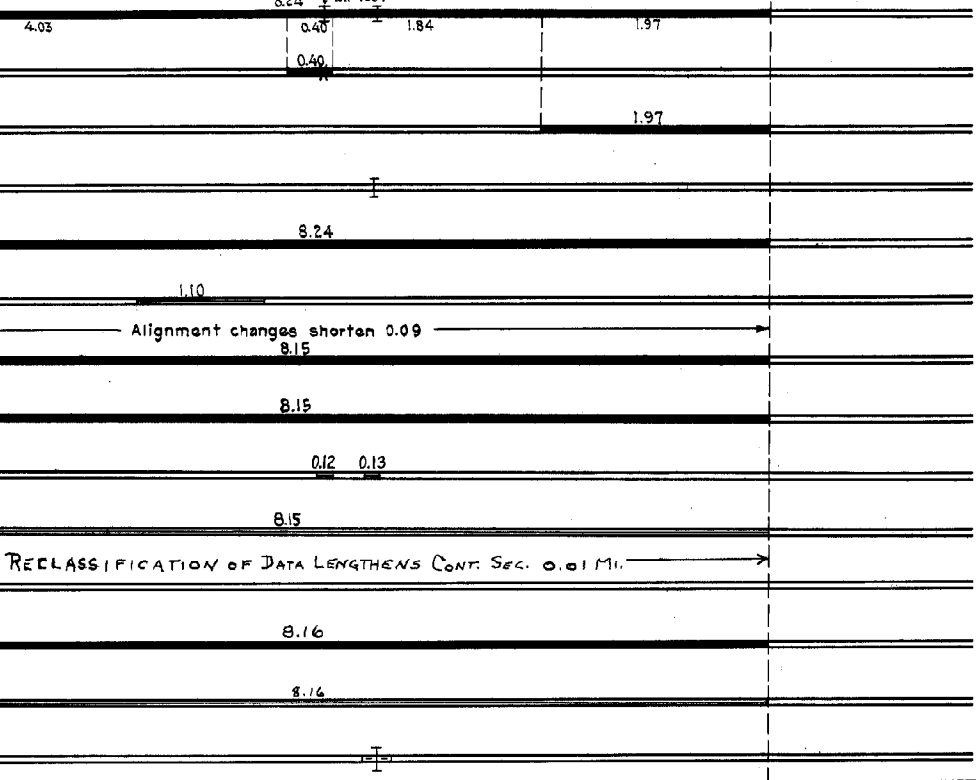

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1937	8.24	8.17	0.07	0.00	0.00	8.17	0.07	0.00
1938	1953	8.24	8.25	0.01	0.00	0.00	8.25	0.01	0.00
1954	1976	8.15	8.14	0.01	0.00	0.00	8.14	0.01	0.00
1977		8.16	8.15	0.01	0.00	0.00	8.15	0.01	0.00

REMARKS: Layout is to scale as of 1934

