


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1507
TRUNK HIGHWAY 92
COUNTY Clearwater
DISTRICT 2A

LIMITS: Jct. T.H. 2 in Bagley - West Co. Line
056+00.737 - 035+00.977



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	24'	2"	No Record of Constr.
1922	92-65-21B	Grading	32'		122
1923	92-65-21B	Gravel	24'	3 3/4"	1800 C.Y./Mile
1930	92-65-22B	Grading Br. 1057 Br. 1688	32'		W 108 D W 108 D 130
1931	92-65-22B	Gravel	24'	2"	900 C.Y./Mile
1932	92-65-21B	Top Tr. Gravel	26'	1 1/2"	14273-20431 Gal./Mi. Maint. Dept.
1932	92-65-22B	Oil Tr. Gravel	26'	1 1/2"	20431 Gal./Mile Maint. Dept.
1938	A.F.E. 17	Gravel Base Mixed Bituminous	25' 25'	5" 1 1/4"	Maint. Dept.
1942	A.F.E. 4	Bit. Retreat & Grade Lift	24'		RT-5, 21429 Gal./Mi. Grav. 5109 C.Y./Mi. Maint. Dept.
1943	A.F.E. 4	Bit. Fog Seal	26'		RC-3, 2406 Gal./Mi. Grav. 139 C.Y./Mi. Maint. Dept.
1943	A.F.E. 4	Spot Treat. Bit. Surf. Repair	28'		RT-5, 2438 Gal./Mi. Grav. 133 C.Y./Mi. Maint. Dept.
1944	A.F.E. 5	Bit. Seal Coat			RT-5, 2880 Gal./Mi. Grav. 44 C.Y./Mi. Maint. Div.
1945	A.F.E. 32	Spot Treat. Bit. Surf. Repair			RT-5, 388 Gal./Mi. Grav. 23 C.Y./Mi. Maint. Div.
1946	A.F.E. 21	Gravel Lifts (Spots) Bit. Resurfacing Mixed Bit.	24' 24'	6" 1"	RT-5, 154744 Gal. Added Agg. 7728 C.Y.

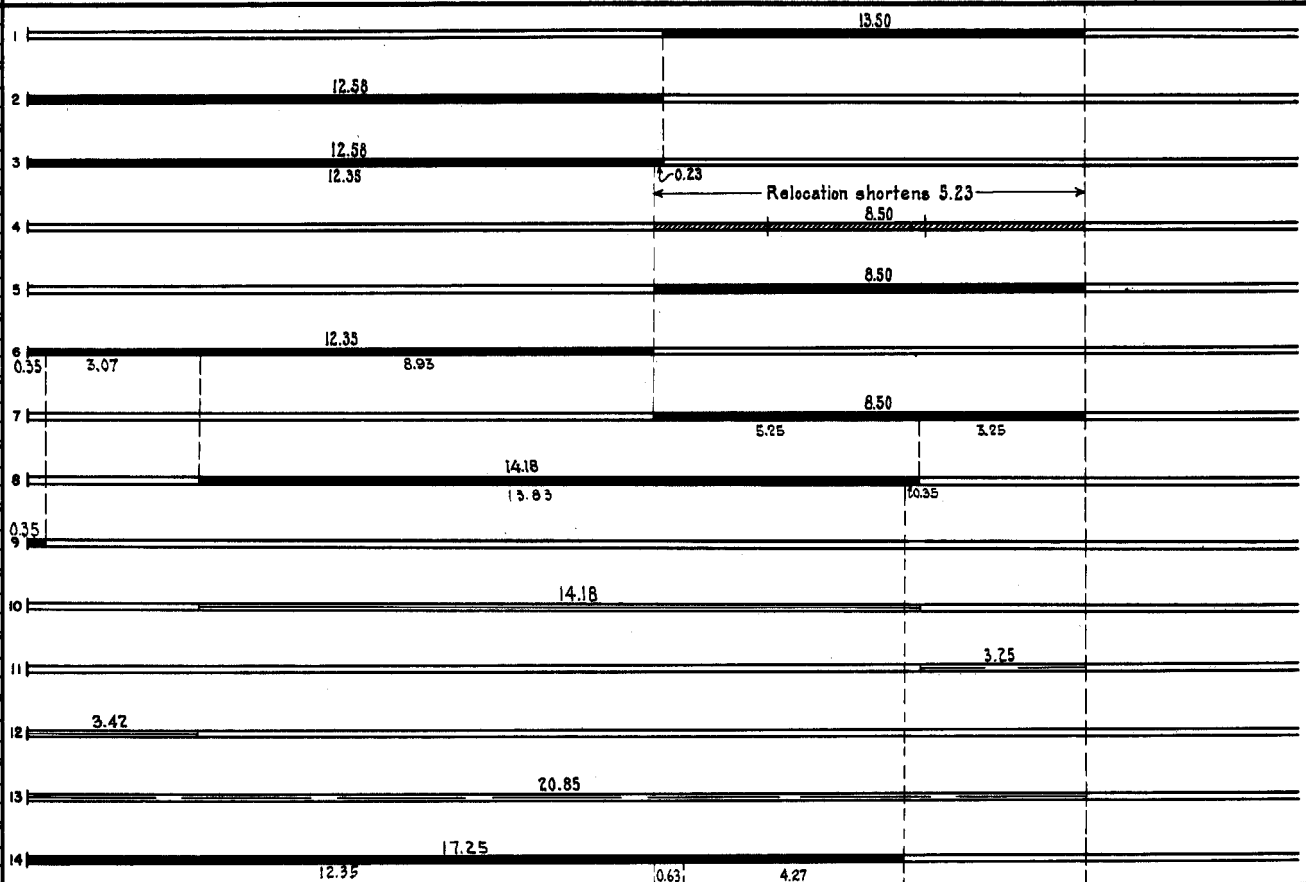

YEARS FROM	TOTAL TO	MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1922	1929	26.08	23.52	0.00	2.56	0.00	26.08	0.00	0.00	0.00
1930	1939	20.85	19.01	0.00	1.84	0.00	20.85	0.00	0.00	0.00
1940	1939	20.85	19.15	0.00	1.70	0.00	20.32	0.00	0.53	0.00
1960	1967	20.85	18.80	0.00	2.05	0.00	20.32	0.00	0.53	0.00
1968		20.73	18.68	0.00	2.05	0.00	20.20	0.00	0.53	0.00

REMARKS: Layout is to scale as of 1930


(1) This work not done under these project numbers but lies within the limits of these projects

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1507
TRUNK HIGHWAY 92
COUNTY Clearwater
DISTRICT 2A

LIMITS: Jct. T.H. 2 in Bagley - West Co. Line
056+00.737 - 035+00.977



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° DIST
		TYPE	WIDTH	THICKNESS	
M		Spot Treat.			
1946	A.F.E. 4	Bit. Surf. Repair			
		Spot Seal Coat			
C		Gravel Lift	28'	7"	(Mixed Prime)
1948	A.F.E. 20	Bit. Surfacing	28'	2"	SC3, 56176 Gal.
		Mixed Bit.			Agg. 19988 Tons
M		Bit. Seal Coat	24'		RCS-082, 29919 Gal.
1949	A.F.E. 5	Bit. Seal Coat	24'		Agg. 755 C.Y.
M		Bit. Fog Seal	24'		RCS-1, 13426 Gal.
1950	A.F.E. 4	Bit. Fog Seal	24'		Agg. 327 C.Y.
M		Spot Treat.			MC3, 7200 Gal.
1951	A.F.E. 4	Bit. Surf. Repair	24'		Agg. 635 C.Y.
		Spot Seal Coat	24'		
M		Spot Treat.			MC3, 8759 Gal.
1952	A.F.E. 4	Bit. Surf. Repair	24'		Agg. 471 C.Y.
M		Spot Treat.			MC3, 3400 Gal.
1953	A.F.E. 604	Bit. Surf. Repair	24'		Agg. 245 Tons
C		Bit. Resurfacing	24'	1" added	MC2, 108100 Gal.
1953	A.F.E. 819	Mixed Bit.	24'		Agg. 9008 Tons
C		Grav. Base (M. Pt. 0.22)	44.5'	6"	
1953	1507-01	Mixed Bit.	44.5'	2"	
		Concrete ("0.00-0.22")	60'	8"	
M		Spot Treat.			Bit. 3600 Gal.
1958	A.F.E. 604	Bit. Surf. Repair	24'		Agg. 297 Ton
C		Grading			
1960	1507-07 & 10	Gravel Base	35'	1 1/2" (100%)	1259
		Road Mix Bit. (Base)	26'	1 1/2"	139,467 Gal. Bit. Mat.
C/M	By Maint.	Bituminous Sidewalk	4'		West Side M. Pt. 0.56-0.81
1961		Bit. Surf. Repair	24'		7985 Gal. Bit. Agg. 336 Tons
M		Light Bit. Seal	27'		RS-2K, 14838 Gal.
1963		Light Bit. Seal	27'		Agg. 510 C.Y.
C		Grading, Gravel			
1968	1507-11	Base, Bit. Base	24'-52'	1 1/2"	Bit. Mat. 880 Ton

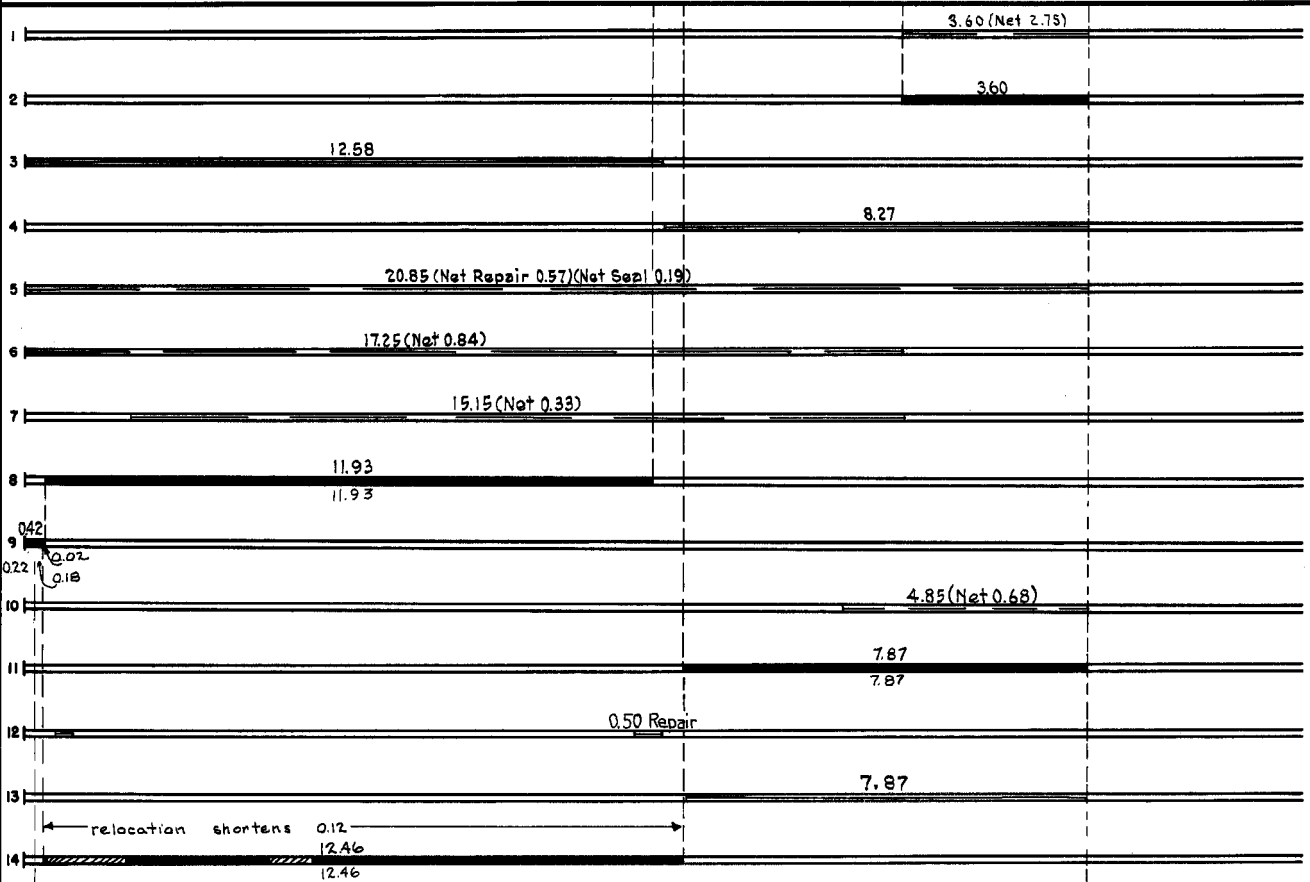

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1.

