


PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2180B
Interstate TRUNK HIGHWAY 94
COUNTY Douglas
DISTRICT 4B

LIMITS: Jct. T.H. 114 - E. Co. Line

YEAR BUILT	PROJECT NO	DESCRIPTION	WIDTH	THICKNESS	REMARKS
C	2180-0709&10	Grading			Divided Highway
1967	2180-21807&106	Br's 21805 & 21806	38' & 38'		Both 125' B.S.-O.H.
	2180-21807	Br. 21807			275' B.S.-U.P.
C	2180-27&28	Sub-base & Base P.C. Concrete	2 @ 24"	9"	
C	2180-21813&14	Br's 21813 & 21814			Both 235' B.S.-U.P.
1967	2180-21815&16	Br's 21815 & 21816	38' & 38'		Both 140' B.S.-O.H.
	2180-21817&18	Br's 21817 & 21818	38' & 38'		Both 111' B.S.-O.H.
C	2180-21819	Br. 21819			212' B.S.-U.P.
1967	2180-21820	Br. 21820			212' B.S.-U.P.
	2180-21821	Br. 21821			285' B.S.-U.P.
M	1976	2180-SF			13800 TONS H SPEC #135- 48 PAISLS #157-87; #136- 135; #155-11
M	1977	2180-SF			JOINT SEAL
M	1980	2180-21821	35.75'		Bridge Repair
	1094-2109114				
C	1981	2180-62			Gene. Pavt. Repair
	1094-2117081				
C	1981	2180-21815			Br. Deck Repair & Overlay
	1094-2117081	21815, 21816			
	1094-2117081	21817, 21818			
C	1982	2180-21805			Br's 21805, 21806 21807, 21810
		Br. Deck Overlay	30'	2"	Br's 21813, 21814
1983	2180-21813	Br. Deck Widening	38'-5"	2"	Br. 21814
M	1984	2180-60			130.8 Mi. For 1402-11, 1480-86, 2180-60, 2680-28 5680-91, 6480-21
	SF	Safety Improvement & Traffic Barrier			
M	1984	SF	9'	1-1/2"	Sp. 2341 22 Tons E.B. under T.H. 127

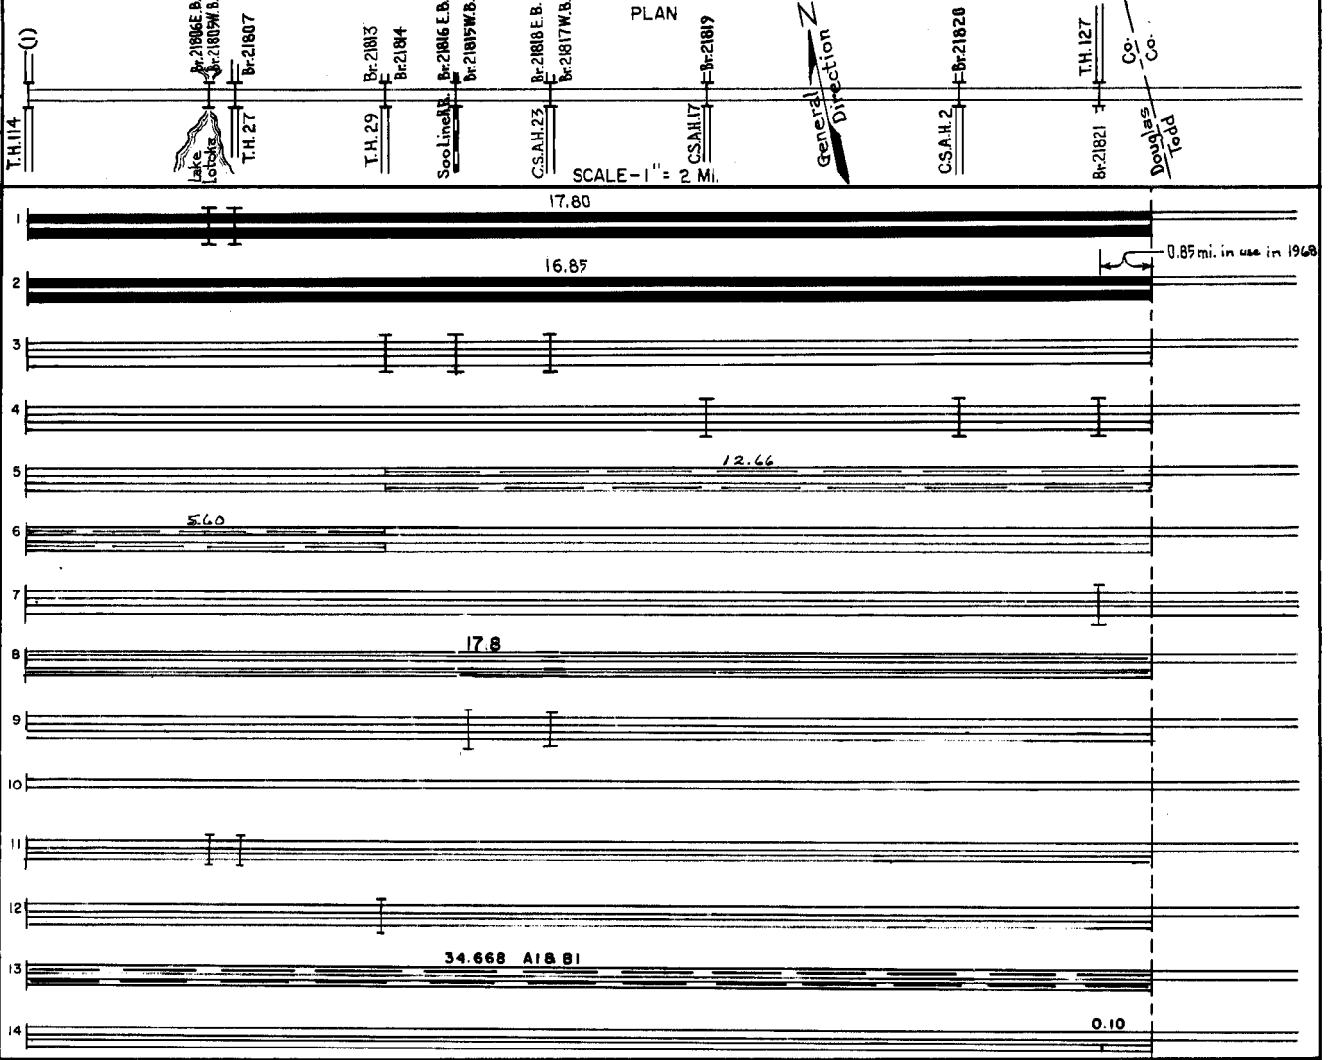

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1967		16.95	16.88	0.07	0.00	0.00	16.88	0.07	0.00	0.00

REMARKS: Layout is to scale as of 1967.
(1) See sheet A1 for bridges at T.H. 114.

