


PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2180B
Interstate TRUNK HIGHWAY 94
COUNTY Douglas
DISTRICT 4B

LIMITS: Jct. T.H. 114 - E. Co. Line

YEAR BUILT	PROJECT NO	DESCRIPTION	WIDTH	THICKNESS	REMARKS
C	2180-0709&10	Grading			Divided Highway
1967	2180-21807&106	Br's 21805 & 21806	38' & 38'		Both 125' B.S.-O.H.
	2180-21807	Br. 21807			275' B.S.-U.P.
C	2180-27&28	Sub-base & Base P.C. Concrete	2 @ 24"	9"	
C	2180-21813&14	Br's 21813 & 21814			Both 235' B.S.-U.P.
1967	2180-21815&16	Br's 21815 & 21816	38' & 38'		Both 140' B.S.-O.H.
	2180-21817&18	Br's 21817 & 21818	38' & 38'		Both 111' B.S.-O.H.
C	2180-21819	Br. 21819			212' B.S.-U.P.
1967	2180-21820	Br. 21820			212' B.S.-U.P.
	2180-21821	Br. 21821			285' B.S.-U.P.
M	2180-SF	JOINT SEAL			13800 TONS H SPEC #135- 48 PAISLS #157-87; #136- 135; #155-11
1976					
M	2180-SF	JOINT SEAL			
1977					
M	2180-21821	Br. No. 21821	35.75'		Bridge Repair
1980					
C	2180-62	Gene. Pavt. Repair			
1981					
C	2180-21815	Br. Deck Repair & Overlay			
1981		Br. 21815, 21816			
		21817, 21818			
C	2180-21805	Br. Deck Overlay			Br's 21805, 21806 21807, 21810
1982					
C	2180-21813	Br. Deck Overlay	30'	2"	Br's 21813, 21814
1983		Br. Deck Widening	38'-5"	2"	Br. 21814
M	2180-60	Safety Improvement & Traffic Barrier			130.8 Mi. For 1402-11, 1480-86, 2180-60, 2680-28 5680-91, 6480-21
1984	SF	Bit. Shoulder	9'	1-1/2"	Sp. 2341 22 Tons E.B. under T.H. 127

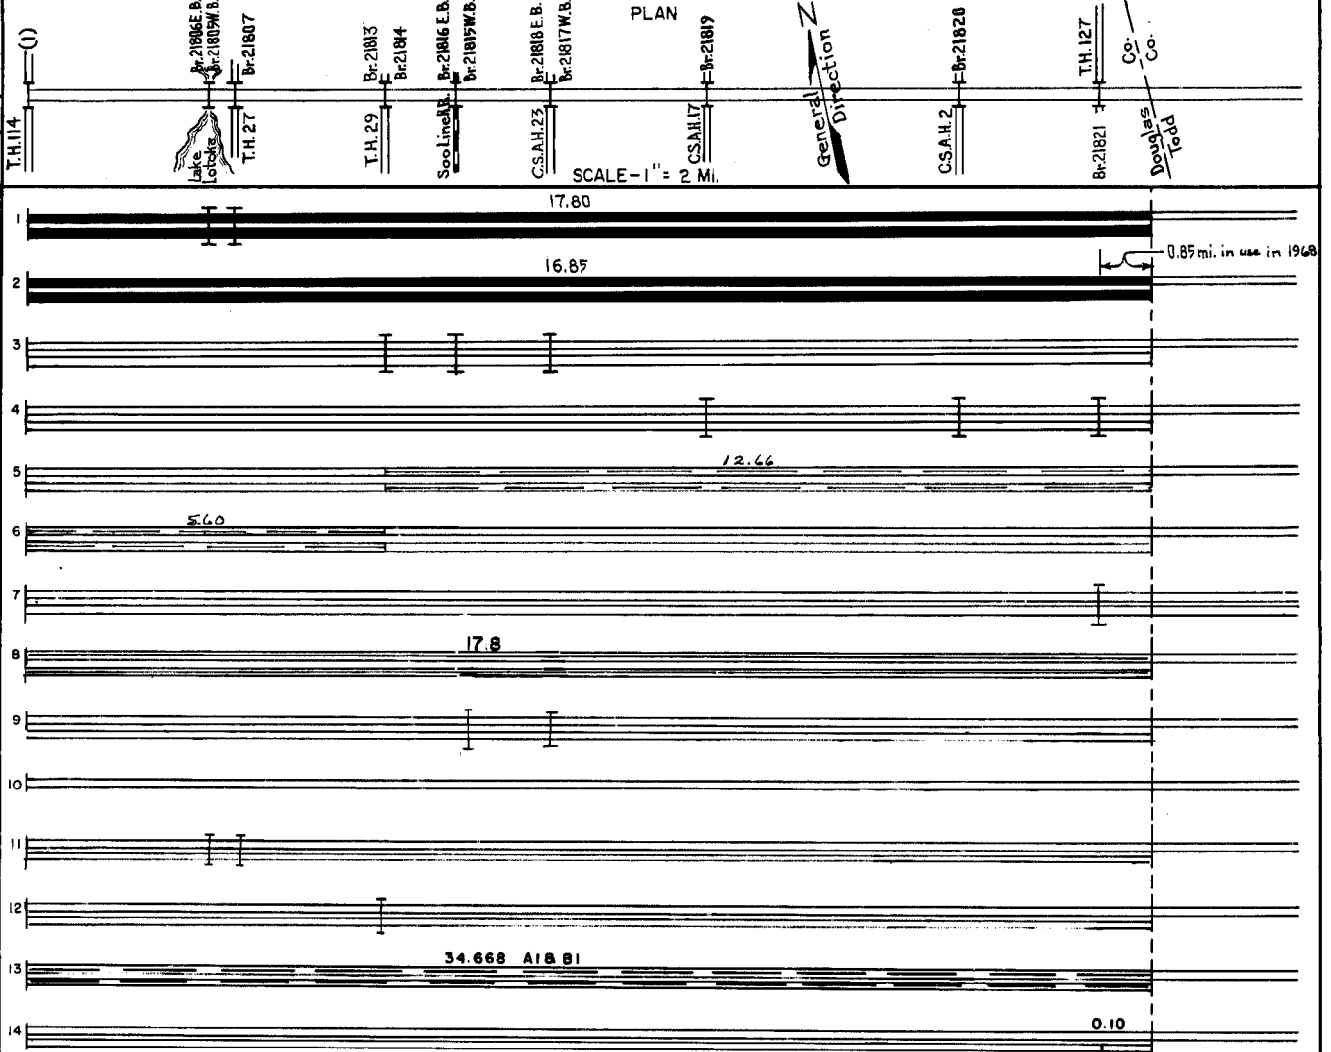

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1967		16.95	16.88	0.07	0.00	0.00	16.88	0.07	0.00	0.00

REMARKS: Layout is to scale as of 1967.
(1) See sheet A1 for bridges at T.H. 114.

