


PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2614
TRUNK HIGHWAY 7B
COUNTY Grant
DISTRICT 4B4

LIMITS Jct. T.H. 94 - Jct. CSAH 82
Ref. Pt. 000+00.000 - 004+00.572



| YEAR BUILT | PROJECT NO. | DESCRIPTION | | | | REMARKS |
|------------|-------------|---------------------------------------|-----------|-----------|---------------------------------------|---------|
| | | TYPE | WIDTH | THICKNESS | | |
| | | Mixed Bit. | 24' | | No Record of Const. | |
| | | | | | Added in 1965 | |
| C | | Sub-base, Base & Plant Mix Bit. Surf. | 24-42' | | | |
| 1959 | 26-610-01 | Bit. Seal Coat (4.18 mi.) | | | Added in 1965 | |
| 1962 | 26-610-05 | Grading, Sub-base | | | 9" Sand-gr. Sub-base | |
| C | | Gravel & Bit. Base | 5' & 1/2" | | | |
| 1965 | 2680-03 | Plant Mix Bit. | 24' | 2" | | |
| 2680-14 | | Grading | | | | |
| C | | Gravel Base | 43' | 6" | | |
| 1968 | 2614-05 | Pl. Mix. Bit. Surf. | 24' | 2" | Bit. Mat'l 367 Ton | |
| C | | Pl. Mix. Bit. Overlay | | | Added in 1968 | |
| 1965 | 2680-14 | Lighting Systems | | | In Ashby at Jct. C.S.A.H. 10 & 82 | |
| C | | Bit. Surfacing | 24' | 3" | Project Begin 0.0475 of S. Ramps 1-94 | |
| 1981 | 2614 SF | Aggregate Shldr. | 8' | Var. | | |
| S | | Bit. Overlay | 24' | 2" | Spec. 2360 | |
| 2004 | 2614-06 | Bit. Seal Coat | | | | |
| 2011 | 8824-98 | | | | | |

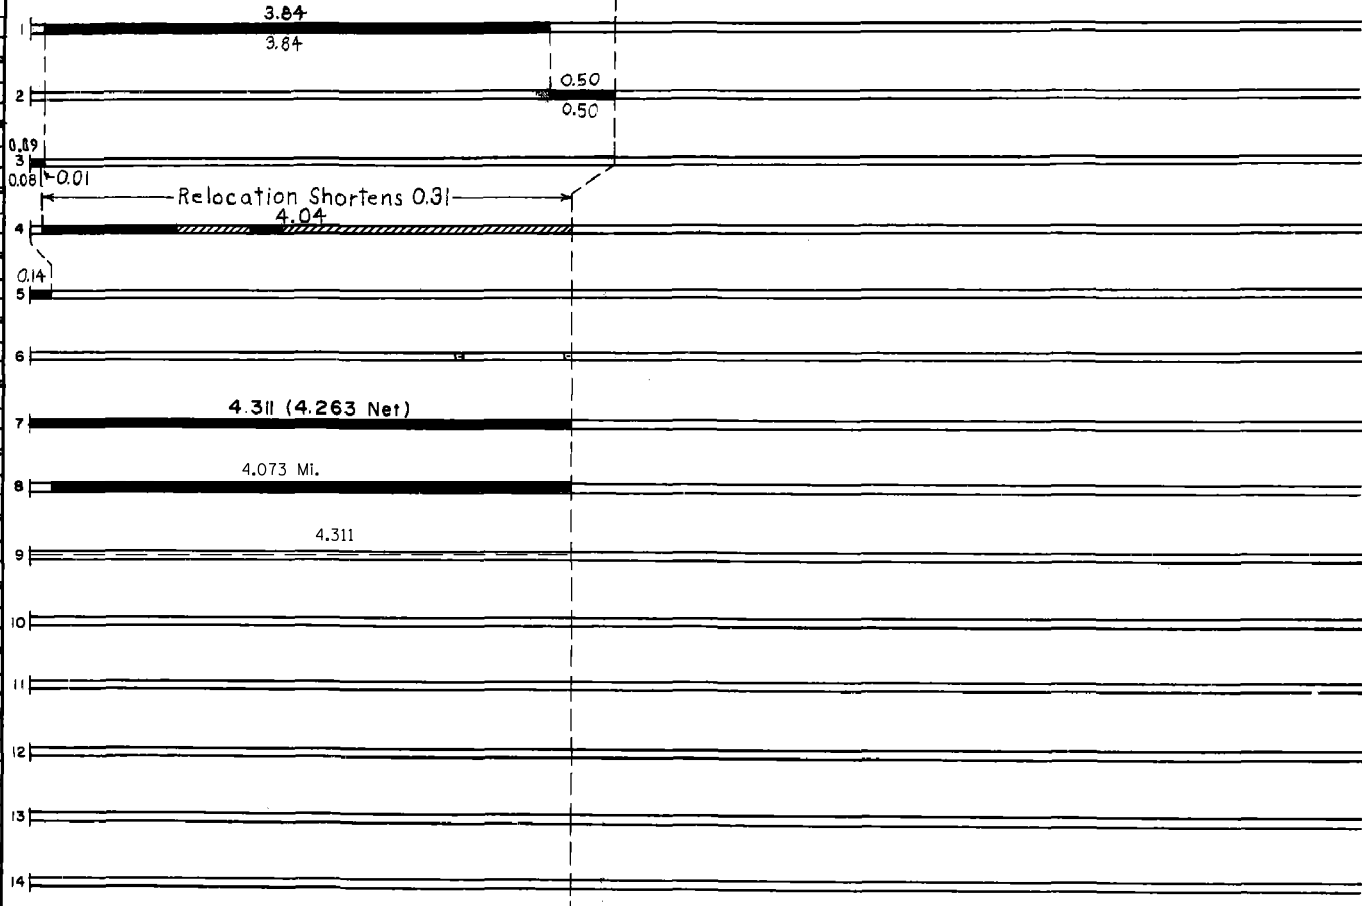

| YEARS | | TOTAL MILES | UNINCORPORATED | | INCORPORATED | | RURAL | | URBAN | |
|-------|----|-------------|----------------|---------|--------------|---------|-----------|---------|-----------|---------|
| FROM | TO | | RDWY. MI. | BR. MI. | RDWY. MI. | BR. MI. | RDWY. MI. | BR. MI. | RDWY. MI. | BR. MI. |
| 1965 | | 4.43 | 3.93 | 0.00 | 0.50 | 0.00 | 4.43 | 0.00 | 0.00 | 0.00 |
| | | | | | | | | | | |
| | | | | | | | | | | |

REMARKS: Layout is to scale as of 1965
