


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2727  
TRUNK HIGHWAY 65  
COUNTY Hennepin  
DISTRICT 5A

LIMITS: S. End of Bridge (Minn. River) - S. Corp. Limits of Minneapolis



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Br. 3184	23'		
					No Record of Constr. 791' D.T. & C.D.G.
1920	65-50-5	Asphaltic Conc. Concrete Base	20'	2" 6"	
1921		Br. 2791	23'		120' C.D.G.
1921		Grading	30'		Co. Job 39
1922	65-50-3	Asphaltic Conc. Concrete Base	18'	2" 6"	
1923	65-50-22	Guard Rail Curb & Gutter			
1927	65-52-21	Br. 4560	40'		84' C.D.G. - O.H.
M	1942 A.F.E. 29	Spot Patch pavt. with plant Mix. Bit.			Maint. Dept.
M	1943 A.F.E. 17	Bit. Resurface	18'		RT 6,8334 Gal./Mi. Grav. 534 CY/Mi. Maint. Dept.
M	1943 A.F.E. 33	Grav. Shoulders			402 C.Y./Mi. Maint. Dept.
C	1947 A.F.E. 19	Bit. Resurfacing Mixed Bit.	18'20" edged	1/8"	RT 6 Mo. 39464 Gal. Agg. 2488 C.Y.
M	1948 A.F.E. 18	Grav. Shoulders (Spots)			3' Rt & Lt. 756 C.Y.
M	1948 A.F.E. 4	Fog Seal			RSC-1 10327 Gal. Agg. 204 C.Y.
C	1949 2727-11 A.F.E. 25	Traffic Signals Bit. Surf. Shoulders	16'		3' Rt & Lt.

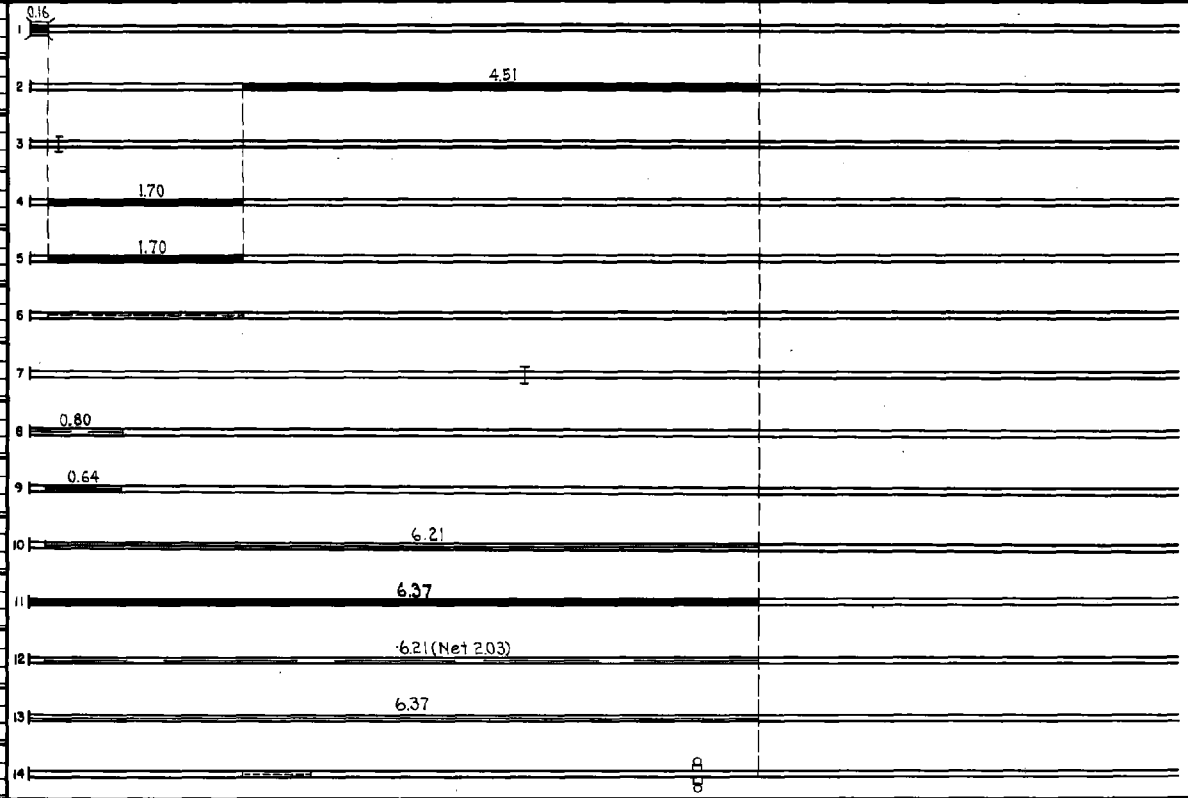

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1926	6.37	4.14	0.18	2.05	0.00	4.14	0.18	2.05	0.00
1927	1952	6.37	4.12	0.20	2.05	0.00	4.12	0.20	2.05	0.00
1953	1959	6.37	0.00	0.00	6.17	0.20	0.00	0.00	6.17	0.20
1960		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1921

