


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 340
TRUNK HIGHWAY 55
COUNTY Kandiyohi
DISTRICT 3B

LIMITS: N. Co. Line - E. Co. Line.



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Gravel	22'	1"	No Record of Constr. Added in 1934.
1936	55-142-24-1A	Grading Br. 5546	32'	27"	150 B.S.
1937	55-142-24-1A	Slab. Gravel	32'	2-4"	80% Grav. & 20% Binder Soil.
1938	3410-01	Mixed Bit.	24'	1 3/4"	
M 1940	A.F.E. 9	Bit Seal Coat			Rd. Tar 3889 Gal./Mi. Grav. 132 CY./Mi. Maint. Dept.
M 1944	3410-05	Gravel Lifts	34'		
M 1945	A.F.E. 4 A.F.E. 16	Spot Treat. Bit. Surf. Repair			RT-6, 983 Gal./Mi. Grav. 8 C.Y./Mi. Maint. Div.
M 1946	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		RT-4, 650 Gal. Agg. 39 C.Y.
C 1947	A.F.E. 17	Bit. Resurfacing Mixed Bit	26'	1"	MC-3, 51959 Gal. Agg. 4207 Tons
M 1949	A.F.E. 5	Bit. Seal Coat	26'		RC-3, 11873 Gal. Agg. 465 C.Y.
M 1955	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC-3, 2929 Gal. Agg. 252 Tons
M 1957	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC-3, 3686 Gal. Agg. 319 Tons
M 1958	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SC-4, 2912 Gal. Agg. 252 Tons
C 1960	3410-08	Grading Gravel Base Road Mix Bit	42' 26'	6-9" 1 1/2"	10,662 Gal. Bit. Mat'l.

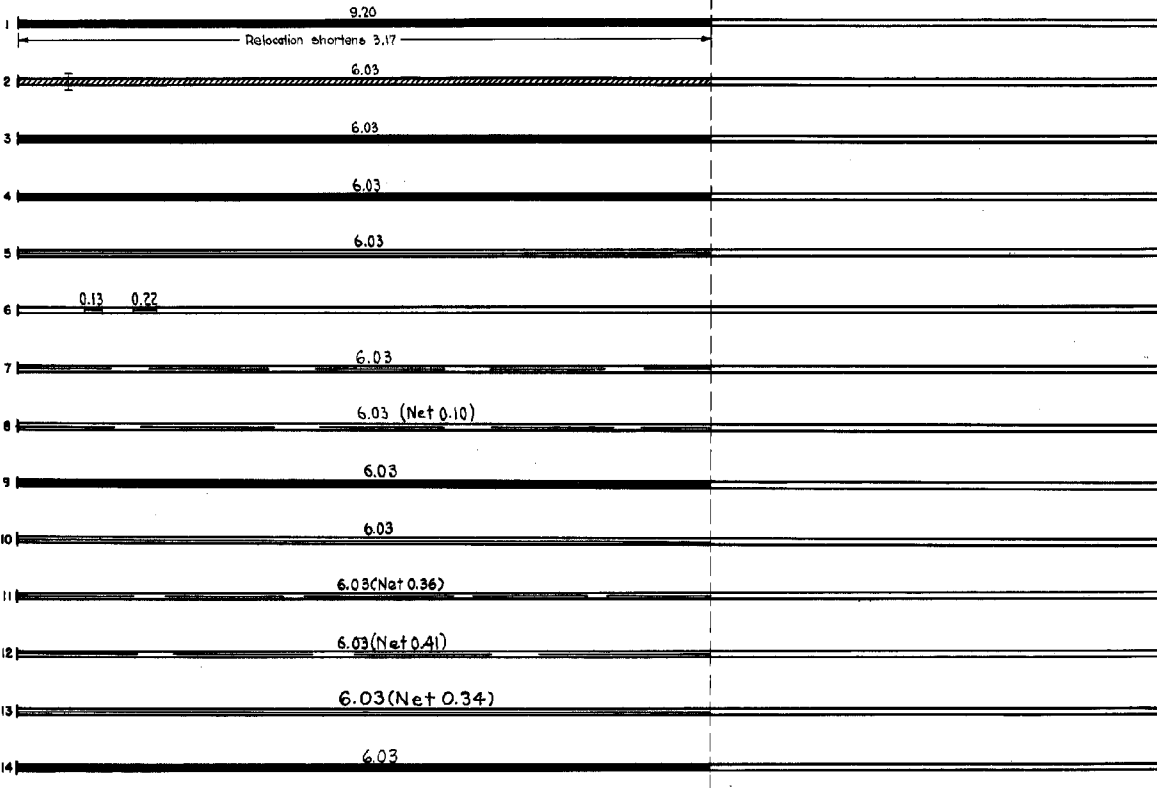

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1935	9.20	9.20	0.00	0.00	0.00	0.00	9.20	0.00	0.00
1936		6.03	4.98	0.03	1.02	0.00	0.00	6.00	0.03	0.00

REMARKS: Layout is to scale as of 1936.

