


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3414
TRUNK HIGHWAY 71
COUNTY Kandiyohi
DISTRICT 8A

LIMITS: Jct. T.H. 17 - N. Co. Line
Ref. Pt. 138+00.512 - 144+00.273



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel	22'	2"	No Record of Constr. Added in 1934.	
1935	71-141-21-1	Grading Gravel	32' 24'	2"		
1936	71-141-21-1	Slab. Gravel	32'	4"	With Clay. Method No. 1. Maint. Dept.	
C	3414-01	Stab. Gray Base Bit. Surf. Treat.	32' 26'	8" 3/4"	Accumulated thick.	
M	1941 A.F.E. 63	Bit. Seal Coat			SC-4, 1003 Gal./Mi. Maint. Dept.	
M	1943 A.F.E. 4	Bit. Surf. Repair			Oil, 2312 Gal./Mi. Maint. Dept.	
M	1947 A.F.E. 5	Bit. Seal Coat	26'		RC-3, 17152 Gal. Agg. 536 C.Y.	
C	1950 3414-03	Spot Base Repair Plant Mix Bit.	24'	1 1/2" added		
M	1954 A.F.E. 605	Light Bit. Seal	24'		RC-2, 8937 Gal. Agg. 383 C.Y.	
C	1962 3414-04	Grading Gravel Base Road Mix Bit. Base	47' 43' 26'	4" 4" 1 1/2"		
M	1962	Light Bit. Seal	25'		RS-2, 10,353 Gal. Agg. 320 C.Y.	
C	1963 3414-06	Plant mix Bit. Bit. Shoulders	24'	3 1/2"		
C	1970 3414-09	Grade Base. Pl. Mix Bit. Surf. Gravel Shldrs	24'	3'		
C	1988 3414-11	Bit. Overlay	24'	1 1/2"	Spec. 2341	

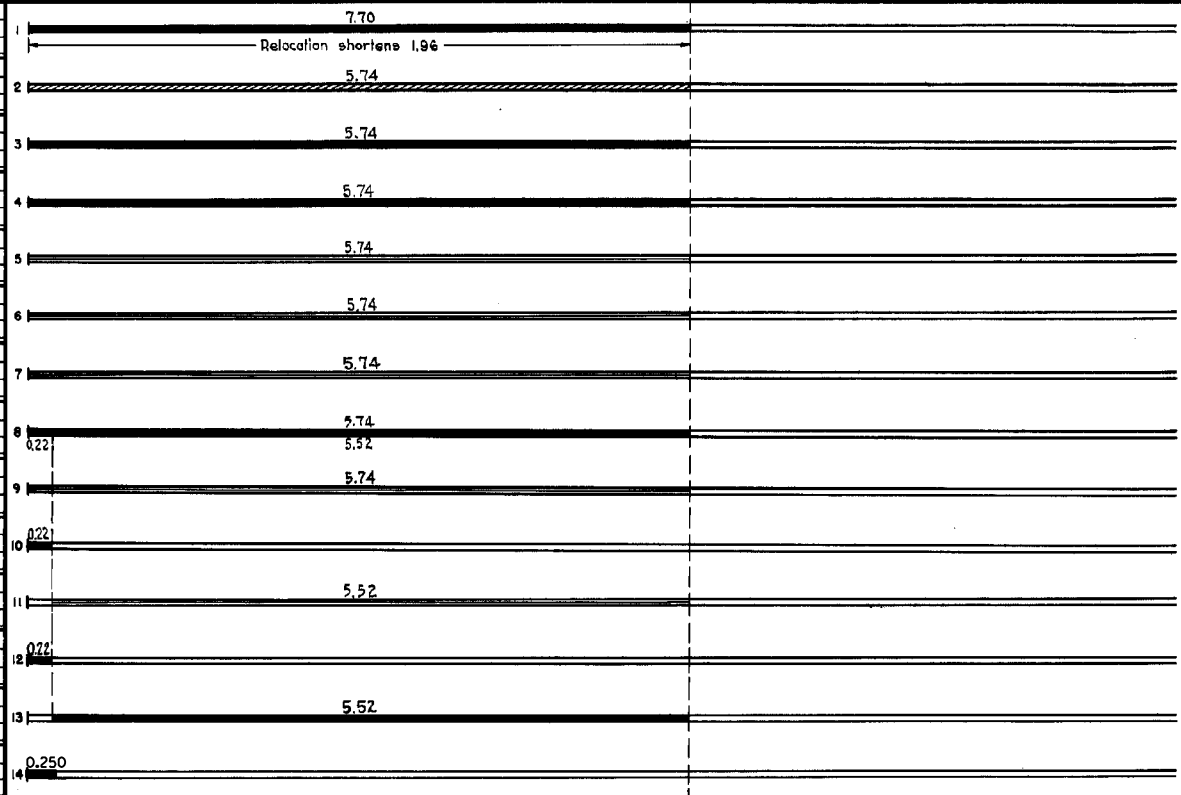

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1934	7.70	6.87	0.00	0.83	0.00	7.70	0.00	0.00	0.00
1935		5.74	5.74	0.00	0.00	0.00	5.74	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1935.
(1) This work not done under this project number but lies within the limits of this project.

