

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3416
TRUNK HIGHWAY 104
COUNTY Kandiyohi
DISTRICT 4B

LIMITS: W. Jct. I.R. 9 - N. Co. Line.

Ref. Pt. 014+00.446 - 018+00.435

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
					No Record of Constr. Added in 1934. 12' Conc. Arch.
1935	104-143-21	Gravel	22'	1 1/2"	500 C.Y. / Mile. Relief Labor.
M	1940	A.F.E. 12			329 C.Y. / Mile. Maint. Dept.
M	1943	A.F.E. 6			313 C.Y. / Mi. Maint. Dept.
M	1945	A.F.E. 6			1612 C.Y.
M	1951	A.F.E. 6			1449 C.Y.
M	1952	A.F.E. 6			573 C.Y.
C	1954	3416-02			Grading Gravel Const. C108 Culv.
C	1955	3416-03			Stab. Sand-Gr. Subbase Stab. Gravel Base Plant Mix Bit.
M	1956	A.F.E. 605			Bit Seal Coat RC-5, 12977 Gal. Agg. 438 C.Y.
C	1959	3416-04			Grading Gravel Mix Bit. (Base)
C&M	1963	7606-16			Light Bit. Seal Plant Mix Bit Gravel Shoulders
M	1985	SF			Spot Overlay
M	1990	M4381			Bit. Overlay Spec. 2341

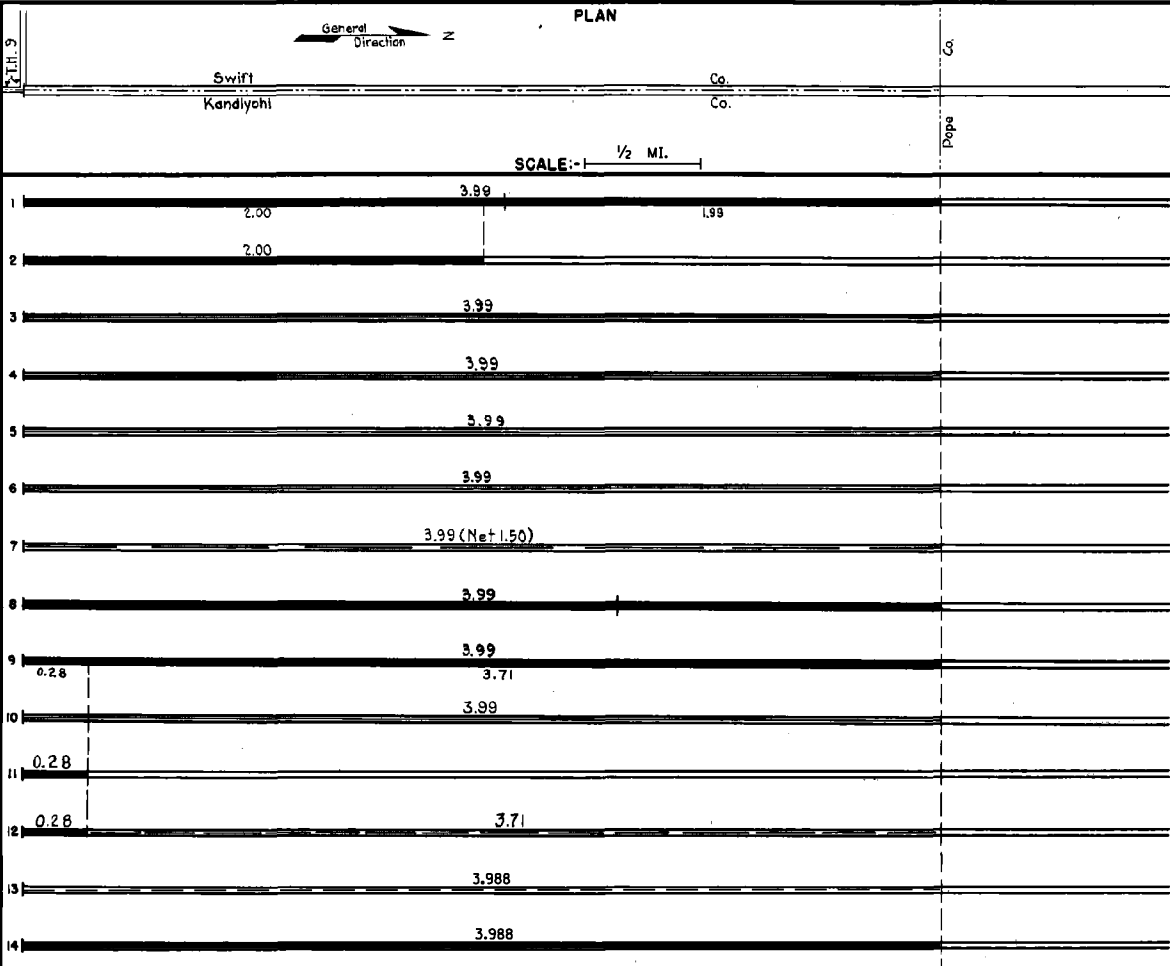

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1934		3.99	3.99	0.00	0.00	0.00	0.00	3.99	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934.

