

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3503
TRUNK HIGHWAY 11
COUNTY Kittson
DISTRICT 25

LIMITS: Jct. T.H. 59 in Karlstad - E. Co Line

Karlstad
1.12 Mi.

PLAN

C.S.A.H. 7

Co. Co


T.H. 59
See Line R.R.

General Direction

Kittson
Roseau

SCALE: - 1" = 1 MI.

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o Dist.
		TYPE	WIDTH	THICKNESS	
		Gravel	24'	1/2"	No Record of Constr.
1936	11-11-46-2A	Grading	32'		1635
1936	11-11-46-2A	Oil Tr. Gravel	26'	1"	Maint. Dept.
1941	A.F.E. 7	Regrade & Reshape Natural Gravel	32'		Maint. Dept.
1946	A.F.E. 17	Bit Surface (831 Mi) Mixed Bit.	24'	1"	RT-6, 181720 Gal. Agg. 4306 C.Y.
1947	A.F.E. 4	Bit. Fog Seal	24'		RT-6, 7927 Gal.
1950	A.F.E. 4	Bit. Fog Seal	24'		RCS-1, 11486 Gal. Agg. 290 C.Y.
1953	A.F.E. 605	Light Bit. Seal	24'		RG2, 10453 Gal. Agg. 603 Tons
1954	A.F.E. 605	Light Bit. Seal	24'		RT-6, 9882 Gal. Agg. 332 C.Y.
1955	3503-02	Grade X-ing Signals			
1956	A.F.E. 604	Bit. Surf. Repair	24'		SC-3, 66112 Gal. Agg. 4850 Tons
1971	3503-05	Grading & Base Plant Mix Bit.	52'	16" curb to curb	969
1974	SF	BIT SURFACING	24'		2174

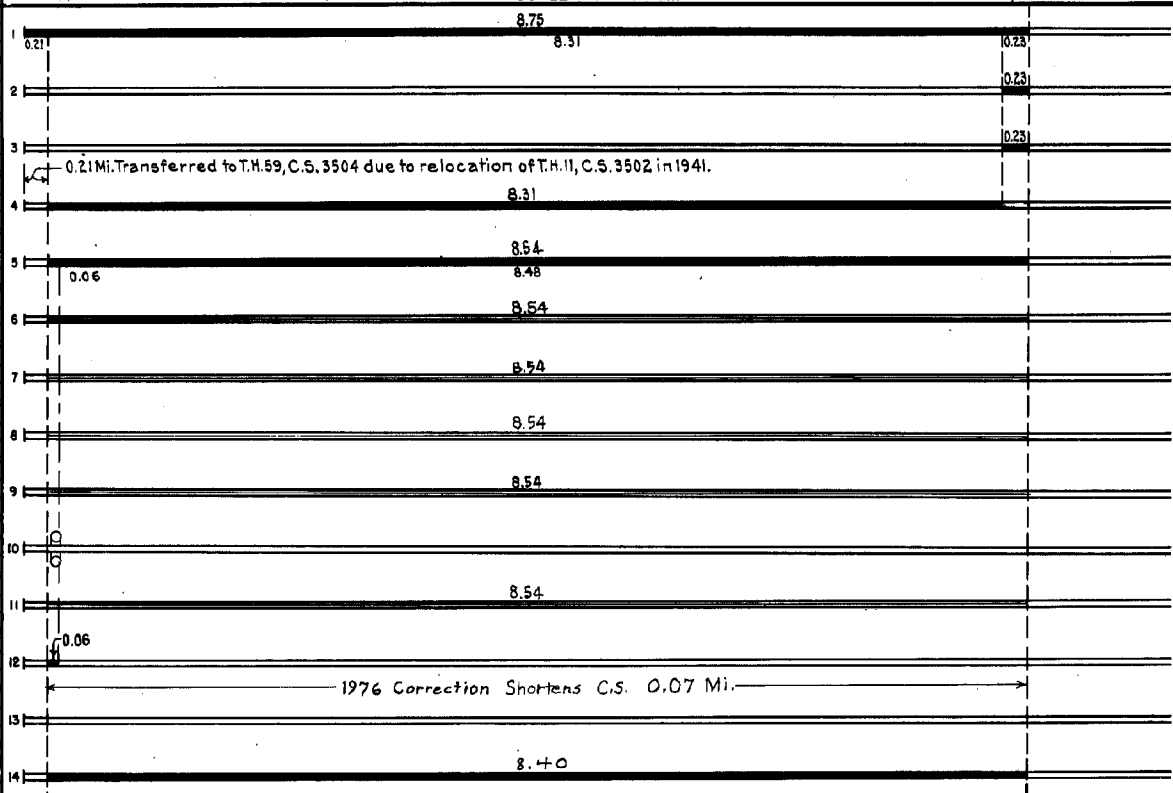

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1940	8.75	7.93	0.00	0.82	0.00	8.75	0.00	0.00	0.00
1941	1961	8.54	7.93	0.00	0.61	0.00	8.54	0.00	0.00	0.00
1962	1966	8.54	7.66	0.00	0.88	0.00	8.54	0.00	0.00	0.00
1967	1975	8.54	7.42	0.00	1.12	0.00	8.54	0.00	0.00	0.00
1976		8.47	7.35		1.12		8.47			

REMARKS: Layout is to scale as of 1921. Plan revised for 1941 relocation of T.H. 11 in Karlstad.
(1) This work not done under this project number but lies within the limits of this project
FOR OTHER PROJECTS SEE DIST. NO. 1675

