

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4403
TRUNK HIGHWAY 59
COUNTY Mahanomet
DISTRICT 4A

LIMITS: S.Co.Line - Jct.T.H.200

Ref.Pt. 287+00.590 - 300+00.197

YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o
		TYPE	WIDTH	THICK-NESS	REMARKS	
1921	59-30-7	Grading Br.3357	24'	20"	75' Truss	
1923	59-30-22	Gravel	20'	3"	1200 C.Y./Mile	
1931	59-30-22B	Grading	40'			
1932	59-30-22A	Grading Gravel Br.5183	40' 24'	1 1/2" 2 1/2"	800-1000 C.Y./Mile 75' Lt.	
1932	59-30-22B	Concrete	20'	9-7-9		
1933	59-30-22C	Concrete	20'	9-7-9		
C	1966	Maint. Proj. Plant Mix Bit. Gravel Shoulders	20'	3"	Over P.C. Conc. inp.	
M	1967	C		21'	CRS-1 Bit, 3233 Gal. FA-1 Agg. 113 C.Y.	
C	1969	4403-02	Pl. Mix. Bit. Surf. Gravel Shldrs.	20'	Over P.C. Conc. inp. 10' Rt. & Lt.	
C	1979	4403-06	PAVEMENT WIDENING Pl. Mix Bit. SURF. FOSS-4 (24)	5' 24' 10'	10 1/2" 1 1/2" 1 1/2"	
C	1979	4403-10	PAVEMENT WIDENING Pl. Mix Bit. SURFACE FOSS-4 (24)	5' 24' 10'	10 1/2" 1 1/2" 1 1/2"	BR.44002 REPL BR. 5183
C	1980	4403-07	Bit. Surface & Striping	4'	2 1/2" 1' Leading Down 10' Lt.	
M	1986	SF	Bit. Shouldering	2'	2 1/2"	
C	1994	4403-14	Turn Lanes			

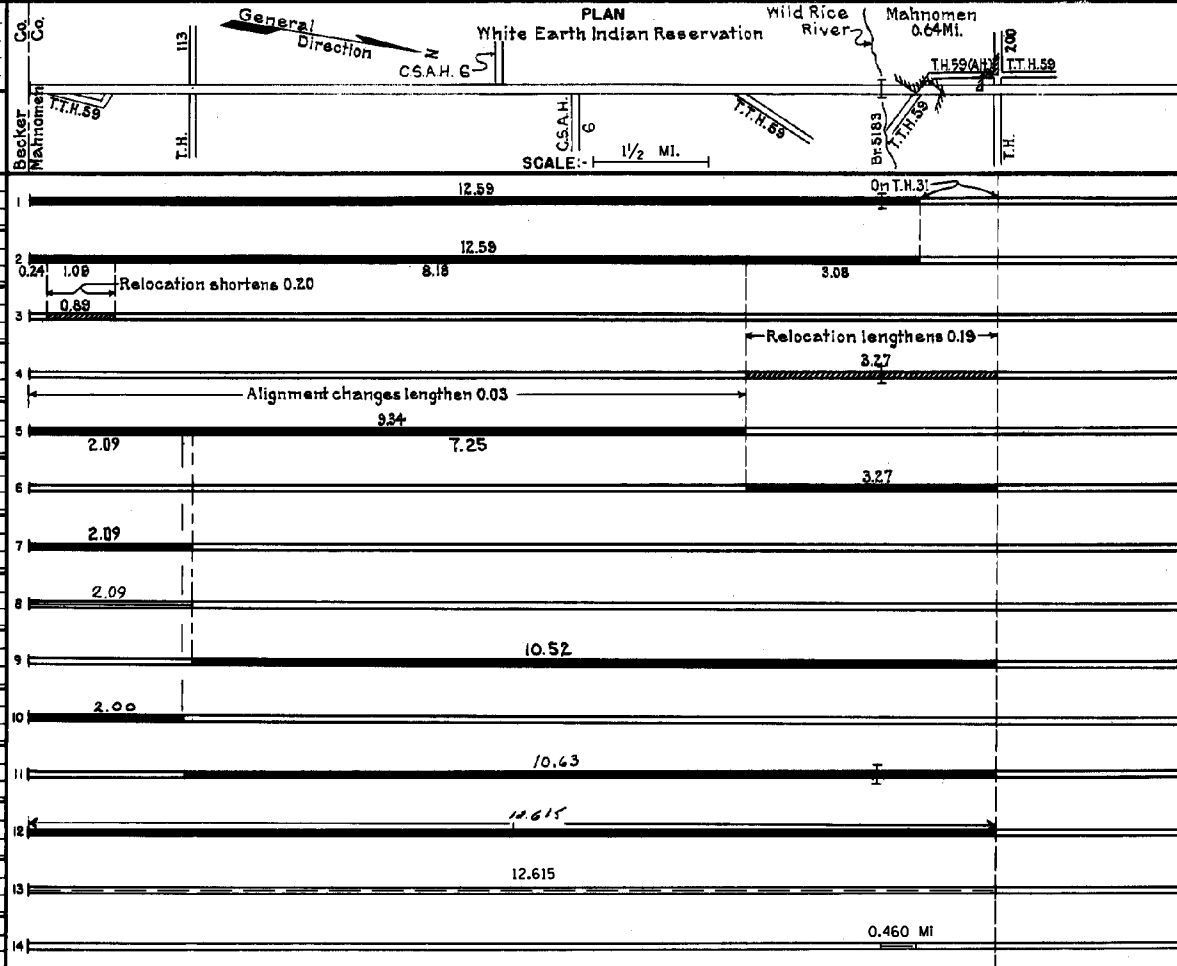

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			ROWY. MI.	BR. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	
1921	1930	2.59	2.51	0.01	0.07	0.00	12.51	0.01	0.07	0.00		
1931	1931	2.35	2.31	0.01	0.07	0.00	12.31	0.01	0.07	0.00		
1932	1951	2.6	2.09	0.01	0.51	0.00	12.09	0.01	0.51	0.00		
1952		2.61	11.96	0.01	0.64	0.00	11.96	0.01	0.64	0.00		

REMARKS: Layout is to scale as of 1932

