

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 5402
TRUNK HIGHWAY 200
COUNTY Norman
DISTRICT 2B

LIMITS: S. Jct. T.H. 32 - N. Jct. T.H. 32

Ref. Pt. 29+00.858 - 31+00.885



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o Dist.
		TYPE	WIDTH	THICKNESS	
		Earth	26'		No Record of Const.
1927		Gravel	24'	2"	1000 C.Y./Mile. Maint. Dept.
1937	A.F.E. 13	Mixed Bit.	24'	1"	Maint. Dept.
M	1941 A.F.E. 12	Bit Seal Coat (High Type)	24'		RC-3, 4083 Gal./Mi. Agg. 129 C.Y./Mi. Maint. Dept.
C	1947 A.F.E. 20	Bit Resurfacing Mixed Bit.	24'	1" Added	SC-3, 15586 Gal. Agg. 1356 Tons
M	1950 A.F.E. 4	Bit Fog Seal	24'		RC-1, 2810 Gal. Agg. 58 C.Y.
M	1954 A.F.E. 605	Light Bit Seal	24'		RS-2 & RG-2, 3027 Gal. Agg. 115 C.Y.
C	1947 A.F.E. 21	Mixed Bit	22'	1" added	See C.S. 5405 for Previous data
C	1956 5402-02	Grading Gravel Base Mixed Bit (Base)	34' 34' 26'	4" 4" 1 1/2"	On 9" min. Select Granular Matl. 1355
M	1957 A.F.E. 605	Light Bit Seal	27'		RC-2 & 3, 4469 Gal. Agg. 180 C.Y.
C	1958 5402-03	Plant Mix Bit.	24'	2"	458
M	1963 c	Light Bit Seal	25'		RS-2K, 3402 Gal. Agg. 127 C.Y. 1363
C	1962 5402-05	Bit Surfacing Bit. Shoulders	24' 4'	2" 2"	4' L & R

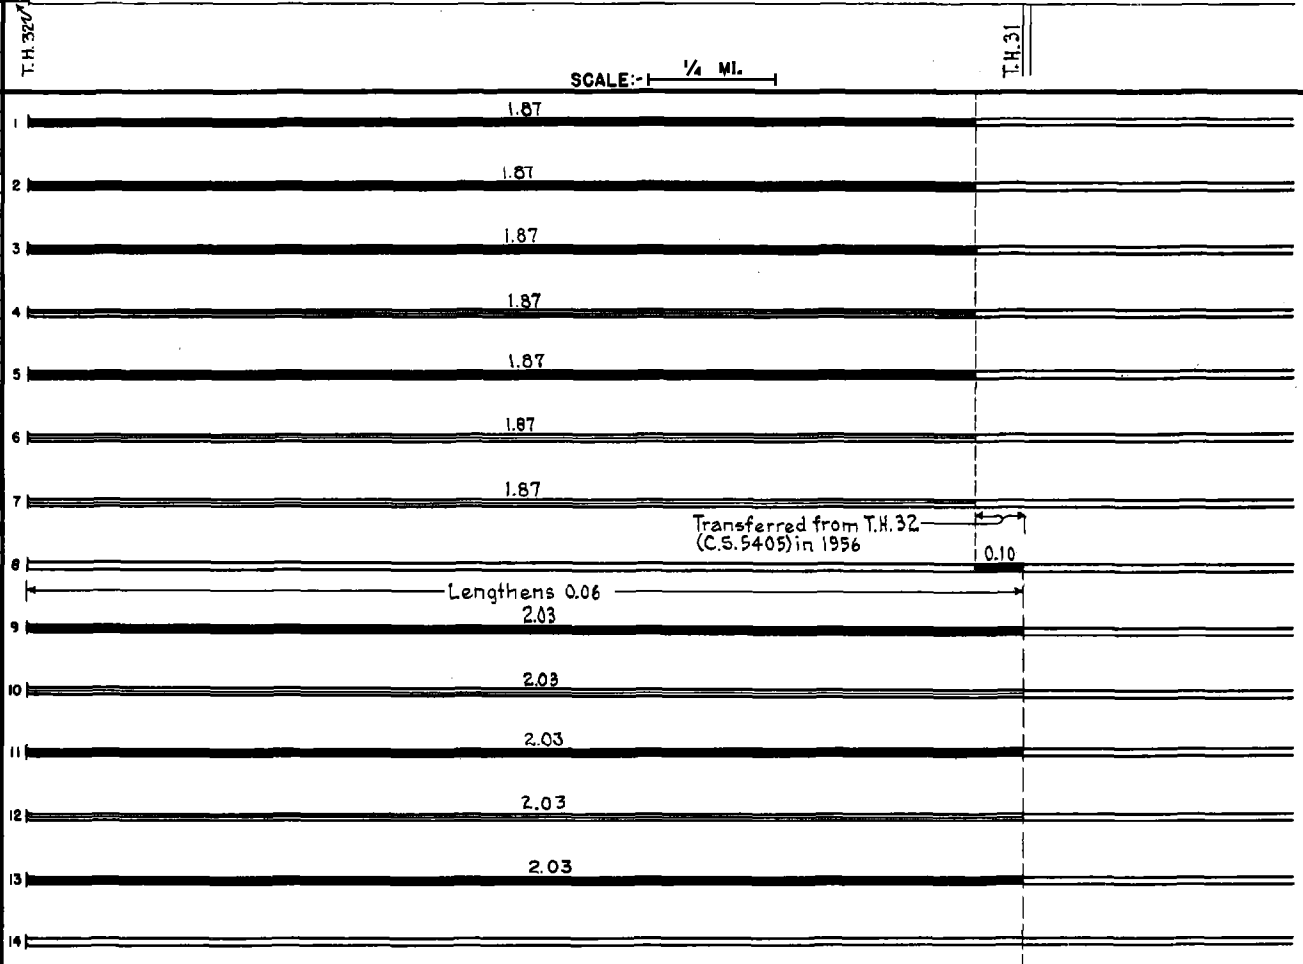

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.		
1927	1955	1.87	1.87	0.00	0.00	0.00	1.87	0.00	0.00	0.00		
1956		2.03	2.03	0.00	0.00	0.00	2.03	0.00	0.00	0.00		

REMARKS: Layout is to scale as of 1934
FOR OTHER PROJECTS SEE DIST. No. 334

