


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5906  
TRUNK HIGHWAY 75  
COUNTY Pine Stone  
DISTRICT 8B

LIMITS: W. Jct. T.H. 30 to Pipestone - N. Co. Line



YEARS BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1920	75-6-20B	Grading Gravel Br. 4718	30' 24' 27'	3 1/2"	Co. Job 2006. 1600 C.Y./Mile. 30' B.S.
1921	75-6-20A	Grading Gravel	24'	3 1/2"	1600 C.Y./Mile.
1922	75-6-02A	Concrete Br. 2858	V.V. 19'	7 1/2"	40' C.D.G.
1922	75-6-01	Grading Gravel	30' 24'	3 1/2"	1600 C.Y./Mile.
1923	75-6-08	Grading Gravel	30' 24'	3 1/2"	1600 C.Y./Mile.
1924		Grading Gravel	24'	3 1/2"	Maint. Dept.
1925	75-6-08	Guard Rail			
1926		Oil Tr. Gravel	24'	1 1/2"	10000 Gal./Mile. Maint. Dept.
	(1)				
1926	75-6-20A	Oil Tr. Gravel	24'	1 1/2"	10000 Gal./Mile. Maint. Dept.
	(1)				
1931	75-6-20A & B 75-6-01 & 08	Oil Tr. Gravel	24'	1 1/2"	10000 Gal./Mile. Maint. Dept.
1936	75-6-24	Br. 5297			WY1010T.
	5906-01	Crossing Signal			G.N. Ry.
1939	5906-02	Crossing Signal			C.S.P.M. & C.R.I. & P.
	5906-03	Crossing Signal			C.M.S.P. & P.R.
1939	A.F.E. 78	Shoulder Gravel			
M		Spot Treat			MCS-1416 Gal./Mi.
1942	A.F.E. 4	Bit Surf. Repair	24'		Grav. 88 C.Y./Mi. Maint. Dept.

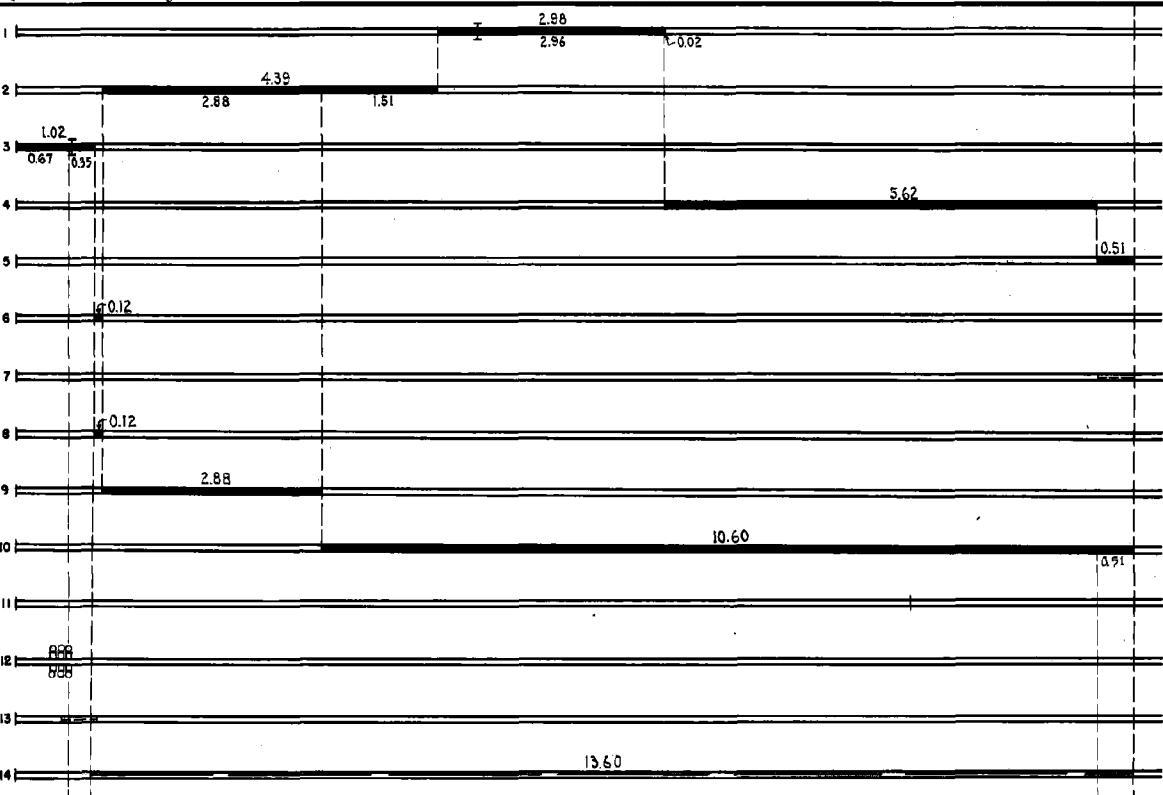

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1924	1949	4.62	13.59	0.01	1.01	0.01	13.59	0.01	1.01	0.01
1930	1954	4.07	13.04	0.01	1.01	0.01	13.04	0.01	1.01	0.01
1955	1960	4.05	13.04	0.01	0.99	0.01	13.04	0.01	0.99	0.01
1961	1961	4.05	12.98	0.01	1.05	0.01	12.98	0.01	1.05	0.01
1962	1962	4.05	12.97	0.02	1.05	0.01	12.97	0.02	1.05	0.01

REMARKS: Layout is to scale as of 1924.


(1) This work not done under these project numbers but lies within the limits of these projects.

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5906  
TRUNK HIGHWAY Pipestone  
COUNTY Pipestone  
DISTRICT 88

LIMITS: W. Jct. T.H. 30 in Pipestone - N. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION		REMARKS	CODE N°	PLAN
		TYPE	WIDTH			
M 1944	A.F.E. 4	Spot Treat. Bit. Surf. Repair		MC-3, 1039 Gal./Mi. Grav. 36 C.Y./Mi. Maint. Div.		1 13.60
M 1945	A.F.E. 4	Spot Treat. Bit. Surf. Repair		Bit. 2524 Gal./Mi. Grav. 110 C.Y./Mi. Maint. Div.		2 13.60
M 1946	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'	SC-3, 11771 Gal. Agg. 558 C.Y.		3 10.60 (Net 1.90)
M 1947	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'	SC-3, 18835 Gal. Agg. 1358 Tons		4 13.60 (Net 3.30)
M 1948	A.F.E. 4	Spot Treat. Bit. Surf. Repair	22'	SC-3, 38300 Gal. Agg. 2785 Tons		5 13.60 (Net 6.85)
M 1949	A.F.E. 4	Spot Treat. Bit. Surf. Repair	22'	MC-2 & SC-3, 21427 Gal. Agg. 1673 Tons		6 9.48 (Net 4.15)
C 1950	5906-13	Grade Widening	46'			7 0.91 m. transferred off of T.H. System due to relocation of C.S. 4107 (T.H. 75) in 1950
C 1950	5906-10	Grading	42'	Removed Br. 8384 & Culverts (2)		8 Shortens 0.04 due to former error
C 1951	5906-14	Gravel Base Plant Mix Bit.	36' 8'-10" 24' 1 1/2"			9 13.40
C 1955	5906-16	Grav. Sub-base Bit. Stab. Base Plant Mix Bit.	20' 12" 20' 8" 50' 3"	Old 30' conc. from Mi. Pt. 0.00-0.52 left in p. & used as part of base		10 13.06 Shortens 0.02
M 1956	A.F.E. 605	Light Bit. Seal	24'	RS-2, 23323 Gal. Agg. 800 C.Y.		11 13.39
M 1958	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'	SC-3 & MC-2, 10858 Gal. Agg. 773 Tons		12 11.05 (Net 1.55)
M 1959	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'	SC-3, 9864 Gal. Agg. 694 Tons		13 11.45 (Net 1.25)
M 1960		Spot Treat. Bit. Surf. Repair	24'	SC-3 & MC-2, 7969 Gal. Agg. 503 Tons		14 10.20 (Net 1.15)

YEARS FROM TO		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet N° 1  
(2) 2-C84; 2-C86; ext. W64; C77; C86; C108-82 (Br. 8970); 4-C75.

