


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4407  
TRUNK HIGHWAY 113  
COUNTY Mahanomen  
DISTRICT 4A

LIMITS: M. Co. Line - Jct. T.H. 59  
Ref. Pt. 009+00.040 - 015+00.327



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	28'3"		No Record of Const. Added in 1949
		Bridge # 6966	17'		16 B.S.
C	A.F.E. 23	Bit. Surfacing			567, 8798 Gal.
1990		Mixed Bit.	24'	1"	Agg. 498 Tons
C	4407-02	Grading	32'		
1953		Gravel	28'	1"	700 C.Y./Mi. (Structural Plate)
M	169 C.M. Arch Culvert				
M	A.F.E. 606	Grav. Resurfacing			3525 TONS
C	4407-03	Sand-Grav. Sub-base	24'	5-12"	
1956		Stab & Bit. Stab. Base	24'	3-6"	
		Plant Mix Bit.	24'	1/2"	
M	A.F.E. 605	Bit. Seal Coat	25'		RC-5, 23992 Gal. Agg. 850 C.Y.
M	C	Light Bit. Seal	25'		RS-1C, 12213 Gal. Agg. 405 C.Y.
M	1979 4407-5F	Bit. Spot Overlay	24'	1 1/2"	Pl. Mix Bit. 1491 Tons
R	1980 4407-07	Bit. Resurfacing	24'	2"	
M	2002 8824-23	Agg. Seal			
S	2006 4407-12	Bit. Overlay	24'	1"	Spec. 2360
S	2006 4407-11	Grading			Mun. Agreement
		Bit. Surfacing	24'	5"	Spec. 2360
	2013 8824-85	Rumble Stripes			Profile

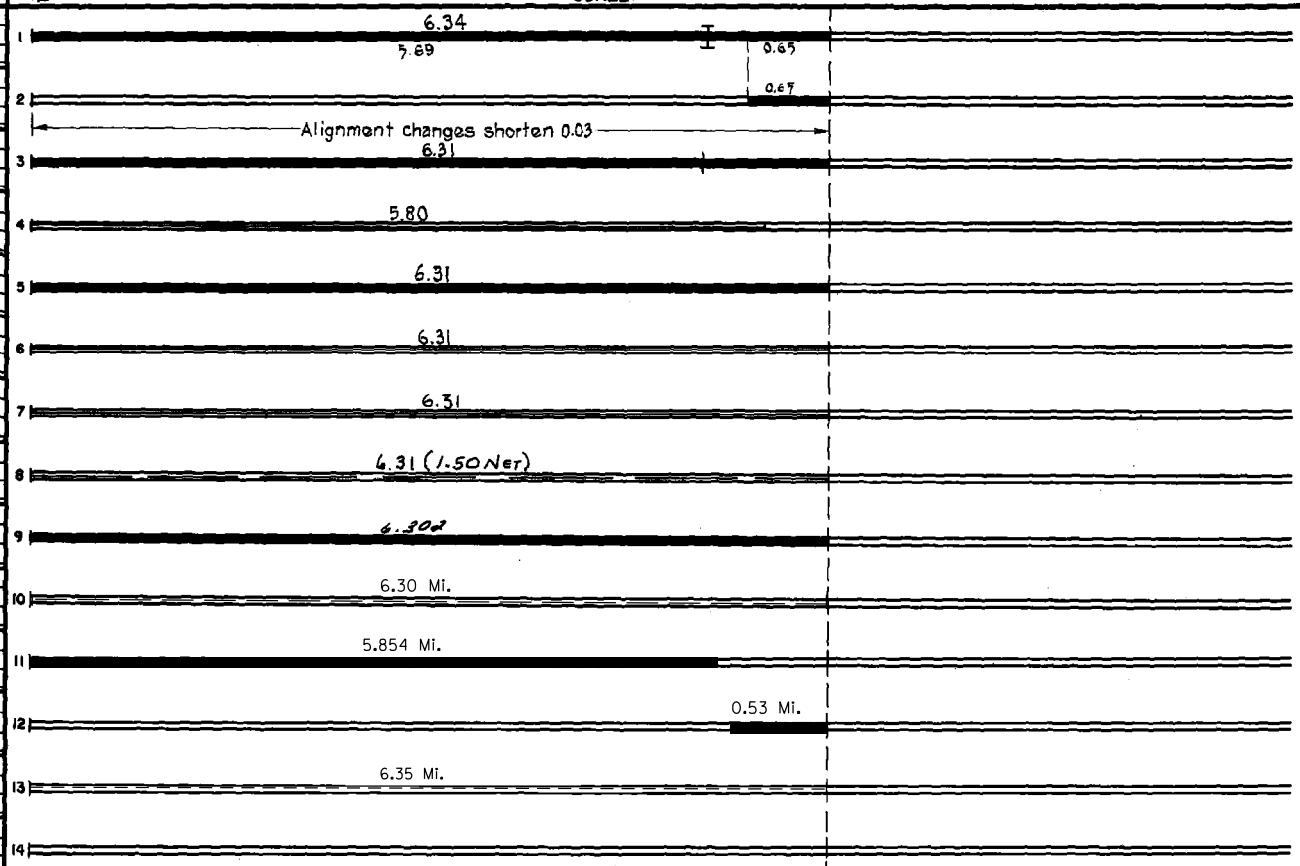

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1952	6.34	5.72	0.01	0.61	0.00	6.33	0.01	0.00	0.00
1953		6.31	5.70	0.00	0.61	0.00	6.31	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1949
