


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6916
TRUNK HIGHWAY 53
COUNTY St. Louis
DISTRICT 1A

LIMITS: W. Corp. Limits of Duluth - Jct. T.H. 33



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1921	53-8-10	Grading Br. 3233 & 3234	30' 26'		
1922	53-8-11	Grading Br. 3465	30' 26'		
1922	53-11-5	Grading	30'		
1922	53-8-01	Concrete	18'	7 1/2"	
1922	53-8-04	Concrete	18'	7 1/2"	
1922	53-8-03	Concrete	18'	7 1/2"	
1922	53-8-02	Concrete	18'	7 1/2"	
1922	53-11-01	Concrete	18'	7 1/2"	
1936	53-11-47	Crossing Signal			
1938	6916-01 A,B&C	Grading 4 Mono. Culverts	41'		
1939	6916-02 A,B&C	Agg. Base	28'	21"	
1939	6916-11 A,B&C	Mixed Bit. Surf.	28'	1"	
1939	6916-10	Seeding			
1939	6916-05 A&B	Mono. Culv. Ext.			
C	6916-135 & C	Concrete Gravel Base	22'	9-6-9	

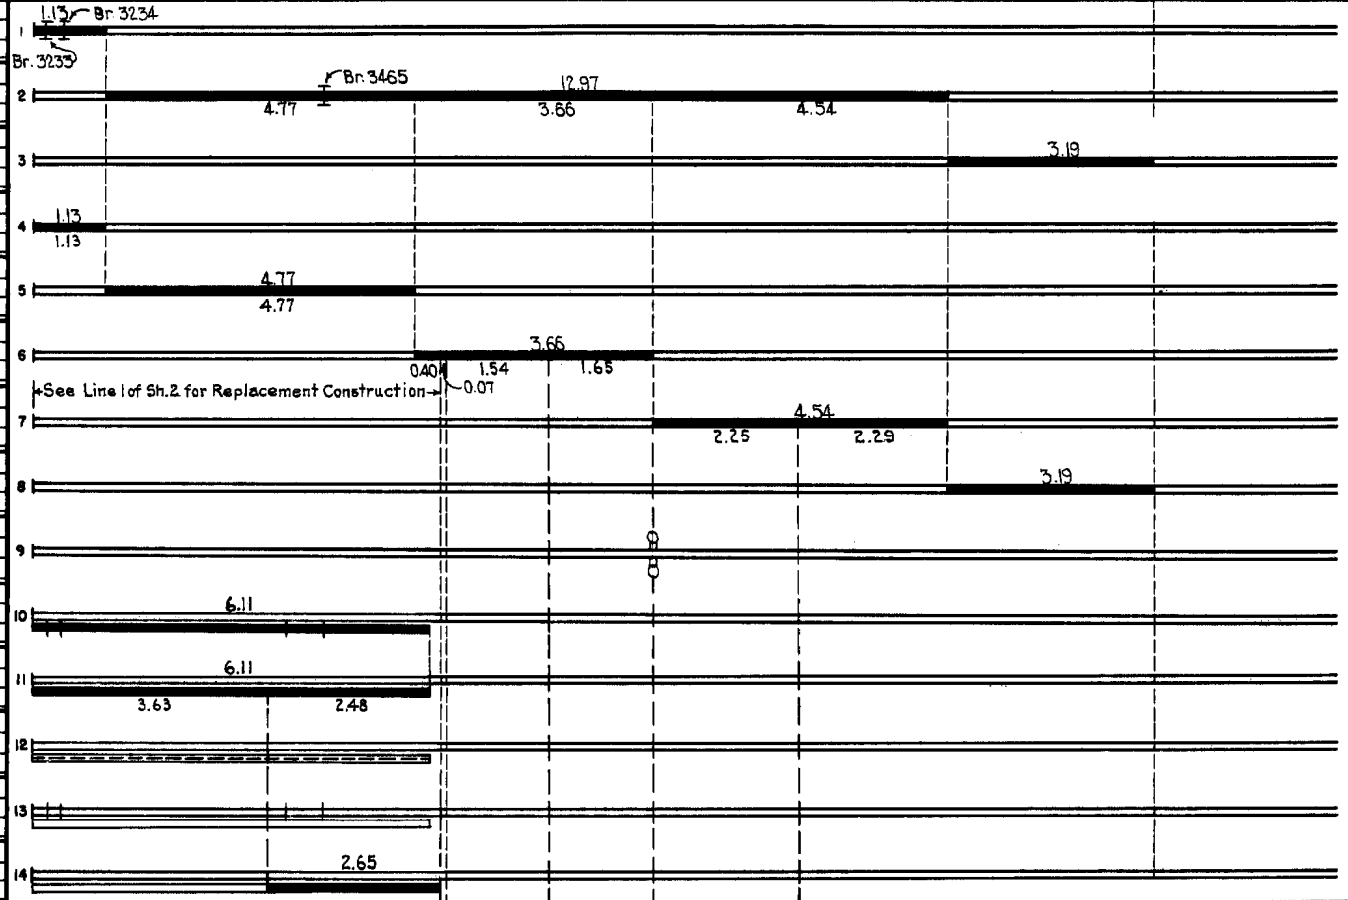

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1922	1939	17.29	17.28	0.01	0.00	17.28	0.01	0.00	0.00	
1940	1941	17.27	17.27	0.00	0.00	17.27	0.00	0.00	0.00	
1942	1951	17.30	17.30	0.00	0.00	17.30	0.00	0.00	0.00	
1952	1974	17.25	17.25	0.00	0.00	17.25	0.00	0.00	0.00	
1975	1975	17.31	17.22	0.09	0.00	17.22	0.09	0.00	0.00	
1976		17.31	11.64	0.09	5.58	11.64	0.09	5.58		


REMARKS: Layout to scale as of 1922.

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6916
TRUNK HIGHWAY 53
COUNTY St. Louis
DISTRICT 1A

LIMITS: W. Corp. Limits of Duluth - Jct. T.H. 33



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
C 1940	6916-04A,B&C	Grading Gravel Lift	37'		1
C 1940	6916-13A,B&C	Concrete Gravel Lift	22'	9-6-9	2
C 1942	6916-15 6916-16	Concrete Gravel Base	22'	9-6-9 4 3/4"	3
C 1942	6916-16 6916-17	Concrete Gravel Base	22'	9-6-9 Var.	4
C 1942	6916-14	Grading Concrete Gravel Base	42' 22'	3" Grav. Shoulders 10' Rt. & Lt. Var.	5
C 1942	1941 A.F.E. 63 1942 A.F.E. 7	Seeding		Seed supplied by R.S.D. (SP 69162273725) Maint. Dept.	6
C 1943	A.F.E. 4	Mixed Bit.	18'	1" On old conc. base. Maint. Dept.	7
C 1945	6916-29	Resloping and Resodding			8
C 1945	6916-28	Bit. Concrete Plant Mix (I)	21'	1 1/2"	9
C 1946	1945 A.F.E. 25 1946 A.F.E. 24 1946 A.F.E. 7	Reshaping Grav. Shoulders Seeding		Spots	10
M 1949	A.F.E. 4	Bit. Fog Seal	21'	RCS-1, 9758 Gal. Agg. 313 C.Y.	11
C 1949	6916-33	Traffic Signals			12
M 1951	A.F.E. 17	Spot Treat. Bit. Surf. Repair	2-4'	MC-4, 3465 Gal. Agg. 210 C.Y.	13
C 1952	6916-38 6916-37	Plant Mix Bit.	22-44'	2'-3"	14

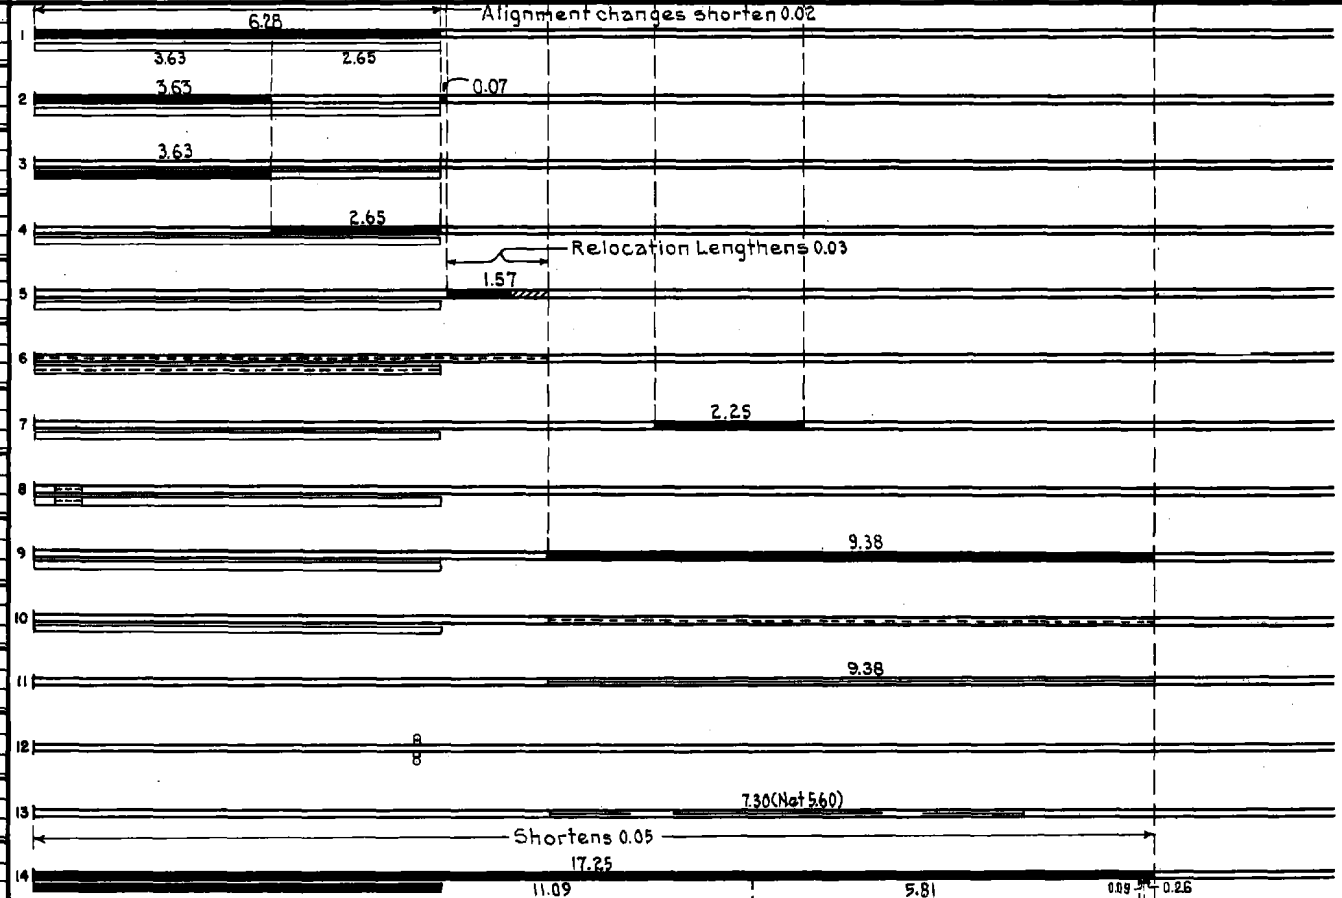

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.


REMARKS: See Sheet No. 1
(1) Approx. 53% of this 9.38 mi. is Plant Mixed Bit. on a variable gravel lift, the balance being Plant Mixed Bit. on the old P.C. Concrete

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6916
TRUNK HIGHWAY 53
COUNTY St. Louis
DISTRICT 1A

LIMITS: W. Corp. Limits of Duluth - Jct. T.H. 33



YEAR BUILT	PROJECT N°	DESCRIPTION		REMARKS	CODE N°
		TYPE	WIDTH THICKNESS		
C 1955	6916-39	Sand-Grav. Sub-base Bit. Stab. Base Plant Mix. Bit.	40' 12" 40' 6" 24' 3"		
M&C 1956	A.F.E. 605 A.F.E. 825	Light Bit. Seal Side Ditch Const.	24'	RC-2, 345 Gal. Agg. 30 C.Y.	10.97
C 1957	6916-40A&B A.F.E. 827	Traffic Signals Deceleration Lanes			
M 1958	A.F.E. 605	Light Bit. Seal	23'	RC-2, 15875 Gal. Agg. 780 C.Y.	9.20 Repair
C&M 1959	A.F.E. 820 A.F.E. 604	Deceleration Lanes Bit. Surf. Repair		Plant Mix 549 Tons	Net Repair 950
C&M 1961		Grade, Base & Rd. Mix Bit on Frontage Road Bit. Surf. Repair		By Maint. At edges of surf imp.	
M 1963	S.F. & E.	Spot Treat Bit. Surf. Repair		Pl. Mix 1368 Tons MC-3, Jack 800 Gal.	9.50 (Net Repair 5.18)
C 1965	6916-46 6916-47	Traffic Signals Lighting System		Flasher System	
C 1966	6916-51	Channelization, Traffic Signals, Lighting System Maint. Proj.	22' 1 1/2"		11.09
C 1967	6916-53	Plant Mix Bit Surf. Gravel Shoulders	22' 1 1/2"		5.96 5.33 5.81
C 1968	6916-55	Grading Base Pl. Mix Bit Surface for Fr. Rd. & Turn Lanes			0.94 1.36 0.96 2.55
C 1968	F011-3(45)	GRADING		FOR BA. INFORMATION SEE C.S. 6911	
C 1969	6917-58 F011-3(47)	GRAVEL BASE P.C. CONC. Pl. Mix Bit. SLDRS	20' 24'	CONST. ON N.B. RDWY IS 0.25 MI.	
C 1970	6916-48 F011-3(48)	GRADING		NO CONST. ON N.B. RDWY. FROM MI. Pt. 12.09 TO 13.41 #S.R. RDWY MI. Pt. 14.40 TO 16.70	

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS: See Sheet No. 1
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	

0.25 0.26
RELOCATION LENGTHS 0.01 MI.

