


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 8612
TRUNK HIGHWAY 241
COUNTY Wright
DISTRICT 3B

LIMITS: Main St. in St. Michael - Jct. T.H. 152

Ref. Pt. 000+00.000 - 003+00.524



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
	A.F.E. 30 (Dist. 9)	Reshaping			Transferred from C.S. 8610 (T.H. 152) in 1955
1938	A.F.E. 31	Mixed Bit.	26'	1"	
C		Grading	34'50"		
1955	8612-02	Sand-Grav. Sub-base	24'30"	15"	
		Gravel Base	3'50"	3"	
C		Bit. Surfacing			MC-0&2, 58488 Gal.
1955	A.F.E. 821	Mixed Bit. (Mixed Prime)	24'	1 1/2"	
C		Sand-Grav. Sub-base*	34'30"	12"	*M.I. Pt. 0.00 - 0.32
1956	8612-04	Bit. Stab. Base*	34'30"	6"	
	8612-03	Plant Mix Bit.	24'30"	3"	
C		Grade X-ing Signals			
1957	8612-06				
M		Bit. Seal Coat	25'		RC-3, 8582 Gal. Agg. 325 C.Y.
1959	A.F.E. 605				
C	8680-35	Grading			
1973	I 094-3 (185) 203	Gravel Base Pl. Mix Bit. Base		14" 1 1/2"	
C	8680-36	Pl. Mix. Bit. Surf.	24'	1 1/2"	
1973	I 094-3 (185) 203	Gravel & Pl. Mix Bit. Shoulders			
C		Pl. Mix Bit. Surf.	24'	1 1/2"	
1979	8612-08	Pl. Mix Bit. Shoulders Right Turn Lane			
C		Bit. Milling	24'	1/2"	
1997	8612-10	Bit. Overlay	24'	Var.	Spec. 2341
S	S05182	Grading, Conc. & Bit. Drainage Wall	48'	Var.	Spec. 2360
2007	8612-11 (Completion)	Box *86X05, Light	48'	Var.	CO, 15'

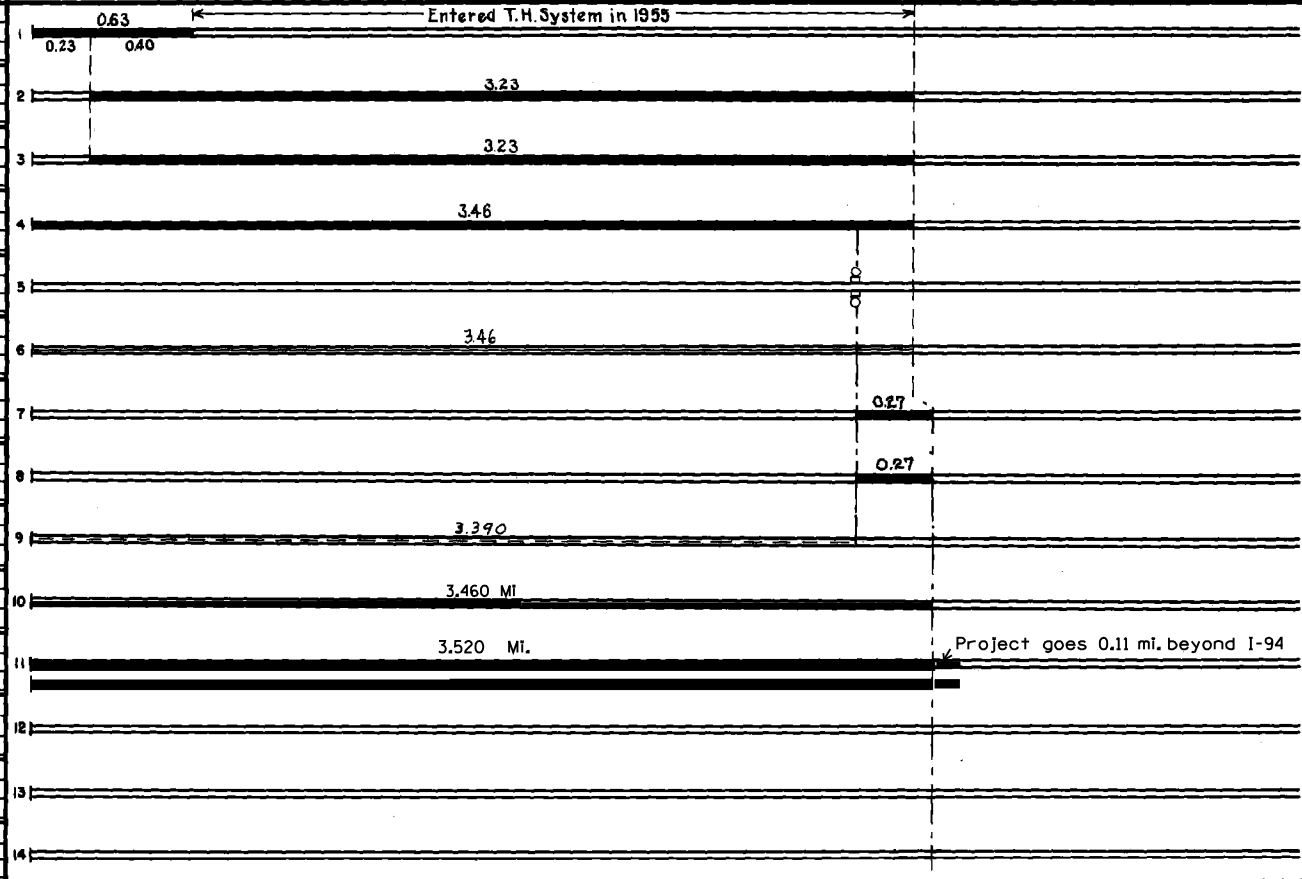

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1955	1972	3.46	2.71	0.00	0.75	0.00	3.46	0.00	0.00	0.00
1973		3.53	2.73	0.05	0.75	0.00	3.48	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1955.
