Wadena Comprehensive Plan

Dec-19-2012

Activity ID	Activity Name	Original Duration	Start	Finish
1.0 Project Management				
Administration				
1.1	Study Management	315	Oct-04-2011 A	Dec-14-2012 A
1.1a	PMT Meeting #1	0	Oct-04-2011 A	
1.1b	PMT Meeting #2	0	Dec-20-2011 A	
1.1c	PMT Meeting #3	0	Oct-10-2012 A	
1.1d	PMT Meeting #4	0	Jan-15-2013*	
1.2	QA/QC	315	Jan-01-2012 A	Dec-14-2012 A
2.0 Comprehensive Plan				
Comprehensive Plan				
2.1	Community Profile	80	Jan-01-2012 A	Feb-01-2012 A
2.2	Goals, Objectives and Vision Statement	40	Mar-01-2012 A	Jun-01-2012 A
2.3	Growth Projections	25	Apr-01-2012 A	Jul-01-2012 A
2.4	Infrastructure Analysis	40	Feb-01-2012 A	May-01-2012 A
2.5	Land Use Alternatives	80	Apr-01-2012 A	Aug-31-2012 A
2.6	Plan Elements and Planning Strategies	202	Sep-01-2012 A	Oct-30-2012 A
2.7	Implementation Plan	21	Oct-31-2012 A	Dec-31-2012 A
2.8	Draft and Final Plan	62	Nov-30-2012 A	Jan-31-2013
3.0 Transportation Plan				
Data Collection				
3.1	Data Collection	20	Jan-02-2012 A	Feb-01-2012 A
Origin-Destination Study				
3.2	Origin-Destination Survey	63	Oct-03-2011 A	Dec-01-2011 A
Traffic Forecasts & Level-of-Service Analysis				
3.3.1	2035 Forecasts	85	Jun-01-2012 A	Aug-31-2012 A
3.3.2	Capacity and LOS Analysis	67	Aug-01-2012 A	Aug-31-2012 A
System Analysis				
3.4.1	Existing Functional Classification	44	Jan-03-2012 A	Feb-01-2012 A
3.4.2	Existing Jurisdiction Review	22	Jan-03-2012 A	Feb-01-2012 A
3.4.3	Future Functional Classification	14	Nov-01-2012 A	Dec-31-2012 A
3.4.4	Future Jurisdiction Review	14	Nov-01-2012 A	Dec-31-2012 A
Access Management and Safety				
3.5.1	Access Analysis	77	Mar-01-2012 A	May-01-2012 A
3.5.2	Safety Analysis	57	Mar-01-2012 A	May-01-2012 A
System Needs				
3.6.1	Improvement Recommendations	14	Dec-01-2012 A	Jan-04-2013
3.6.2	TH Corridor Vision	14	Nov-01-2012 A	Dec-31-2012 A
Sub Area Needs				
3.7	Sub Area Needs	85	Aug-01-2012 A	Dec-31-2012 A
Modal Assessment				
3.8	Modal Assessment	1	May-01-2012 A	Jul-02-2012 A
Implementation Plan				
3.9	Implementation Plan	20	Dec-01-2012 A	Jan-17-2013
Draft and Final Reports				
3.10	Draft and Final Reports	1	Nov-30-2012 A	Jan-17-2013
4.0 Public Involvement				
Steering Committee Meetings				
4.1	Steering Committee Meetings	296	Jan-25-2012 A	Feb-01-2013
4.1a	Steering Committee Meeting 1	0		Jan-25-2012 A
4.1b	Steering Committee Meeting 2	0		Apr-20-2012 A
4.1c	Steering Committee Meeting 3	0		Jun-06-2012 A
4.1d	Steering Committee Meeting 4	0		Aug-21-2012 A
4.1e	Steering Committee Meeting 5	0		Oct-24-2012 A
4.1f	Steering Committee Meeting 6	0		Jan-15-2013*
4.1g	Steering Committee Meeting 7	0		Feb-01-2013*
Focus Group Meetings				
4.2	Focus Group Meetings	0		Feb-17-2012 A
Open House Public Meetings				
4.3.1	Early Public Meeting	0		Feb-17-2012 A
4.3.2	Mid-Study Public Meeting	0		Dec-31-2012*
4.3.3	Draft Plans Public Meeting	0		Jan-17-2013*
Presentations				
4.4.1	MnDOT District 4	0		Dec-31-2012*

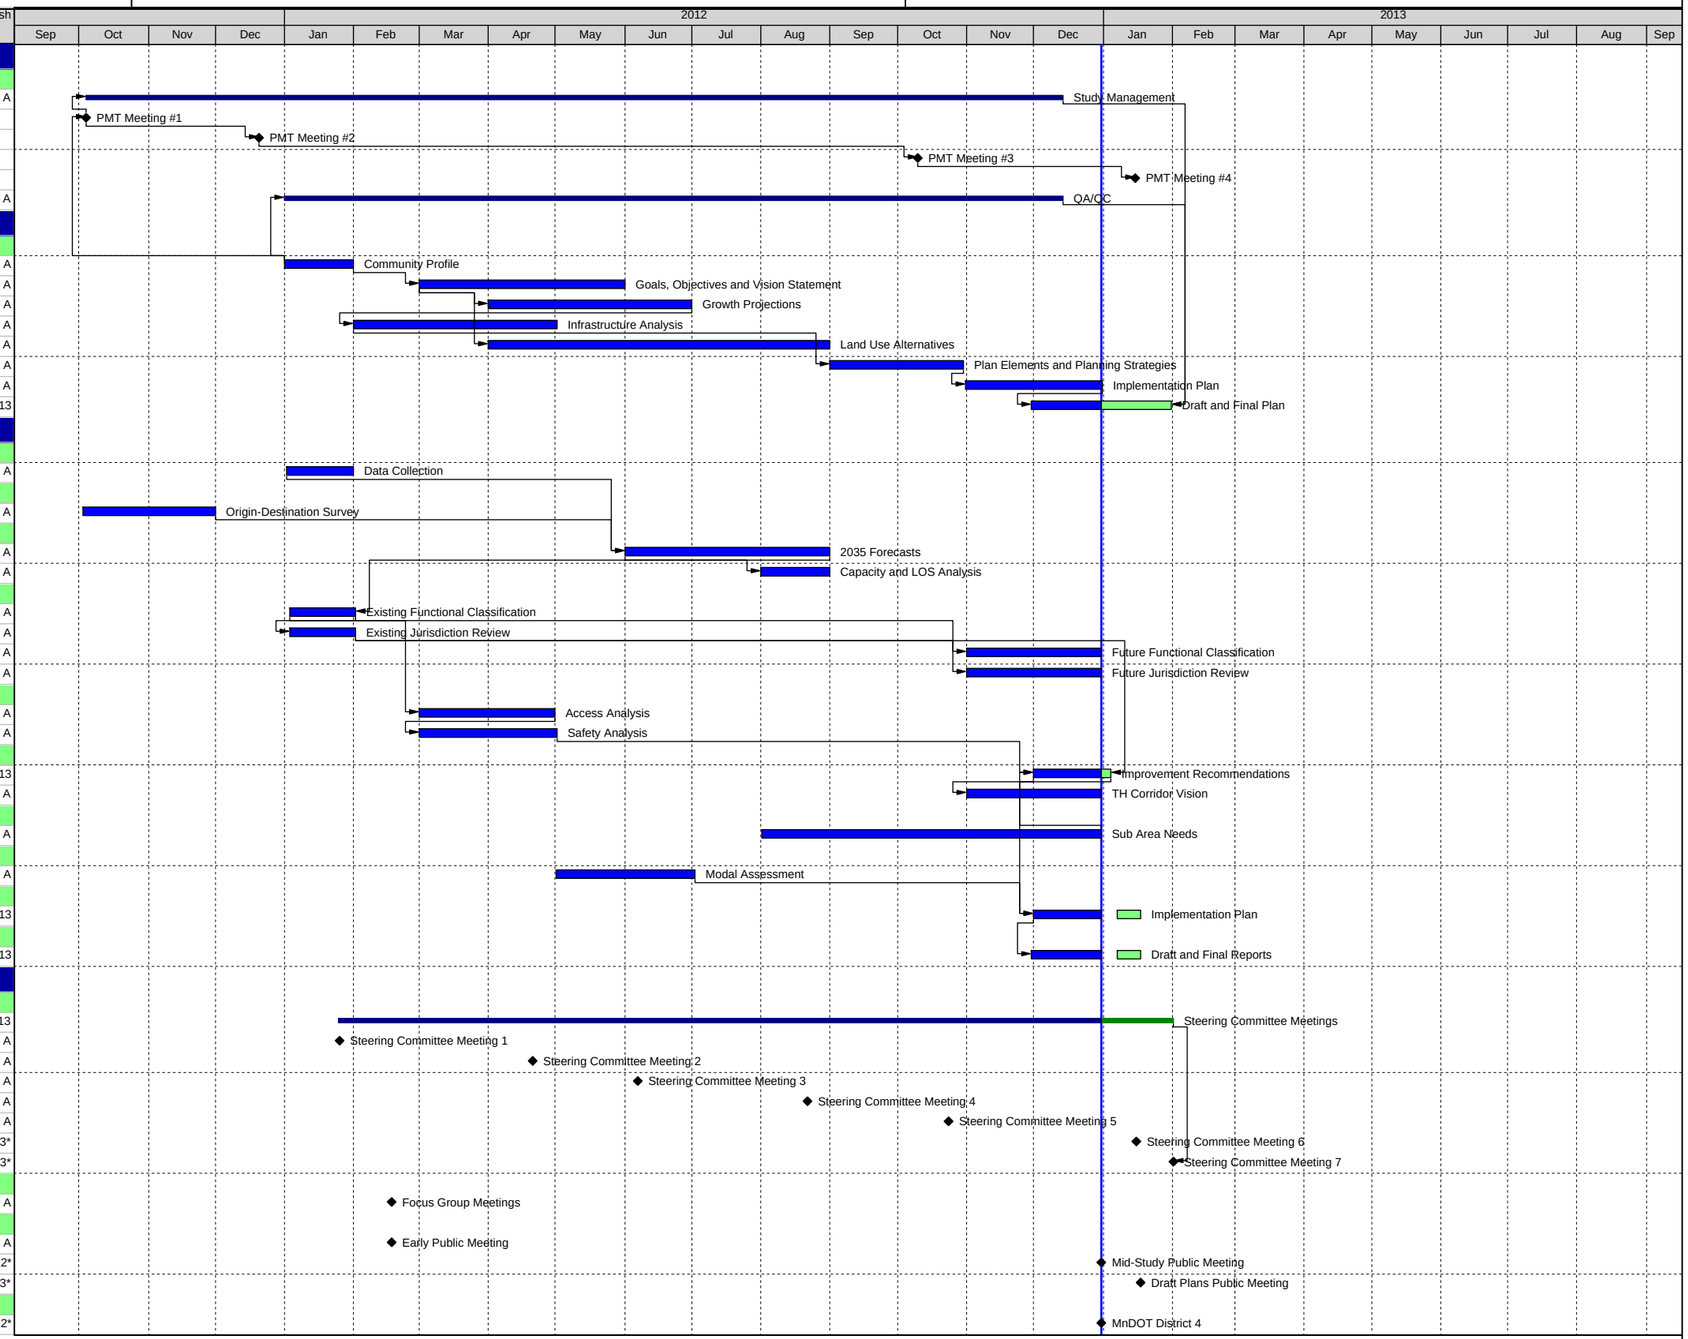
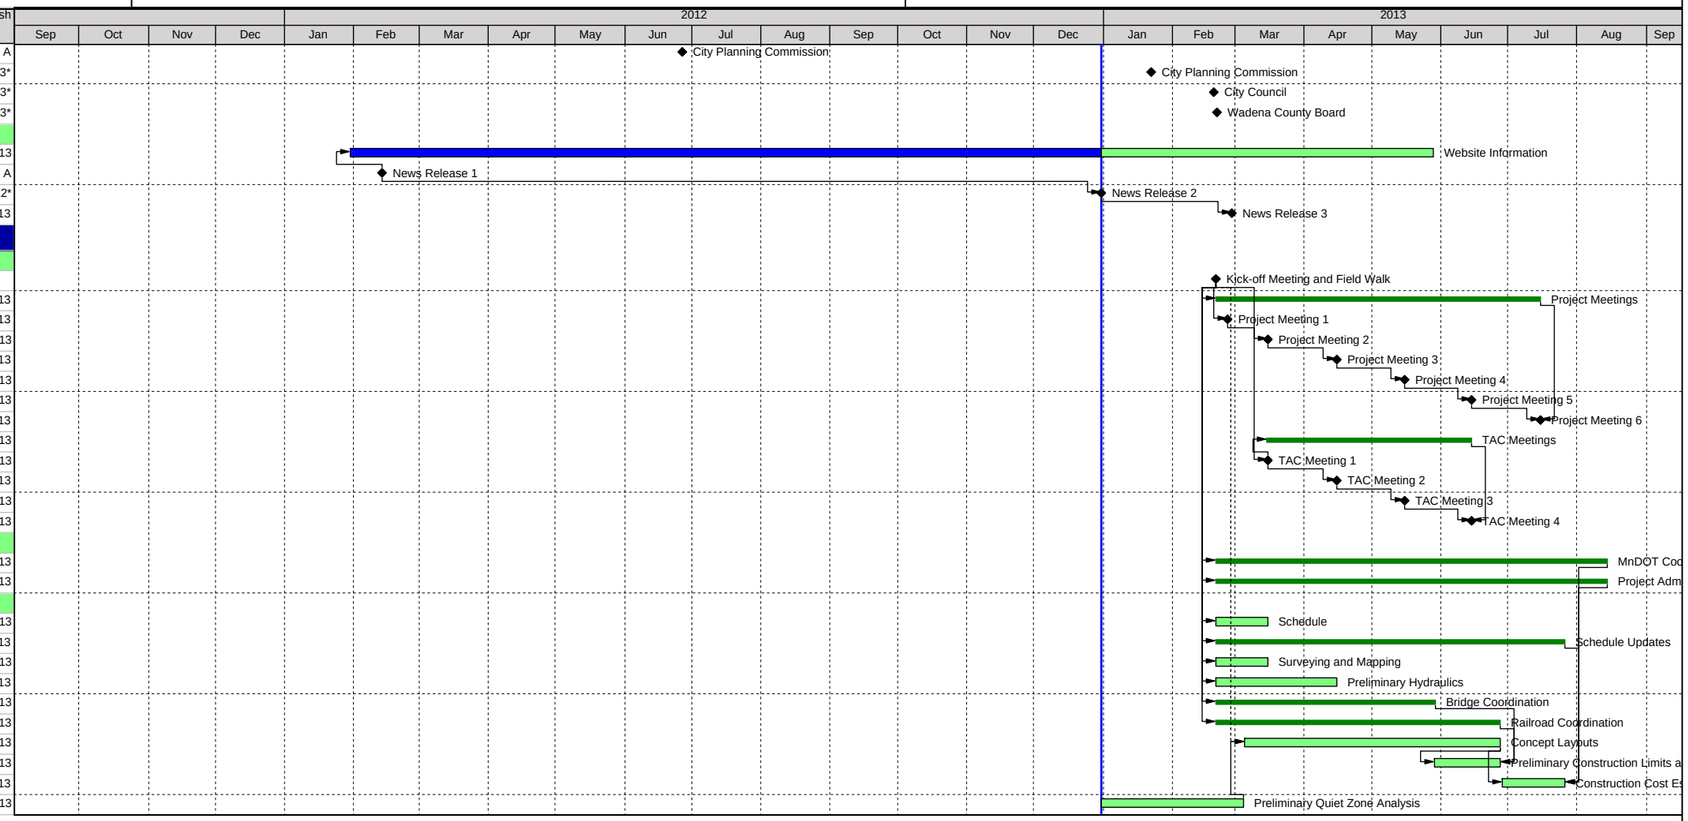
Activity ID	Activity Name	Original Duration	Start	Finish
4.4.2	City Planning Commission	0		Jun-26-2012 A
4.4.2b	City Planning Commission	0		Jan-22-2013*
4.4.3	City Council	0		Feb-19-2013*
4.4.4	Wadena County Board	0		Feb-20-2013*
Study Information				
4.5.1	Website Information	341	Jan-30-2012 A	May-28-2013
4.5.2	News Release 1	0		Feb-13-2012 A
4.5.3	News Release 2	0		Dec-31-2012*
4.5.4	News Release 3	0		Feb-27-2013
5.0 Conceptual Preliminary Design				
Project Management - Meetings				
5.1.1	Kick-off Meeting and Field Walk	0	Feb-20-2013*	
5.1.2	Project Meetings	102	Feb-20-2013	Jul-15-2013
5.1.2a	Project Meeting 1	0		Feb-25-2013
5.1.2b	Project Meeting 2	0		Mar-15-2013
5.1.2c	Project Meeting 3	0		Apr-15-2013
5.1.2d	Project Meeting 4	0		May-15-2013
5.1.2e	Project Meeting 5	0		Jun-14-2013
5.1.2f	Project Meeting 6	0		Jul-15-2013
5.1.3	TAC Meetings	65	Mar-15-2013	Jun-14-2013
5.1.3a	TAC Meeting 1	0		Mar-15-2013
5.1.3b	TAC Meeting 2	0		Apr-15-2013
5.1.3c	TAC Meeting 3	0		May-15-2013
5.1.3d	TAC Meeting 4	0		Jun-14-2013
Project Management				
5.1.4	MnDOT Coordination	124	Feb-20-2013	Aug-14-2013
5.1.5	Project Administration	124	Feb-20-2013	Aug-14-2013
Concept Engineering				
5.2.1a	Schedule	18	Feb-20-2013	Mar-15-2013
5.2.1b	Schedule Updates	111	Feb-20-2013	Jul-26-2013
5.2.2	Surveying and Mapping	18	Feb-20-2013	Mar-15-2013
5.2.3	Preliminary Hydraulics	39	Feb-20-2013	Apr-15-2013
5.2.4	Bridge Coordination	70	Feb-20-2013	May-29-2013
5.2.5	Railroad Coordination	91	Feb-20-2013	Jun-27-2013
5.2.6	Concept Layouts	82	Mar-05-2013	Jun-27-2013
5.2.7	Preliminary Construction Limits and ROW Maps	22	May-29-2013	Jun-27-2013
5.2.8	Construction Cost Estimates	20	Jun-28-2013	Jul-26-2013
5.2.9	Preliminary Quiet Zone Analysis	45	Dec-31-2012*	Mar-04-2013
