FORM RL-7

SHEET 1 OF 1

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1814
TRUNK HIGHWAY 371B
COUNTY Crow Wing
DISTRICT 3A

LIMITS: Jct. MNTH - 371 - MNTH - 210

Ref. Pt. 000+00.000 - 006+00.526



YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C 2001	1814-01	Bit. Mill & Overlay	24'	3"	Spec 2350
C 2002	1809-58	Grading, Bit. Surfacing	48' &	4.5"	Spec. 2350
		Bridge	24'		
M 2007	8823-101	Agg. Seal			FA-2
C 2009	1814-02	Milling Bit. Overlay	var.	var.	
C 2018	1814-06	Grading Full Dep.Reclam. Bit. Surfacing reconstruction	var.	6"-7" 6" 8"	Bit. over Conc. ML & TL's agg. base
C 2018	1814-09	Bituminous Mill & Overlay ML, shldrs ramps and loops	var.	2"	Spec. 2360

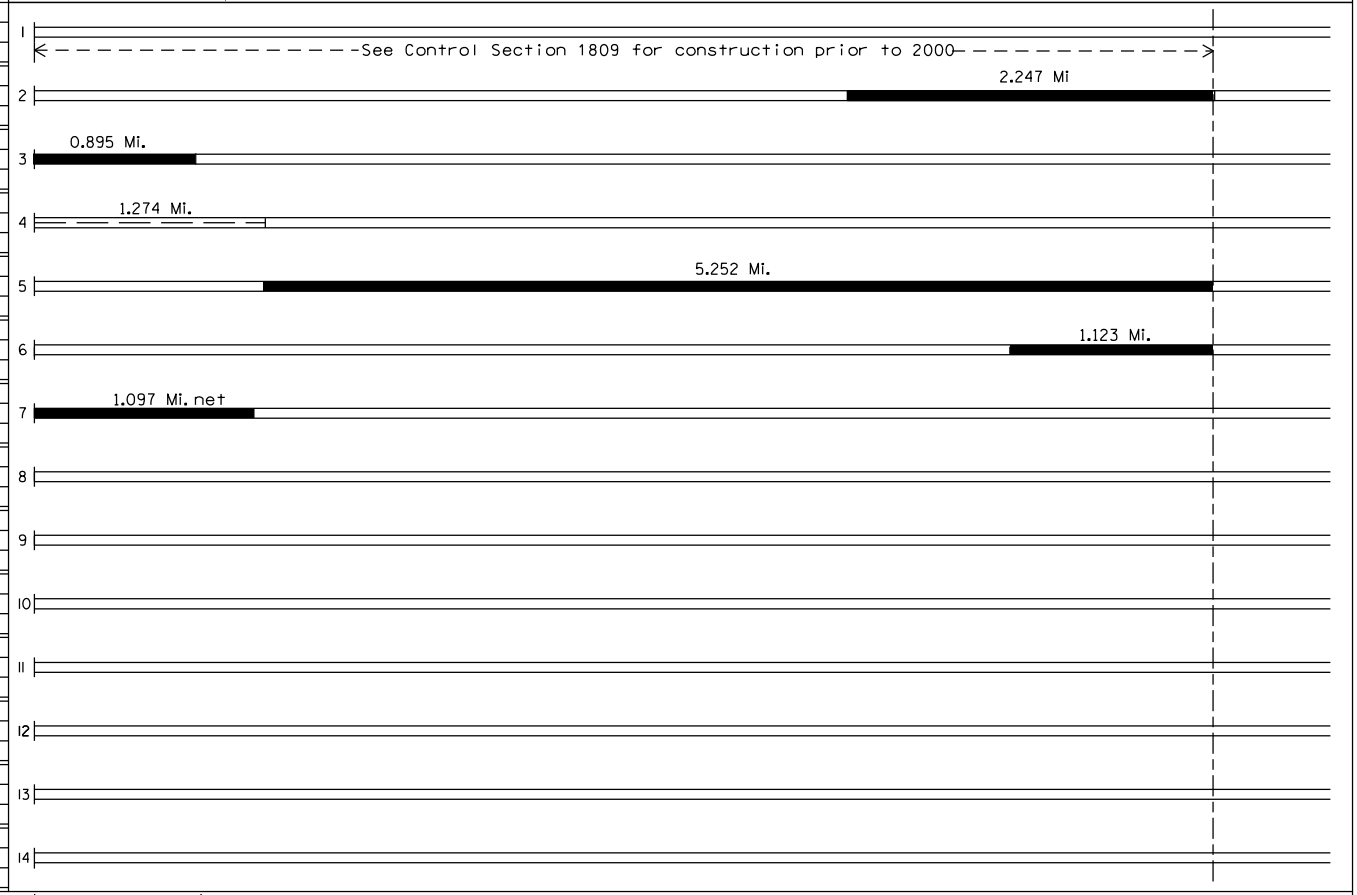

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
