FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2705
TRUNK HIGHWAY 7
COUNTY Hennepin
DISTRICT 5A

LIMITS: S. Co. Line - Jct T.H.41 in Excelsior



YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
					No Record of Constr.	
		Bit. Tr. Gravel	27'	2"	Added in 1934.	
		Regrading	40'			
1938	A.F.E. 21	Mixed Bitum.	27'	2"	Maint. Dept.	
M	A.F.E. 47	Frost Boil Corr.			SC-3, 2796 Gal./Mi.	
1941	A.F.E. 24	& Spot Treat.	28'		Grav. 497 C.Y./Mi.	
		Bit. Surf. Repair			Maint. Dept.	
M		Spot Treat.			SC-3A, 1239 Gal./Mi.	
1942	A.F.E. 4	Bit. Surf. Repair	24'		Grav. 49 C.Y./Mi.	
					Maint. Dept.	
M	A.F.E. 23	Subgrade Treat.	24'		RT-6, 1982 Gal./Mi.	
1943	A.F.E. 4	Spot Treat.			Grav. 382 C.Y./Mi.	
		Bit. Surf. Repair	27'		Maint. Dept.	
M					RT-6, 613 Gal./Mi.	
1944	A.F.E. 4	Bit. Fog Seal (Spots)	24'		Sand 5 C.Y./Mi.	
					Maint. Div.	
M		Spot Treat.			RT-6, 6190 Gal./Mi.	
1945	A.F.E. 4	Bit. Surf. Repair	24'		Grav. 267 C.Y./Mi.	
					Maint. Div.	
M		Spot Treat.			MC2, 8809 Gal.	
1948	A.F.E. 4	Bit. Surf. Repair	24'		Agg. 452 C.Y.	
M					SC-3, 21301 Gal.	
1952	A.F.E. 4	Bit. Surf. Repairs	22'	1"	Agg. 1666 Tons	

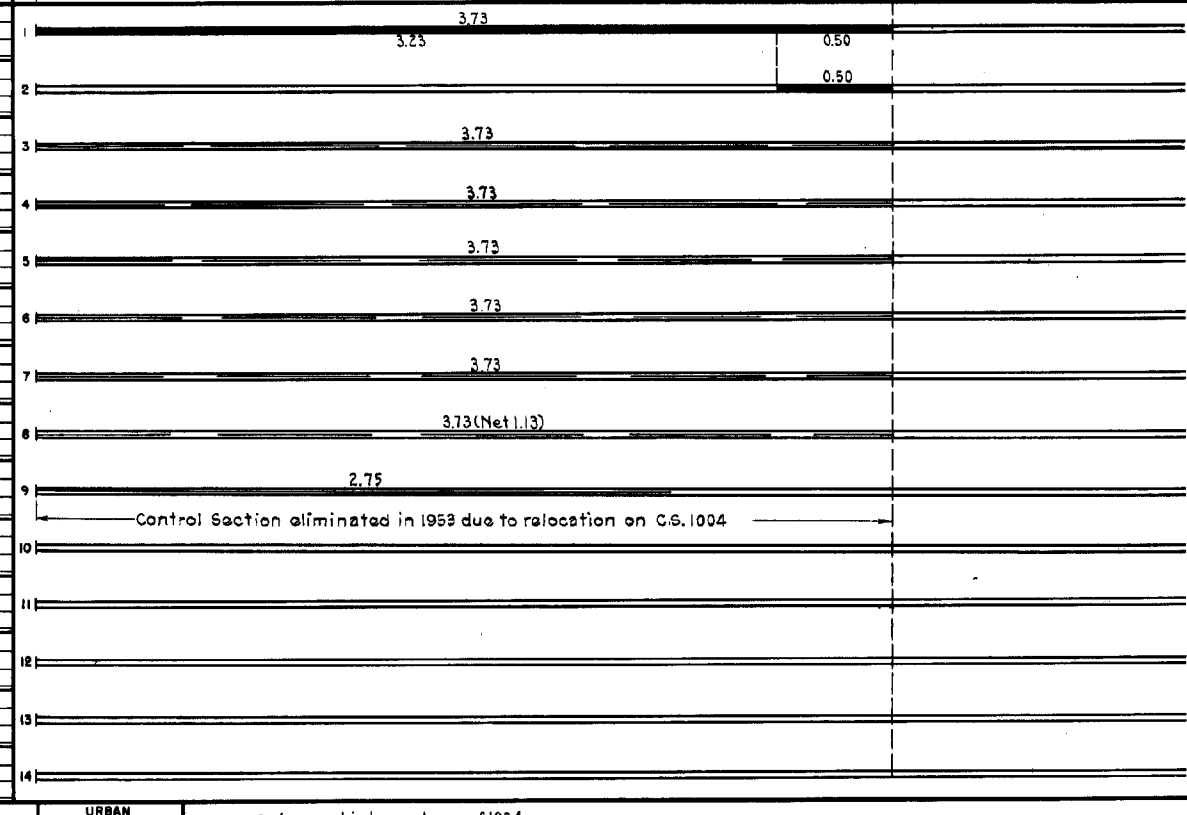

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1952	3.73	3.23	0.00	0.50	0.00	3.23	0.00	0.50	0.00
1953		0.00								

REMARKS: Layout is to scale as of 1934

6-11-54
