FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5612
TRUNK HIGHWAY 52
COUNTY Otter Tail
DISTRICT 4A

LIMITS: W. Co. Line (E. Corp. Limits of Rothsay) - N. Jct. T.H. 59.

PLAN



YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Earth	20'		No Record of Constr.	
		Grading	30'			
1926	52-64-23	Gravel	24'	2½"	1200 C.Y./Mile.	
1932	52-64-23	Concrete	20'	8-7-9		
C		Grading, Sub-base			10" Sand-Gravel Sub-base	
1962	5680-21&38	Gravel & Rd. Mix Bit. Base		5½-1½		
		Bit. Surf.	24'	3"	1" Rd. Mix & 2" Plant Mix	
C	5680-49	Grade, Base				
1968	5680-59	Pl. Mix. Bit. Surf.	Var.	2"-3"		
	5612-04	Pl. Mix. Bit. Shldrs.				

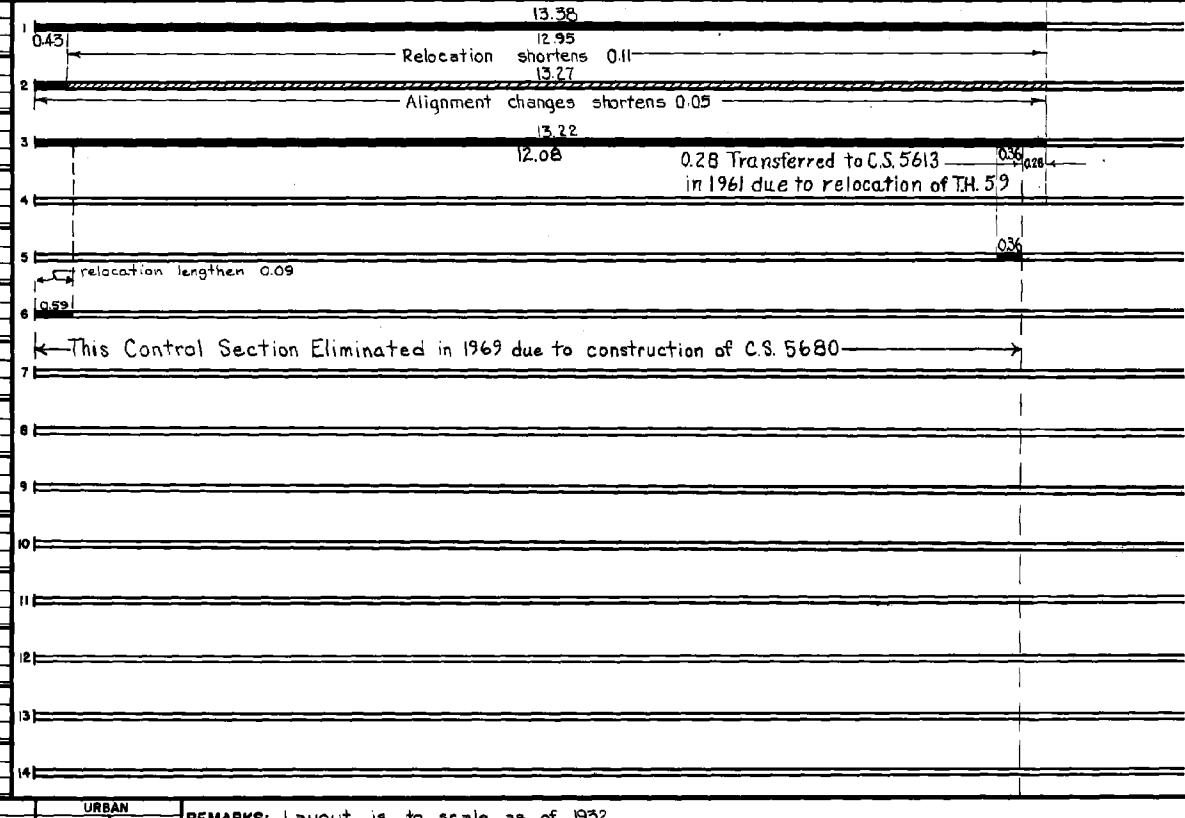

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED ROWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED ROWY. MI.	INCORPORATED BR. MI.	RURAL ROWY. MI.	RURAL BR. MI.	URBAN ROWY. MI.	URBAN BR. MI.
1921	1925	13.38	12.45	0.00	0.93	0.00	13.38	0.00	0.00	0.00
1926	1931	13.27	12.78	0.00	0.49	0.00	13.27	0.00	0.00	0.00
1932	1950	13.22	12.73	0.00	0.49	0.00	13.22	0.00	0.00	0.00
1951	1960	13.22	12.71	0.00	0.51	0.00	13.22	0.00	0.00	0.00
1961	1967	12.94	12.43	0.00	0.51	0.00	12.94	0.00	0.00	0.00
1968	1969	13.03	12.52	0.00	0.51	0.00	13.03	0.00	0.00	0.00
1969		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1932.
