FORM R.L.-7 REV. 3-58

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

SHEET 1 OF 1

CONTROL SECTION 6810
TRUNK HIGHWAY 313
COUNTY Roseau
DISTRICT 2B

LIMITS: Jct. T.H. 11 in Warroad — International Boundary

Ref. Pt. 000+00.000 - 006+00.266

Dist. No.	Year Built	Project No	Description: Type	Width	Thickness	Remarks
	1957		Gravel	34'	2"	Graded under S.P. 68-510-01 Added in 1959.
	M 1960		Spot Gravel Resurfacing			Gravel 246 Tons
262	C 1962	6810-01	Sand-Gravel Sub-base Gravel & Rd. mix bit. base Road Mix Bit. Surf.	32' 30' 26'	8"-18" 2&2" 1½"	
	C 1964	SF	(At Custom House) Mixed Bit. on Gravel Base			On Service Road & Parking Area
2576	M 1976	SF	Bit. Surfacing Seal Coat			Pl. Mix 4760 Ton Agg. 180 Ton
	C 1983	6810-05	Grading Bit. Surfacing & (3) Rt. Turn Lanes	30' 12'	1½" 1½"	Bit. Spec. 2331 Bit. Spec. 2331
	M 1997	6810-07	Mill & Bit. Overlay	24'	3"	Spec. 2341
	C 2002	6810-06	Grading Bit. Overlay	40' 20'	1½"	Type MV 3 Spec. 2350
	M 2005	8822-52	Bituminous Seal Coat	28'		F2

PLAN

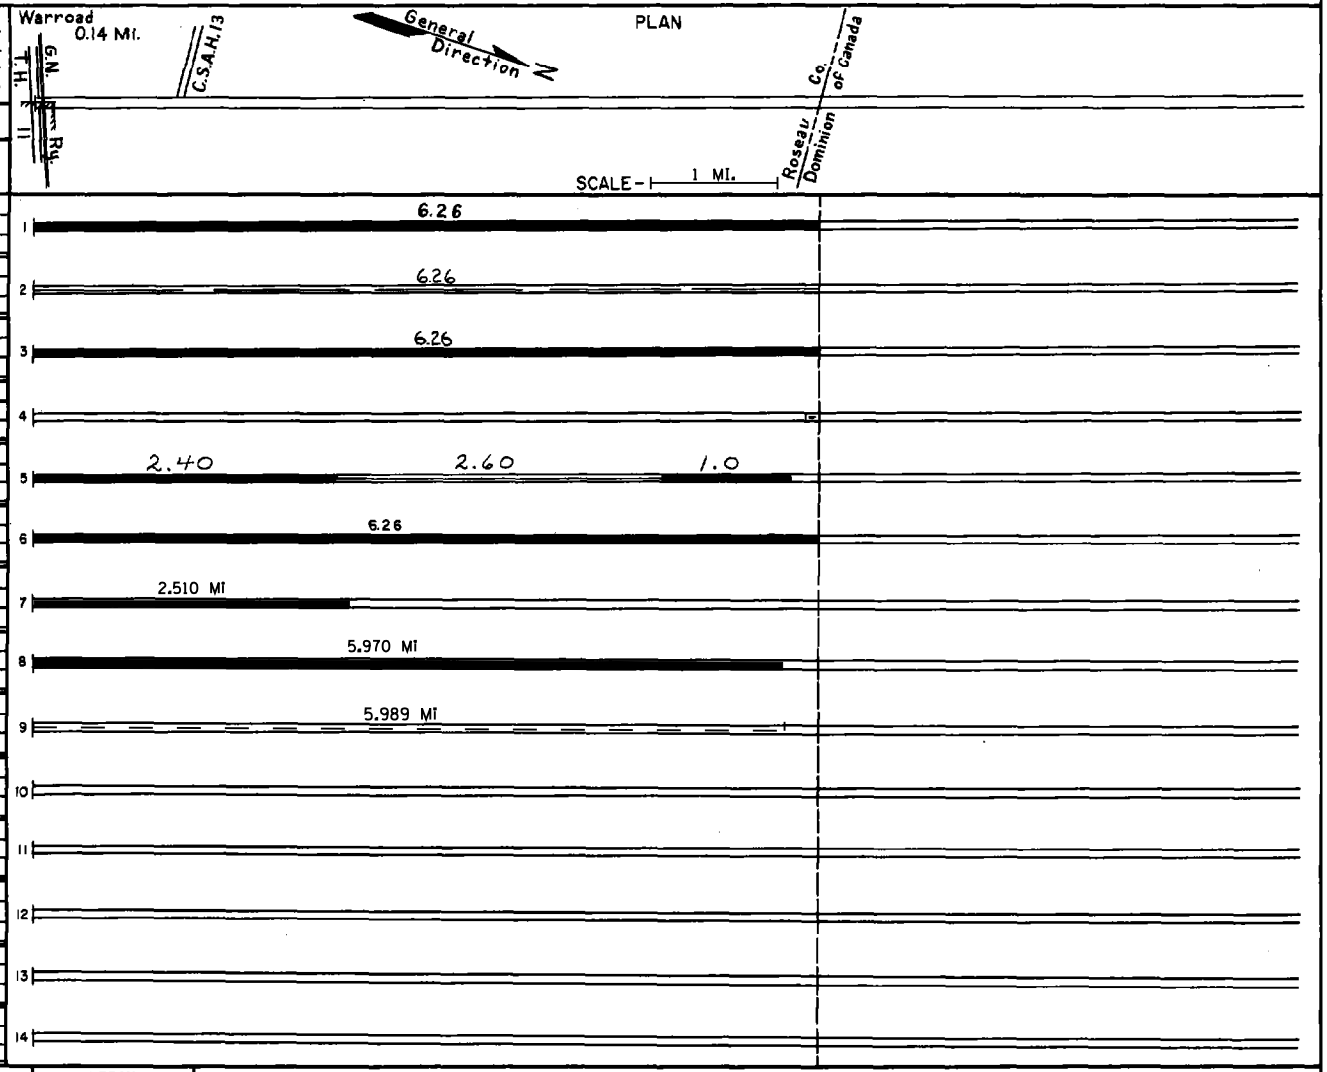

Years From	Years To	Total Miles	Unincorporated Rdwy. Mi.	Unincorporated Br. Mi.	Incorporated Rdwy. Mi.	Incorporated Br. Mi.	Rural Rdwy. Mi.	Rural Br. Mi.	Urban Rdwy. Mi.	Urban Br. Mi.
1959		6.26	6.12	0.00	0.14	0.00	6.12	0.00	0.14	0.00

REMARKS: Layout is to scale as of 1959.
