R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7324
TRUNK HIGHWAY 302
COUNTY Stearns
DISTRICT 3A

LIMITS: Jct. T.H. 71 in Sauk Centre - State Home School for Girls

Ref. Pt. 000+00.000 - 000+00.943

YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Gravel	22'		No Record of Const. Added in 1951	
C 1953	7324-01	Grading	20'-24'		3½-9½ Select Mat'l	
		Gravel Base	20'-24'	2½"		
		Mixed Bit.	20'-22'	1½"		
M 1962		Light Bit. Seal	22'		RS-2, 1526 Gal. Agg. 60 C.Y.	
M 1967	C	Bit. Seal Coat	25'		CRS-2 Bit. 2,482 Gal. FA-3 Agg. 100 C.Y.	
C 1972	-02	Pl. Mix Bit.	20'	1½"		
M 1984	7324 SF	Chip Seal - Seal Coat	18'-22'		FA-2 Seal Coat Rock 196 Ton 3000 Gal. CRS-2 Emulsion	

PLAN



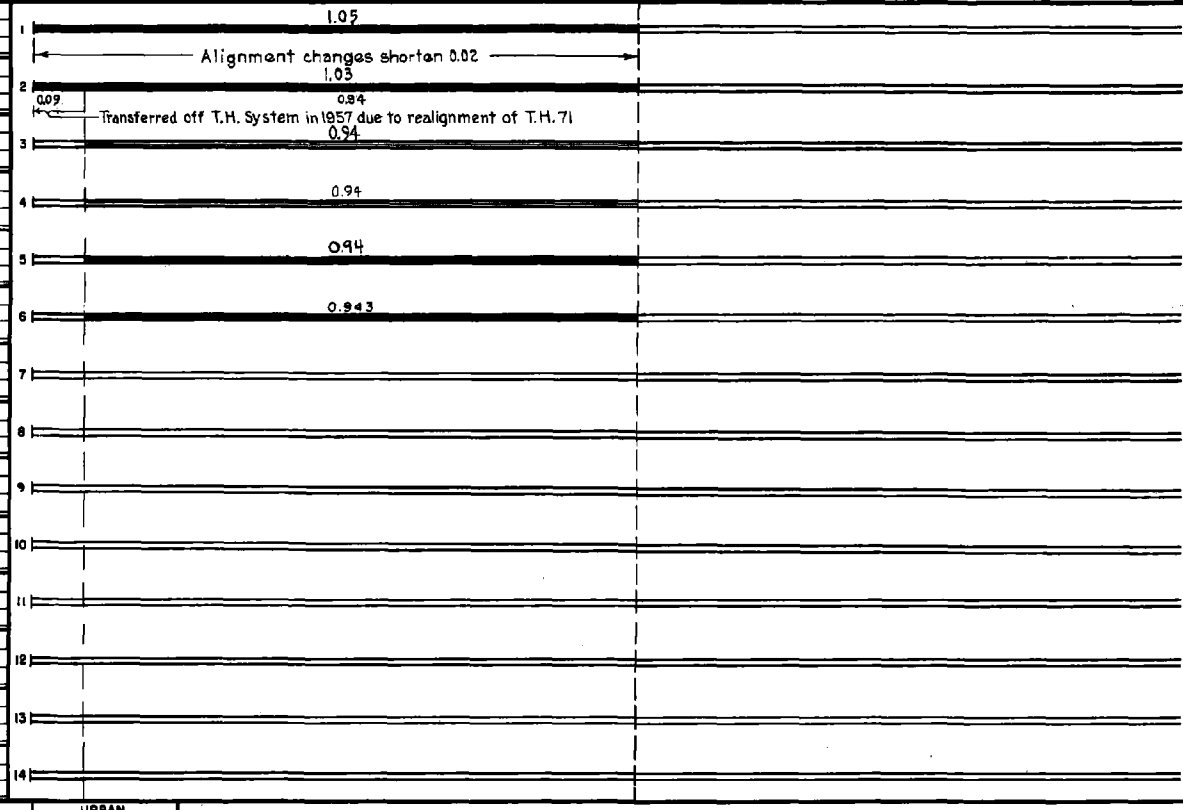

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1951	1952	1.05	0.18	0.00	0.87	0.00	0.18	0.00	0.87	0.00
1953	1956	1.03	0.16	0.00	0.87	0.00	0.16	0.00	0.87	0.00
1957		0.94	0.16	0.00	0.78	0.00	0.16	0.00	0.78	0.00

REMARKS: Layout is to scale as of 1951
