FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7909
TRUNK HIGHWAY 74
COUNTY Wabasha
DISTRICT 6A

LIMITS: S. Co. Line - Jct. T.H. 61

Ref. Pt. 051+00.989 - 055+00.393

YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Gravel	24'		No Record of Constr. Added in 1934	
C 1942	A.F.E. 22	Regrading			Maint. Dept.	
C 1943	1942 A.F.E. 6	Crushed Rock Surfacing			709 C.Y./Mi. Maint. Dept.	
	1943 A.F.E. 6					
	(1)	Bit. Surf.-Treated	24'	3/4"		
M 1949	A.F.E. 4	Bit. Surf. Repair	24'		MC-3, 858 Gal. Agg. 45 C.Y.	
M 1949	A.F.E. 6	Crushed Rock Resurfacing (Spots)			470 C.Y.	
M 1950	A.F.E. 6	Crushed Rock Resurfacing (Spots)	24'		962 Tons	
M 1951	A.F.E. 4	Bit. Surf. Repair	24'		MC3, 1880 Gal. Agg. 102 C.Y.	
M 1952	A.F.E. 6	Crushed Rock Resurfacing	24'		1577 Tons	
M 1953	A.F.E. 604	Bit. Surf. Repair	24'		MC2, 240 Gal. Agg. 15 C.Y.	
	A.F.E. 866	Repair Culvert				
M 1954	A.F.E. 818	Bit. Surf. Repair	24'		MC-3, 3452 Gal. Agg. 260 Tons	
C 1969	7904-18	Grade-Bit Base, Surf.	24'	7"		
	7904-25	Pl. Mix. Bit.	24'	2"		
		Gravel Shoulders	12'			
M 1978	SF	Bit. Overlay Sand Seal	20'	3/4"	Pl. Mix AC 2341 300 T. RC 800 Tack 550 Gal.	
C 1989	7909-01	Grading Bit. Overlay	23'	2"	Spec. 2331	

PLAN



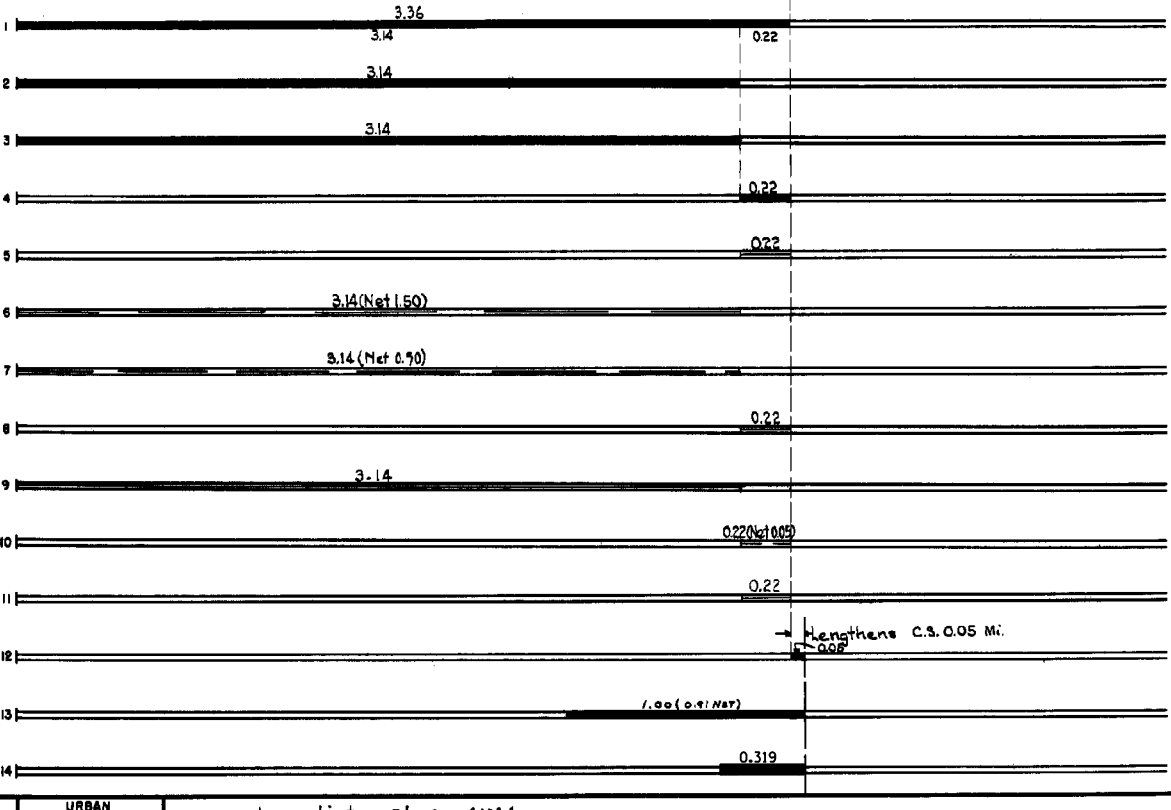

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934		3.36	3.36	0.00	0.00	0.00	3.36	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934
(1) No record of this work. Maint. foreman indicates 1938.
