FORM R.L.-7 REV. 2-40

SHEET 1 OF 3

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8309
TRUNK HIGHWAY 60
COUNTY Watonwan
DISTRICT 7B

LIMITS: E. Jct. T.H.4 in St. James - S. Jct T.H.15



YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
1919	60-16-5	Concrete	VW		City Paving No Record of Constr.	
1919	60-16-1	Concrete	V.W.		City Paving No Record of Constr.	
1920	60-16-1	Concrete	18'	7½"		
		Br. 2844 (1)	18'		30° C.T.G.	
1921	60-16-1	Concrete	18'	7½"		
		Br. 2843 (1)	16'		58° B.S.	
1922	60-16-24	Tile Drain				
		Guard Rail				
1922		Br. 2843	22'		Br. Widening 58° B.S. Maint. Dept.	
		Grading	36'			
1939	8309-01A&B	Br. 5844	30'		50° B.S.	
		Concrete	20'	9.79		
C 1940	8309-04 A.F.E. 6	Seeding			Maint. Dept.	
C 1941	8309-02	Br. 5972			C106D replaces old Br. 2844.	
M 1950	A.F.E. 22	Repair Tile Line				
C 1951	8309-07	Regrading	3842		Old concr. buried or removed	
	8309-08	Concrete	2244	8.97.9	(8.43 Mi. on 6" Sand-Grav.)	
(2)	8309-09	Traffic Signals				
C 1954	A.F.E. 817	Rip Rap			At Br. 5844	
C 1966	SF	Bit. Surf. Repair	22'	1½"	Bit. Mix. 799 Ton	
M 1967	C	Light Bit. Seal	22'		CRS-1 Bit. 1,626 Gal. FA-1 Agg. 48 C.Y.	

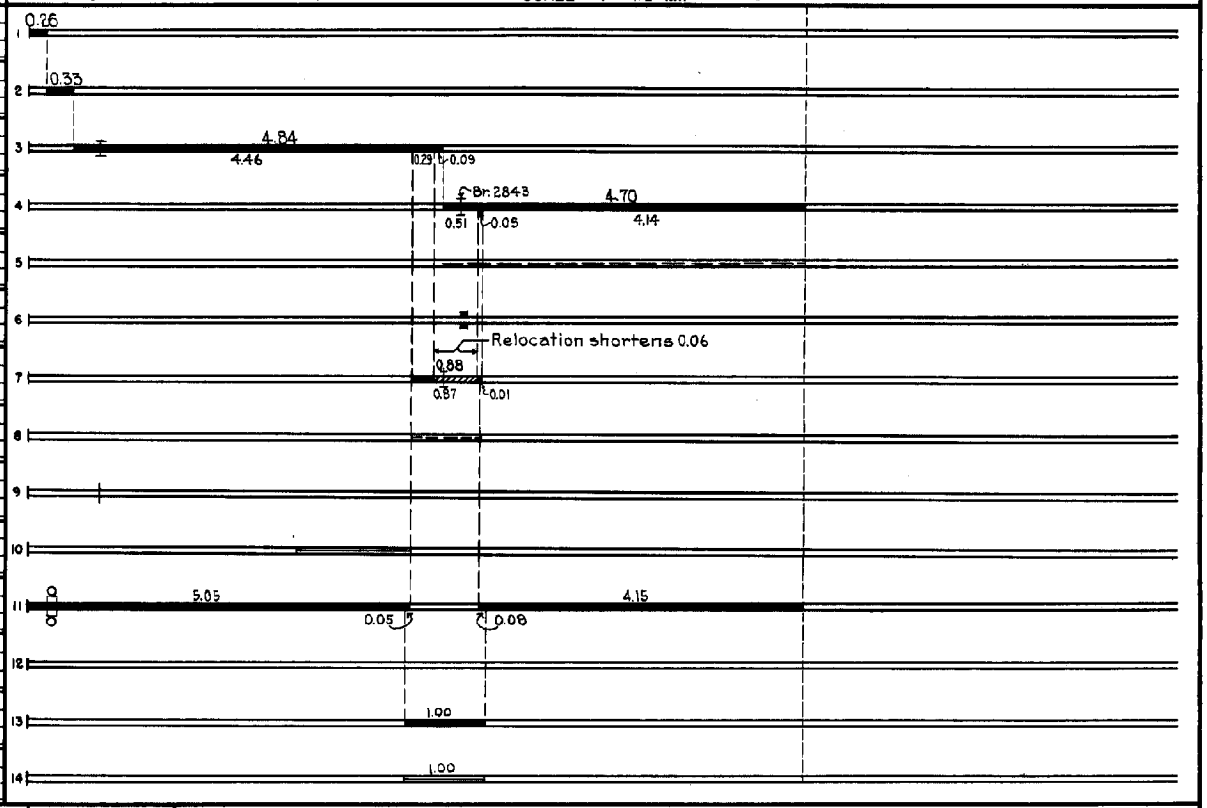

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED ROWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED ROWY. MI.	INCORPORATED BR. MI.	RURAL ROWY. MI.	RURAL BR. MI.	URBAN ROWY. MI.	URBAN BR. MI.
1921	1938	10.13	9.52	0.02	0.59	0.00	9.52	0.02	0.59	0.00
1939	1970	10.07	9.46	0.02	0.55	0.00	9.46	0.02	0.59	0.00
1971	1972	10.07	8.96	0.02	1.09	0.00	8.96	0.02	1.09	0.00
1972		10.07	8.88	0.02	1.17	0.00	8.88	0.02	1.17	0.00

REMARKS: Layout is to scale as of 1921.

(1) Br. 2844 & 2843 in place. (2) Contracts on S.P. 8309-07 & 8309-08 not final but work substantially complete.

Mn/DOT 29450 (4-76)
FORM RL-7

SHEET 2 OF 3

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8309
TRUNK HIGHWAY 60
COUNTY WATONWAN
DISTRICT 78

LIMITS: W. Jct. TH 4, Br 83028 — Jct TH15 at Br 83005

Ref. Pt. 065+00.499 - 077+00.693

YEAR BUILT	PROJECT NO	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C		Grading, Base,			Br 83029, 83030
1976	8309-21	Concrete Surf	24'	9"	2-168' P.P.G.
	FF016-1(39)	Bit. Shoulders	10', 3'	2"	
C		Grading, Base			
1976	8309-25	Concrete Surf	24'	9"	
	FF016-1(44)	Bit. Shoulders			
C					
1976	8303-10	Grading			W.B. Lane Only
	FF015-1(46)				
C		Grading, Base,			Br 83005
1976	8303-05	Concrete Surf	24'	9"	329' PPG - OH
	FF016-1(47)	Bit Shoulders	10', 3'		
C					Br 83025 - 342' Pre B.S.
1978	8309-20	Grading			Br 83026 - 312' Pre B.S.
	FF016-1(48)				Br 83027 - 345' Pre B.S.
C					
1979	8309-24	Concrete Surf	24'	9"	
	FF016-1(50)	Bit. Shoulders	3', 10'		
C					Rest Area Building
1980	8309-17	St. James Rest Area			Site Developments
	SF				Disposal Site & Lighting
C					
1985	SF	Constr. Exp. Joints			Contract No. 4136
M					
1985	SF	Wedge Paving	1"		Sp. 2331 758 Tons
					Included with CS 8308
M					
1987	SF	Wedge Paving			
C				4"	Spec. 2331
1988	8309-39	Bit. Overlay	24'	1"	Spec. 2361
M					
1989	M4330	Joint Repair			
M					
1989	M4331	Joint Repair			
M					
1990	M4374	Crack Sealing			



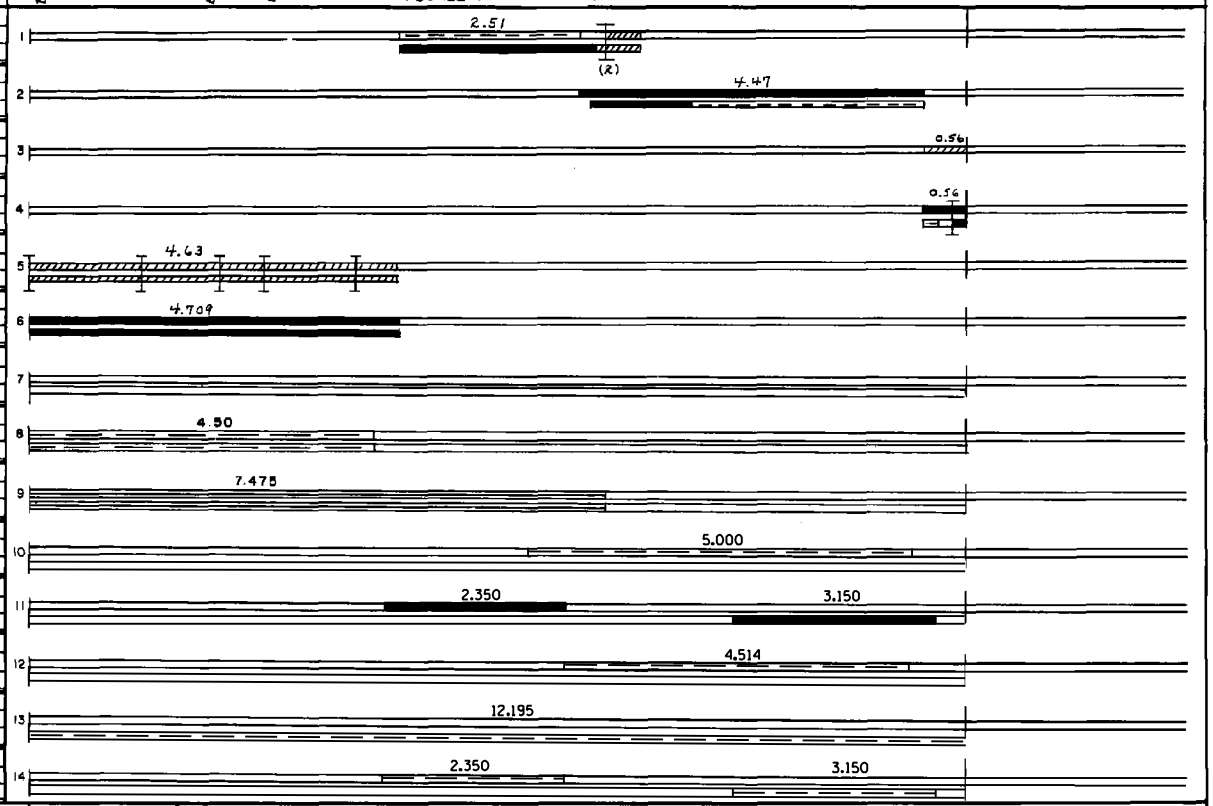

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

FORM RL-7

SHEET 3 OF 3

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8309
TRUNK HIGHWAY 60
COUNTY Watonwan
DISTRICT 7B

LIMITS: W. Jct. T.H. 4 - Jct. T.H. 15

Ref. Pt. 065+00.499 - 084+00.096



YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
M					
1991	M4452	Joint Repair			
M					
1991	M4486	Edge Drains			
M					
1992	M4557	Joint Repair			
M					
1992	M4560	Bit. Shouldering			
M					
1993	M93129	Edge Drains			
M					
1994	M94229	Bit. Shouldering			
C		Milling	24'	5"	
1998	8309-41	Bit. Overlay	24'	2"-3"	Spec. 2350
M		Major			
2001	8827-15	Crack Repair		var	
M					
2004	8305-30	Concrete Joint Repair	24'	var	
2013	8827-202	Aggregate Seal Coat			Type F2
		Approach Work	Var.	9"	Non-reinforced Conc.
2014	8309-47	Br. 83029, 83030			

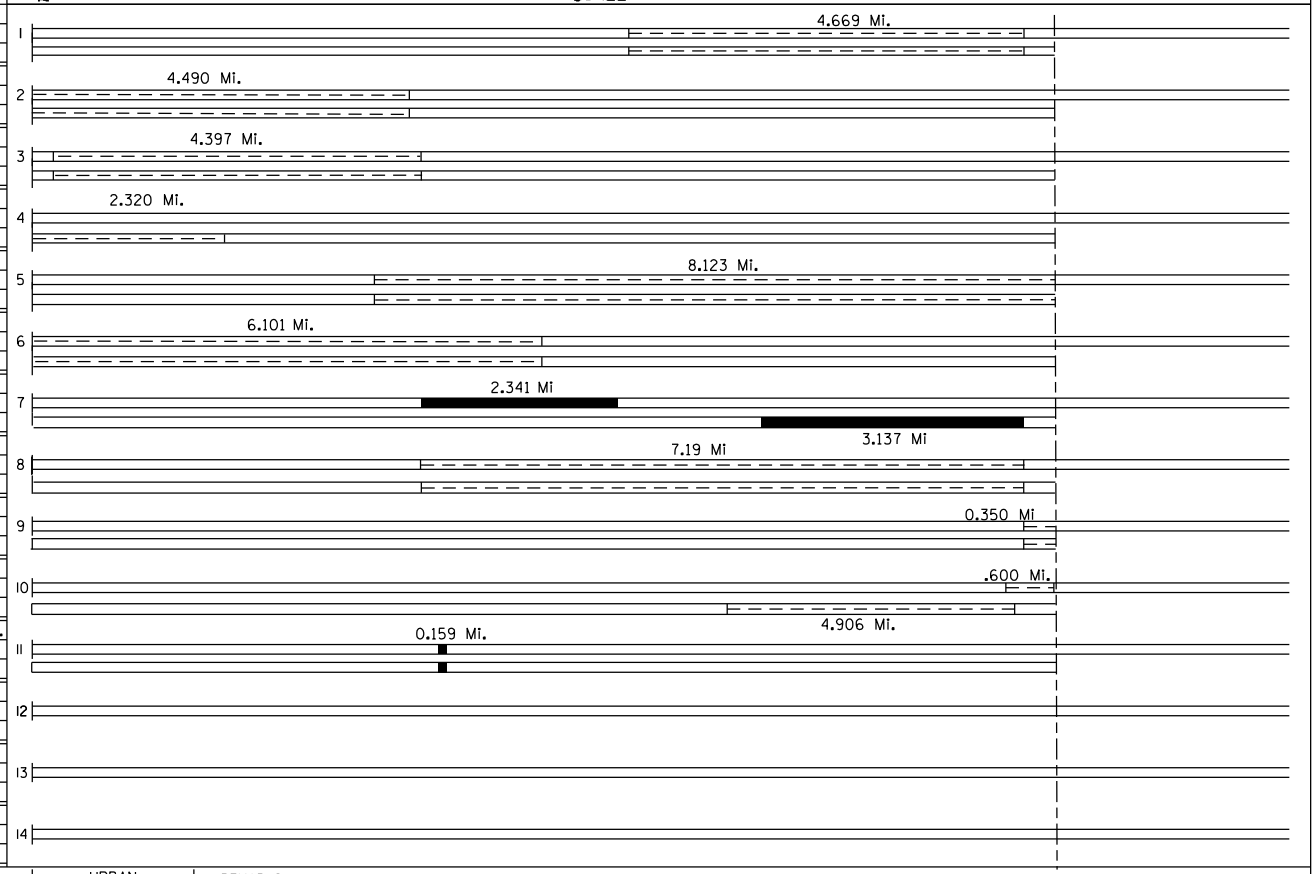

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
