PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4105
TRUNK HIGHWAY 23
COUNTY Lincoln
DISTRICT 8B

LIMITS: So. Co. Line ~ E. Co. Line

Ref. Pt. 048+00.814 - 050+00.004

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
					No Record of Const.	
		Gravel	32'	2"		
					Added in 1934	
		Grading	32'			
1934	39-88-21-18	Gravel	32'	1½"	1290 Tons/Mi.	
C		Bit. Surf. Treat.	26'	¾"		
1941	4105-01	Stab. Sand-Grav. Base	32'	5½"	4" Sand - 1½" Gravel	
M					SC-3 & RC-3, 3366 G/Mi	
1945	A.F.E. 5	Bit. Seal Coat			Grav. 119 C.Y./Mi.	
					Maint. Div.	
M		Spot Treat.			MC-3, 2150 Gal.	
1947	A.F.E. 4	Bit. Surf. Repair			Agg. 126 Tons	
M		Spot Treat.			MC-3, 3088 Gal.	
1948	A.F.E. 4	Bit. Surf. Repair	24'		Agg. 206 Tons	
C		Gravel Base	32'	4"	added thickness	
1950	4105-03	Plant Mix Bit.	24'	1½"		
		Spot Subgr. Corr.				
M					RS2, 2072 Gal.	
1954	A.F.E. 605	Light Bit. Seal	24'		Agg. 74 C.Y.	
M						
1961		Light Bit. Seal	25'		RS-2, 2012 Gal.	
					Agg. 65 C.Y.	
C		Grading	65			
1973	4105-06	Gravel & Bit. base		18 &	1½"	
		Plant Mix Bit	24	3		
M						
1984	SF	Bit. Overlay	24'	1½"	Sp. 2331 166 Ton	
					Contract No. 4100	
C						
1985	4105-07	Bit. Surfacing	24'	3½"		
		Bit. Shoulders	10'	Var.		
M						
1991	M4442	Bit. Sealing				
S						
2002	4105-08	Bit. Mill & Cold recycle.	24'	6"	Spec 2360	

PLAN

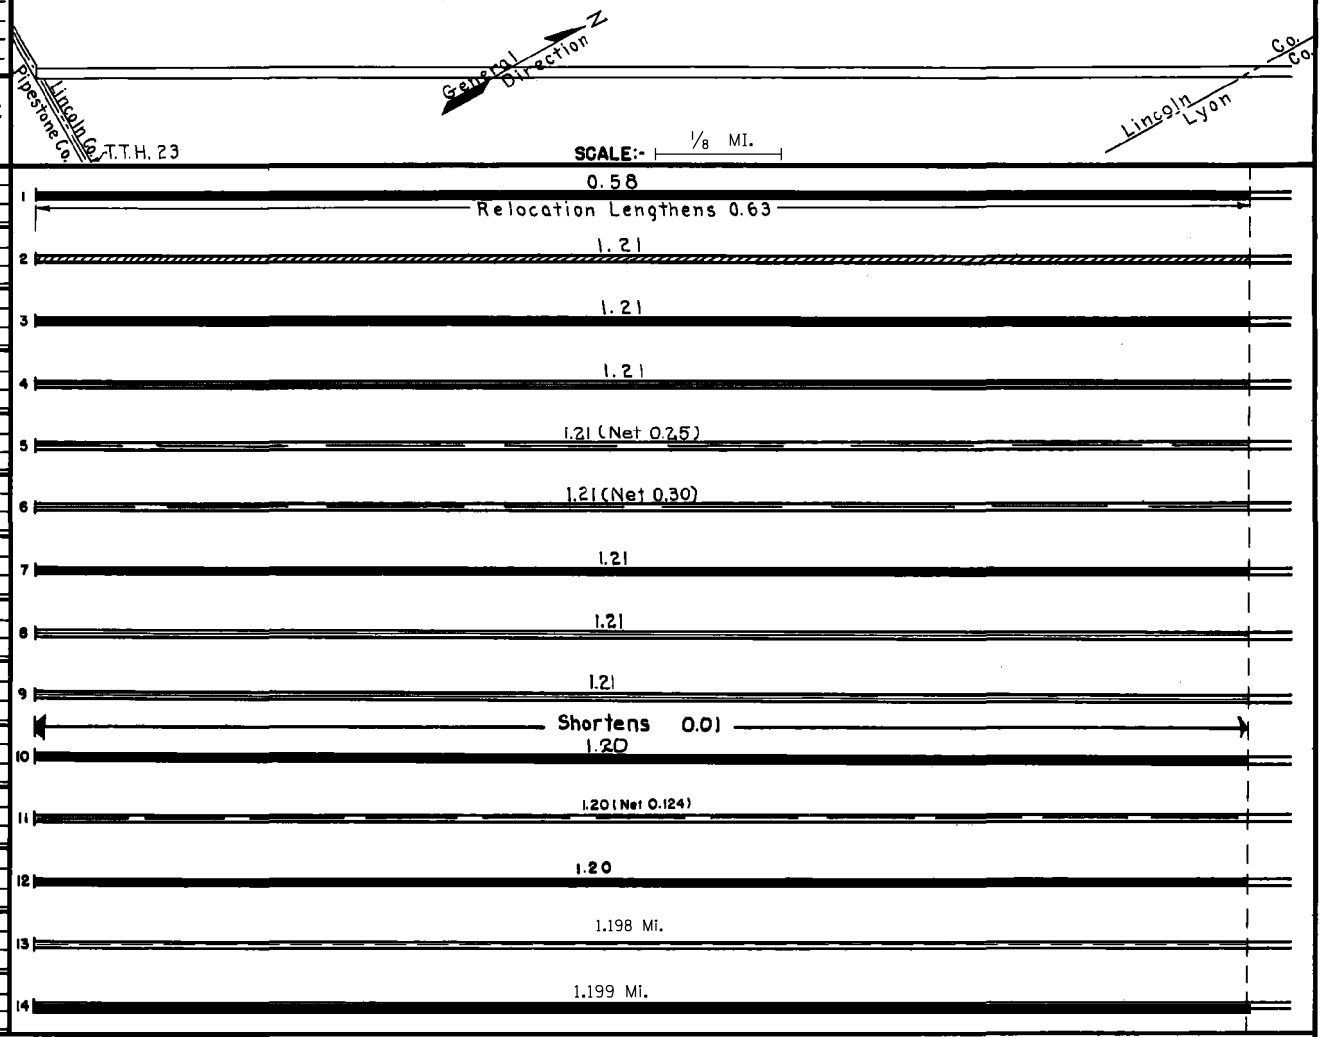

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1934	0.58	0.58	0.00	0.00	0.00	0.58	0.00	0.00	0.00
1934	1973	1.21	1.21	0.00	0.00	0.00	1.21	0.00	0.00	0.00
1973		1.20	1.20	0.00	0.00	0.00	1.20	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4105
TRUNK HIGHWAY 23
COUNTY Lincoln
DISTRICT 8B

LIMITS: Pipestone-Lincoln Co line - Lincoln-Lyon Co line

Ref. Pt. 048+00.814 - 050+00.004

YEAR BUILT	PROJECT No	DESCRIPTION			
		TYPE	WIDTH	THICK NESS	REMARKS
2013	8828-143	Agg. Seal Fog Seal			FA-2

PLAN



1.199 Mi.

1
2
3
4
5
6
7
8
9
10
11
12
13
14

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
