FORM R.L.-7 REV. 3-58

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

SHEET 1 OF 1

CONTROL SECTION 6941
TRUNK HIGHWAY 39
COUNTY St Louis
DISTRICT 1A1

LIMITS: (In Duluth) E. Jct. T.H. 23 – W. End of Oliver Bridge

Ref. Pt. 000+00.000 - 000+00.900



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
		Br. 6540			T.P.G. over N.P.R.Ry.
		Bit. Surface	28'		297-8'
					Year built unknown
					This highway added
1943		Mixed Bit.	27'	1½"	by legislature in
					1943. Order 15743
C					
1950	AFE 18	Bit. Resurface	27'	1½"	
		Gravel Shoulders	4'		Rt. & Lt.
M					
2002	6941-07	Mill & Bit. Overlay	24	1½"	Spec. 2350
C		Bit. Surfacing	var.	4.5"	
2019	6941-34	Bit Milling	24'	3"	6" Agg. base C-6
		Bit. Overlay - rural	24'	3"	

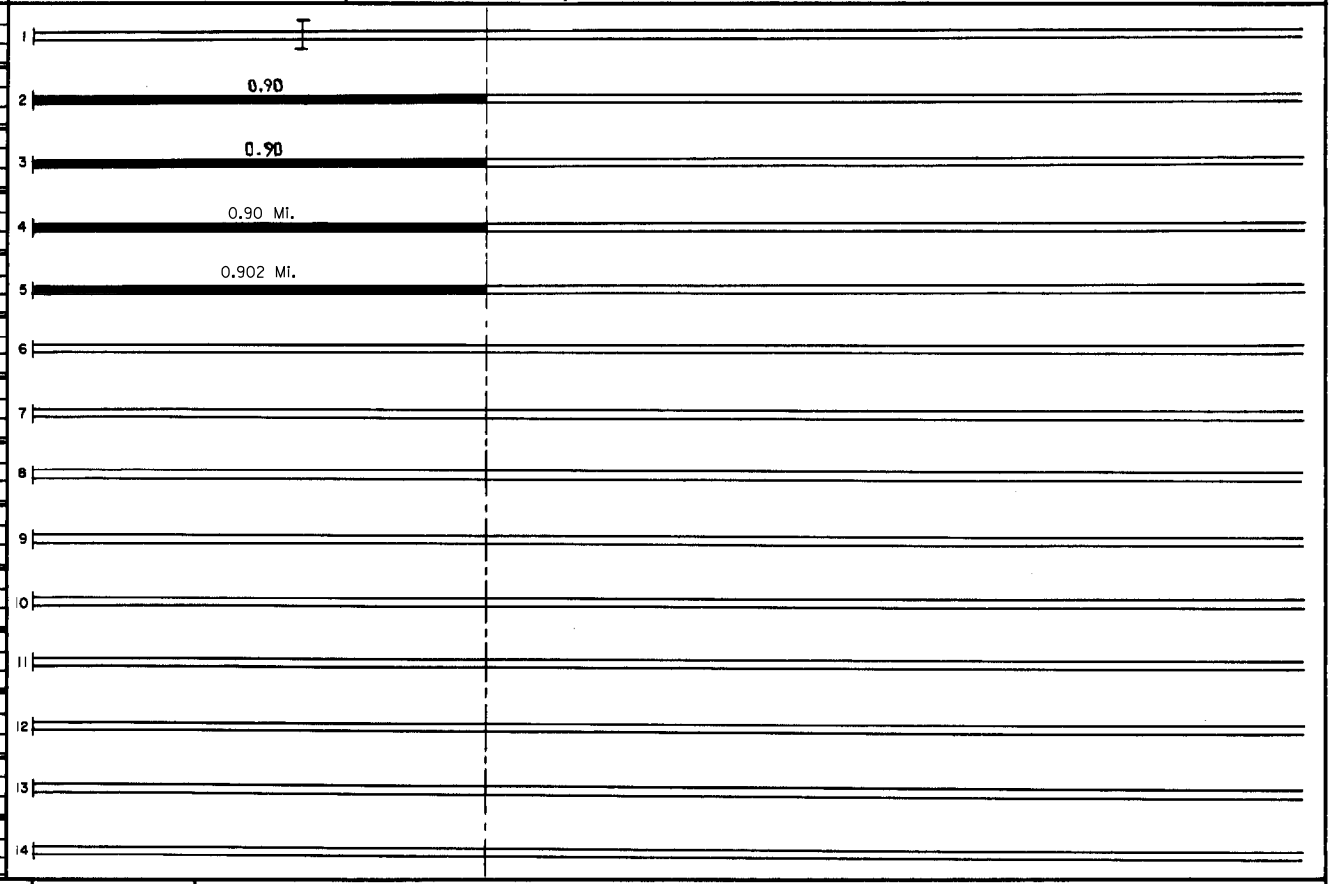

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1943		0.90	0.00	0.00	0.84	0.06	0.00	0.00	0.84	0.06

REMARKS: Layout is to scale as of 1969.
