FORM R.L.-7 REV. 2-40

SHEET 1 OF 2

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8410
TRUNK HIGHWAY 210
COUNTY Wilkin
DISTRICT 4A

LIMITS: Bridge over Bois des Sioux River at Breckenridge.

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Br. ?	18'		No Record of Constr. 1-20 R.S. 1-100 Steel Truss & 3-30 R.S.	
1930	3=3-59	Br. 4720	40'		172' C.O.G.	
C 1952	8410-01	Plant Mix Bit. Re-Surf. on Br. Floor	40'	2"		
M 1962		Light Bit. Seal	40'		RS-2, 28 Gal. Agg. 5 C.Y.	

PLAN



SCALE:- 1" = 0.02 MI.

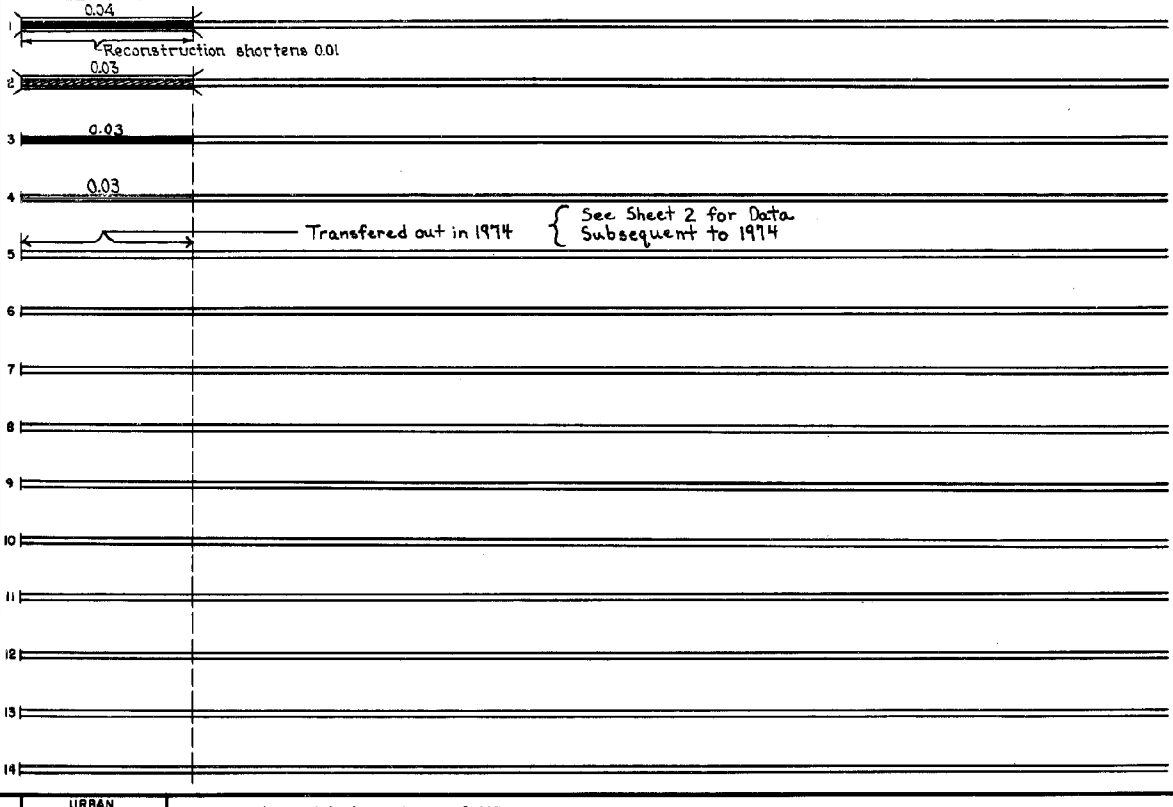

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1921	1929	0.04	0.00	0.00	0.00	0.04	0.00	0.00	0.00	0.04
1930		0.03	0.00	0.00	0.00	0.03	0.00	0.00	0.00	0.03

REMARKS: Layout is to scale as of 1930.

Interstate Bridge.

4-75

FORM R.L.-7 REV 7-74

SHEET 2 OF 2

PREPARED BY
TRANSPORTATION PLANNING AND PROGRAMMING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8410
TRUNK HIGHWAY 210
COUNTY Wilkin
DISTRICT 4A

LIMITS: ½ Bridge over Red River of the North at Breckenridge

Ref. Pt. 000+00.000 - 000+00.033

YEAR BUILT	PROJECT NO	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C 1974	84002	Br 84002	44'		350' B.S.

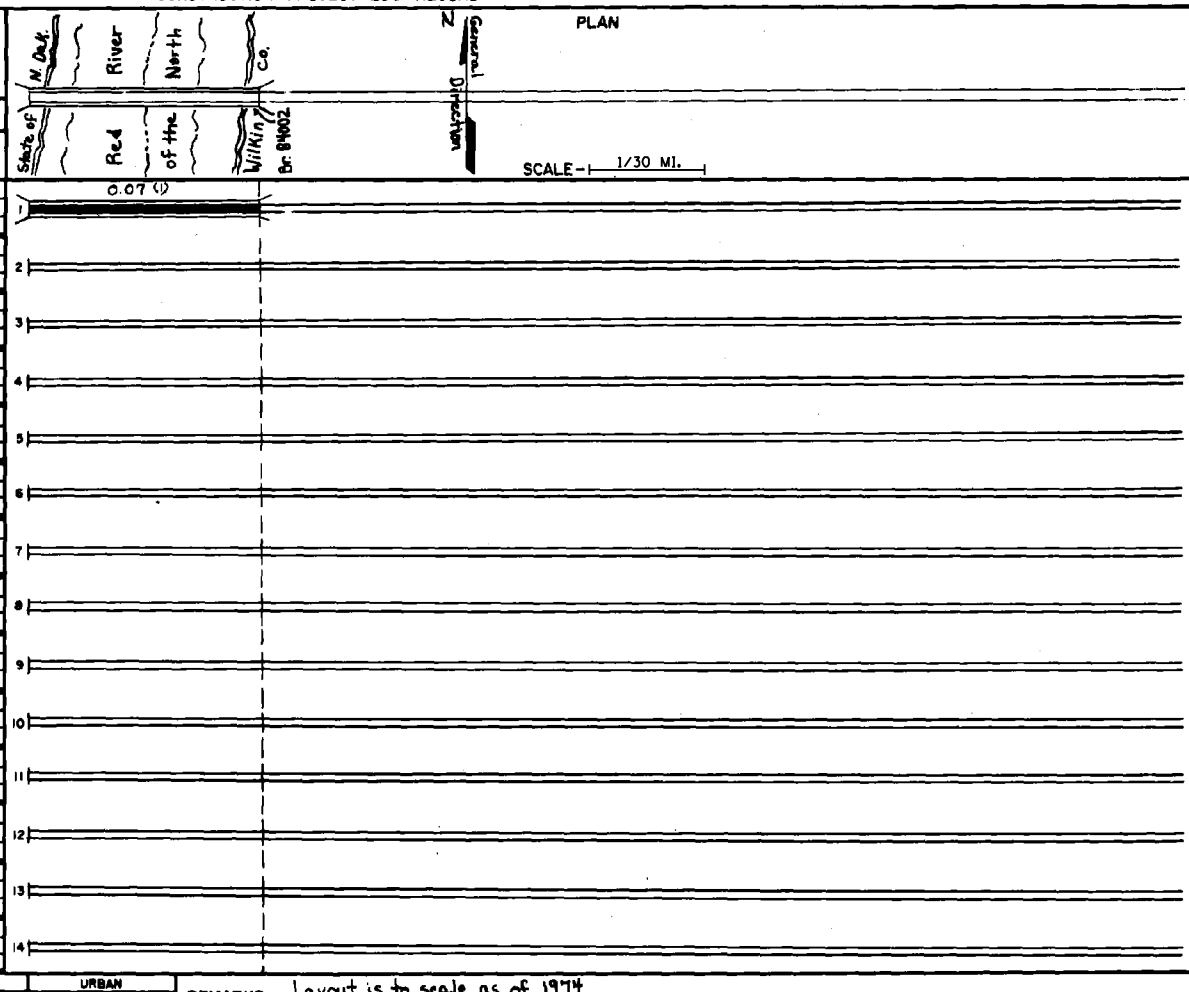

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1974		0.03		0.03						

REMARKS: Layout is to scale as of 1974
Interstate Bridge
(1) ½ Bridge used for Minnesota Mileage
