FORM RL-7

SHEET 1 OF 1

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0214
TRUNK HIGHWAY 10
COUNTY Anoka
DISTRICT Metro

LIMITS: E. Jct. MNTH-47 - Anoka/Ramsey Co. Line
Ref. Pt. 232+00.415 - 235+00.638



YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C					
1988	0214-07	Grading, Bit. Surfacing	48′	7"	Spec. 2331
				1"	Spec. 2361
C		Br. 02045, 02046			Over TH. 65
1993	0214-10	Br. 02047			Over Airport RD.
		Br. 02048			Over Co. RD. J
C		Grading	62′		
1993	0214-10	Surfacing	Var.	9"	Spec. 2331, 2341
		Agg. Base	56′	2"	Class 5
M					
1995	SF	Bit. Milling	24′	1½"	
		Bit. Overlay	24′	1½"-3"	
C		Grading	50′		
1997	0214-11	Agg. Base	48′	6"	Class 6
		Bit. Surfacing	24′	Var.	Spec. 2331, 2347, 2361
C		Br. 02035			Over TH. 47 N.B
1999	0214-12	Br. 02037			Over TH. 610 & Univ.
		Br. 02044			Under Ped Walkway
C		Grading			Wearing (31WEA50000)
1999	0214-12	Surfacing	36′	9"	Binder (47BIB50070)
		Agg. Base	56′	6"	Class 6
C					
1999	0214-13	Br. Const. # 02043			Under Polk St. NE
C					
1999	0214-13	Grading, Surfacing	48′	3-4"	SP-9.5
					SP-12.5
S		Milling	var.	4"	
2010	0214-41	Bit. Overlay	var.	4"	Spec. 2360
S		Grading			
2015	0214-44	Tension Cable			
		Guardrail			Mi. based on P10 EB
S					
2015	0214-46	UTBWC Microsurfacing		¾"	Spec. 2353
	8825-536	Seal coat & Fog seal			Spec. 2354 Spec. 2356

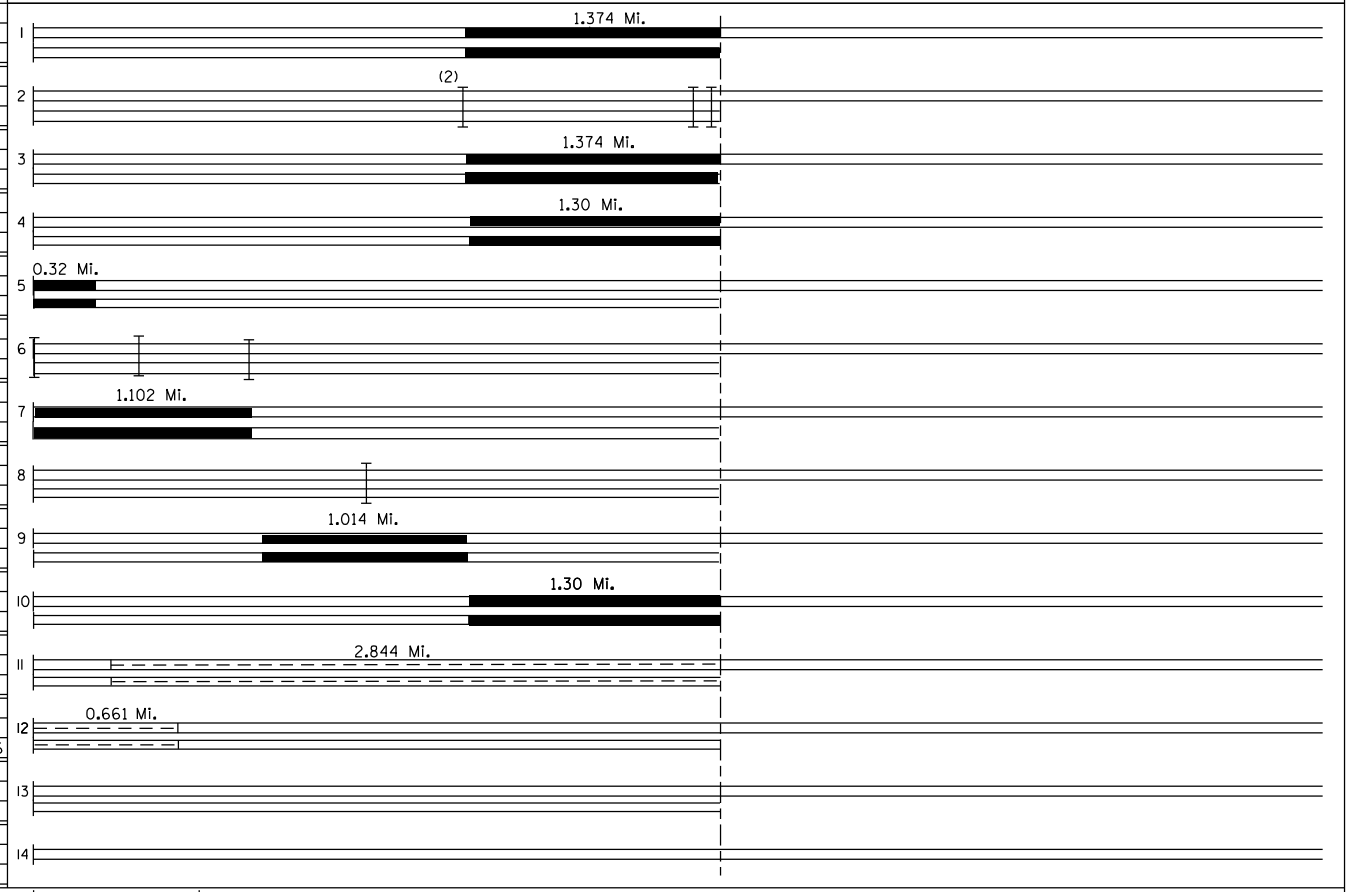

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
