FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2789
TRUNK HIGHWAY 394
COUNTY Hennepin
DISTRICT Metro

LIMITS: Jct I-494 in Minnetonka - Washington Ave in Minneapolis

Ref. Pt. 000+00.000 - 009+00.375



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C 1983	2789-25	Grading & Surfacing			Temp. Conn. on Hawthorne Ave
C 1984	2789-33	Grading & Surfacing			On Laurel Ave from Penn Ave to Louisiana Ave
C 1984	2789-35	Pond Excavation			At TH 100 & TH 55
C 1985	2789-13	Br 27701 Br 27702 Br 27703			
C 1985	2789-28	Electric Lighting			On 11th St, 12th St & Linden Ave
C 1985	2789-41	Interim Grading, Bit. Surfacing		1 ½" 6 ½"	Spec. 2341 Spec. 2331
C 1986	2789-14	Grading, Conc. Surfacing	36'	9"	Br 27829 Br 27830
C 1986	2789-19	Br 27756 Br 27758			
C 1986	2789-27	Traffic Control Signal System			On 5th St at 2nd Ave N & at 3rd Ave N
C 1986	2789-36	Storm Sewer			On Laurel Ave from Hampshire Ave to Glenwood Ave
C 1986	2789-45	Br 27706 Br 95893 (5th Street Parking Garage)			
C 1986	2789-46	Electric Lighting System			On 5th St from 2nd Ave N to 3rd Ave N
C 1987	2789-16	Grading, Conc. Surfacing Br 27738, 27739, 27740	36'	1 ½" 10 ½"	Br 27741 Spec. 2361 Br 27742 Spec. 2331 Br 27743
C 1987	2789-42	Traffic Signs & Devices			

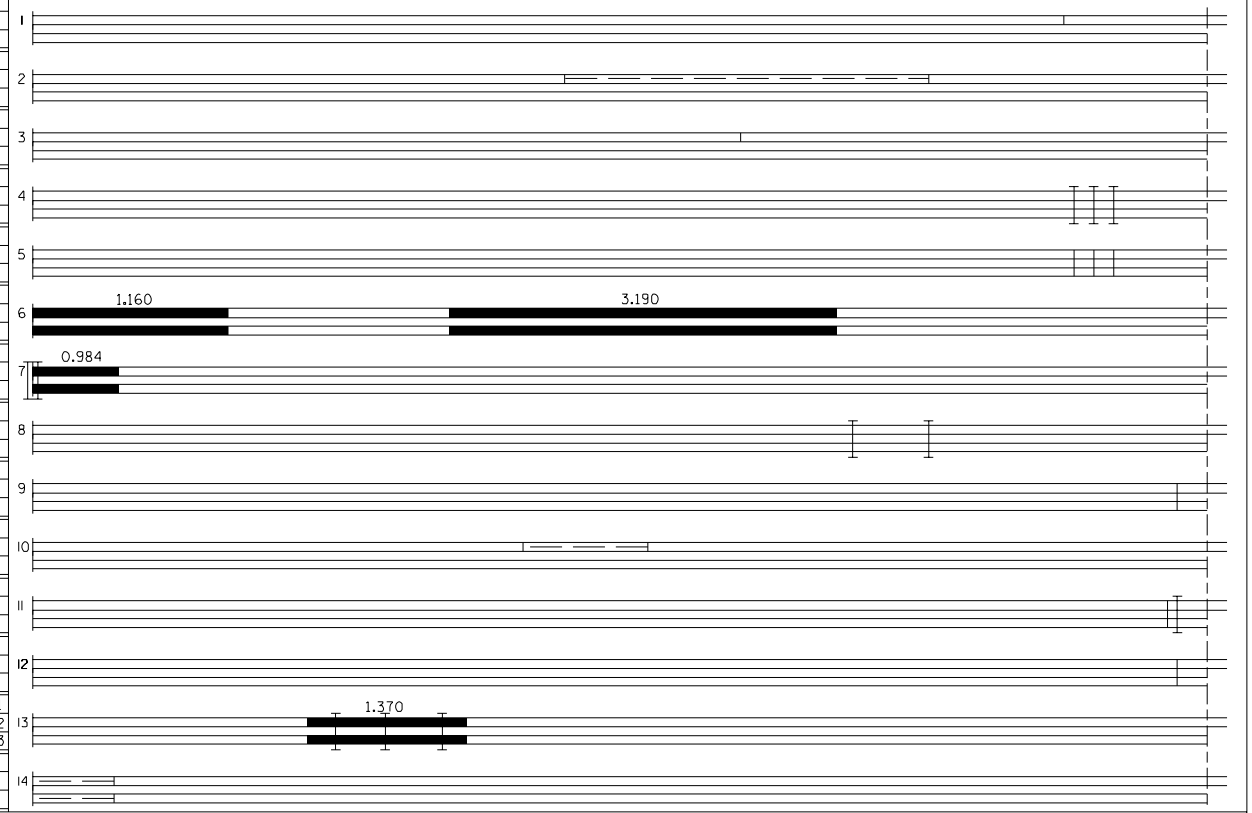

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2789
TRUNK HIGHWAY 394
COUNTY Hennepin
DISTRICT Metro

LIMITS: Jct I-494 in Minnetonka - Washington Ave in Minneapolis

Ref. Pt. 000+00.000 - 009+00.375



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C 1987	2789-48	Grading, Conc. Surfacing	36'	10"	Br 27770 Br 27776
C 1987	2789-58	Detached Frontage Rd			
C 1987	2789-60	Electric Lighting System			
C 1988	2789-15	Grading, Bit. Surfacing Br 27117	36'	1" 3" 7"	Spec. 2361 Br 27731 Spec. 2341 Br 27736 Spec. 2331 Br 27737
C 1988	2789-17	Grading, Bit. Surfacing Br 27710, 27711, 27744	36'	1" 3" 7½"	Spec. 2361 Br 27745 Spec. 2341 Br 27746 Spec. 2331 Br 27747
C 1988	2789-20	Grading, Conc. Surfacing Br 27757	39'	10"	
C 1988	2789-52	Storm Sewer			On Glenwood Ave from Soo Line RR to Turners X-road
C 1988	2789-54	Transit Station			at Plymouth Road
C 1988	2789-56	Electric Lighting System			
C 1988	2789-59	Traffic Signs & Devices			
C 1988	2789-62	Electric Lighting System			
C 1988	2789-63	Br 27704, 27730 Br 95892 (7th Street Parking Garage)			
C 1988	2789-66	Traffic Signs & Devices			
C 1988	2789-70	Traffic Signs & Devices			

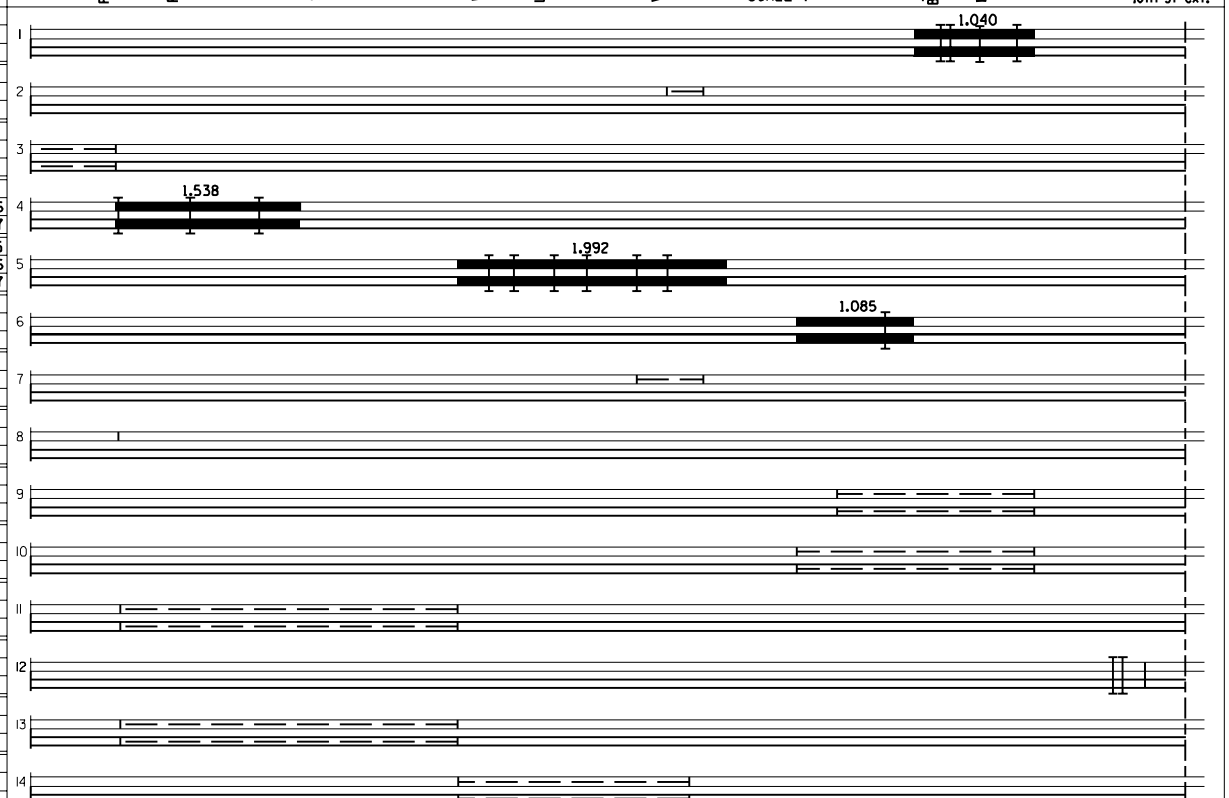

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2789
TRUNK HIGHWAY 394
COUNTY Hennepin
DISTRICT Metro

LIMITS: Jct I-494 in Minnetonka - Washington Ave in Minneapolis

Ref. Pt. 000+00.000 - 009+00.375

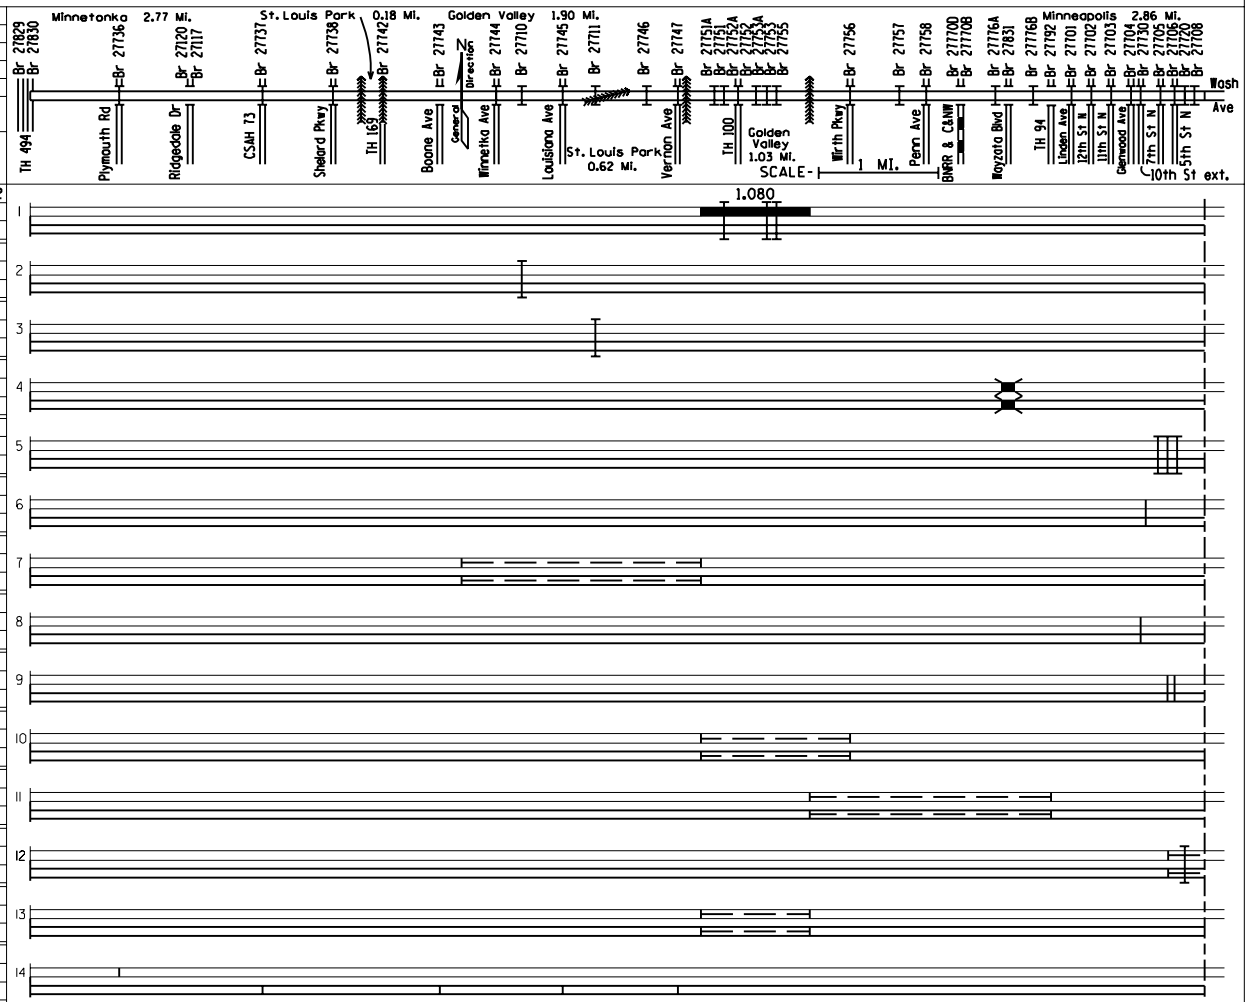

YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C		Grading, Conc. Surfacing			Br 27790,92,99129,31,32
1989	2789-18	Br 27748,49,50,51,52,53	36'	4"	Spec. 2361
		Br 27754,55,86,87,88,89		8½"	Spec. 2341
C					
1989	2789-27710	Br 27710			
C					
1989	2789-27711	Br 27711			
C					
1989	2789-27831A	Redeck Br 27831			
C		Br 27705			
1989	2789-64	Br 27716			
		Br 27732			
C					
1989	2789-67	Grading & Surfacing			On 1st Ave N,
					On 9th St N
C					
1989	2789-68	Traffic Signs			
		& Devices			
C					
1989	2789-72	Grading & Surfacing			On 10th St N
C					On 2nd Ave N,
1989	2789-73	Grading & Surfacing			On 6th St N,
		On 1st Ave N,			On 7th St N
C					
1989	2789-74	Electric Lighting			
		Sytem			
C					
1990	2789-43	Traffic Management			
		System			
C		Storm Sewer,			
1990	2789-65	Retaining Walls			
		Br 27720			
C					
1990	2789-69	Traffic Signs			
		& Devices			
C		Transit Facilities			At General Mills Blvd,
1990	2789-78	At Plymouth Rd,			At Louisiana Ave,
		At CSAH 73,			At Vernon Ave

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2789
TRUNK HIGHWAY 394
COUNTY Hennepin
DISTRICT Metro

LIMITS: Jct I-494 in Minnetonka - Washington Ave in Minneapolis

Ref. Pt. 000+00.000 - 009+00.375



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICK NESS	REMARKS
C 1990	2789-86	Storm Sewer, Retaining Wall			Br 27708, 27733 Br 95894 (4th Street Parking Garage)
C 1990	2789-89	Traffic Management System			
C 1990	2789-90	Landscaping			
C 1991	2789-12	Grading, Conc. Surfacing	48'	9"	
C 1991	2789-85	Br 27798			
C 1991	2789-87	Electric Lighting System			
C 1991	2789-88	Traffic Signs & Devices			
C 1991	2789-91	Landscaping			
C 1992	2789-37	Traffic Control Signal System			On city streets from Hawthorne Ave/12th St N to 2nd Ave/6th St N
C 1992	2789-44	Traffic Management System			
C 1992	2789-93	Landscaping			
C 1993	2789-98	Traffic Management System			
C 1993	2789-99	Traffic Management System			
C 1993	2789-103	Park and Ride			at Louisiana Ave

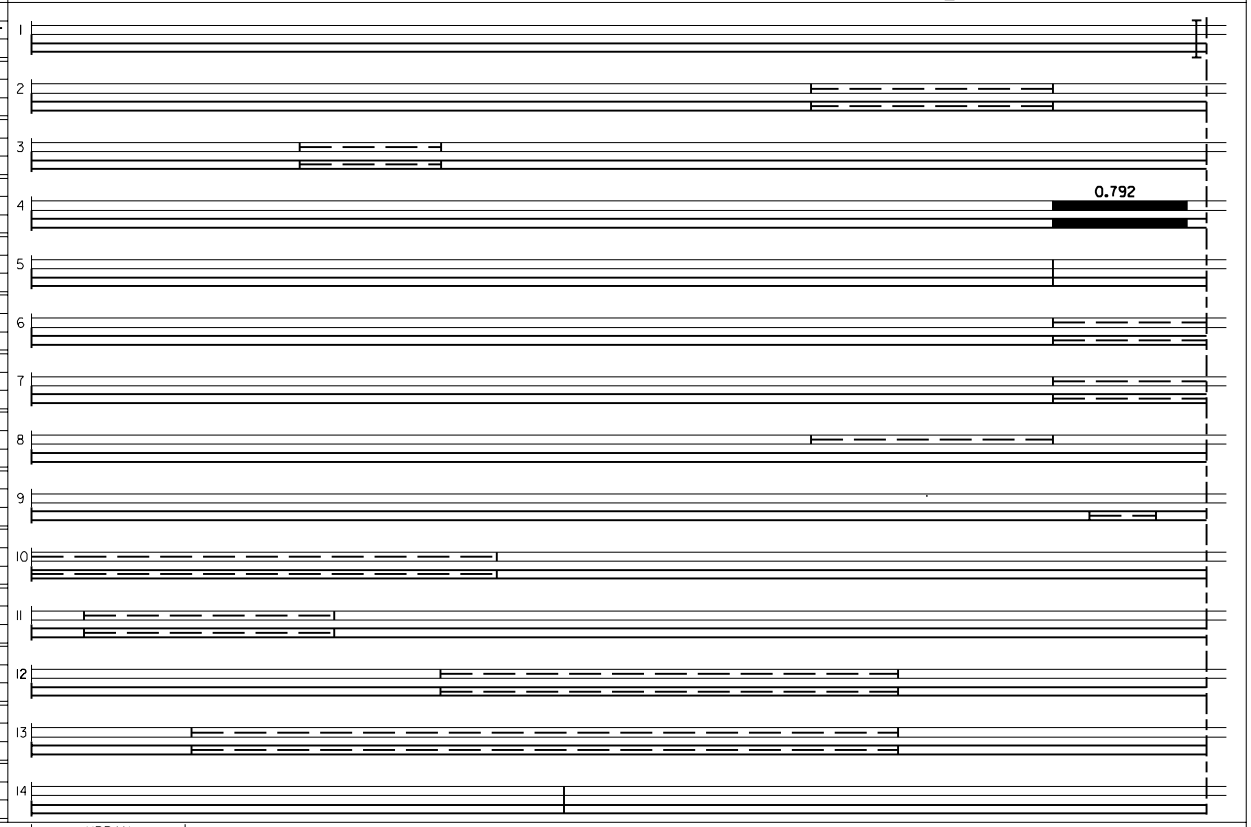

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2789
TRUNK HIGHWAY 394
COUNTY Hennepin
DISTRICT Metro

LIMITS: Jct I-494 in Minnetonka - Washington Ave in Minneapolis

Ref. Pt. 000+00.000 - 009+00.375



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C		Grading & Surfacing			
1994	2789-105	of HOV bypass			WB I-394 to NB TH-169
		ramp meters			
C					
1996	2789-108	Bit. Overlay	40'	1¾"	Spec. 2361
		Noise Walls			
C					
1998	2789-110	HOV ramp			T.H 169 to EB T.H 394
S		Milling &	36'	2"	EB & WB USTH 394
2004	2789-120	Bituminous Overlay	36'	2"	Spec. 2356 WB
					EB
S		Grading			WB to I494
2013	2789-133	Bit. Surfacing	var.	NB	& SB Exit ramps WB
		shldr work			
S				Frontage rd/Minntonka	
2013	2789-141	Grading & Bit. Surf.		Muni.	agreemt 04650 WB
		Exit ramp TH-394			
S					
2015	2789-152	UTBWC MicroSurfacing		¾"	Spec. 2353
	8825-536	Seal coat & Fog seal			Spec.2354, Spec.2356
S		Grading, Bit.&Conc. Mill		N &	S Frontage rds
2015	2789-136	CPR, Conc. Grinding,			
		Bit. Surf.			Redeck Br 27799L EB

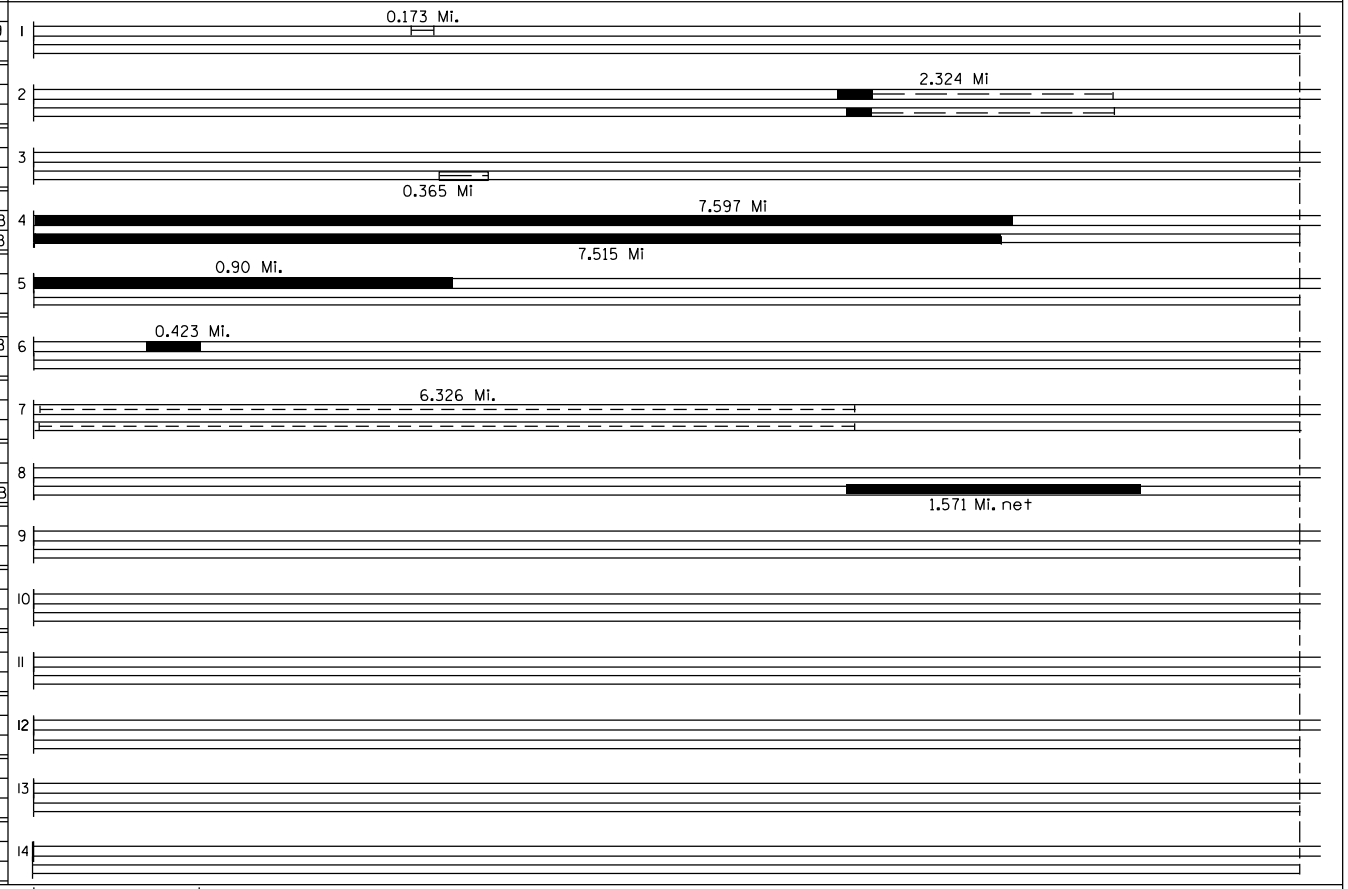

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
