FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3511
TRUNK HIGHWAY 11
COUNTY Kittson
DISTRICT 2B

LIMITS: Bridge over Red River at Robbin (Not Inc.)

Ref. Pt. 000+00.000 - 000+00.099

PLAN



SCALE:- 0.10 MI.

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
(1)		Br. 142	17'		No Record of Constr. 850 Steel Truss & Timber Appr.	
C. 1939		Br. 142 762' L.T., H.T. & W.P.T.			Remove Approx. 80' of W.P.T. Br. Crew Nº 3.	
C. 1954 (2)	3511-02	Br. 6690	28'		2-254' B.S. & 550' H.T.	
M. 1960	S.F.	BR #6690 Raise E. End of Br. Exc. under E. Ba. Apr.			1350 C.Y. Exc.	

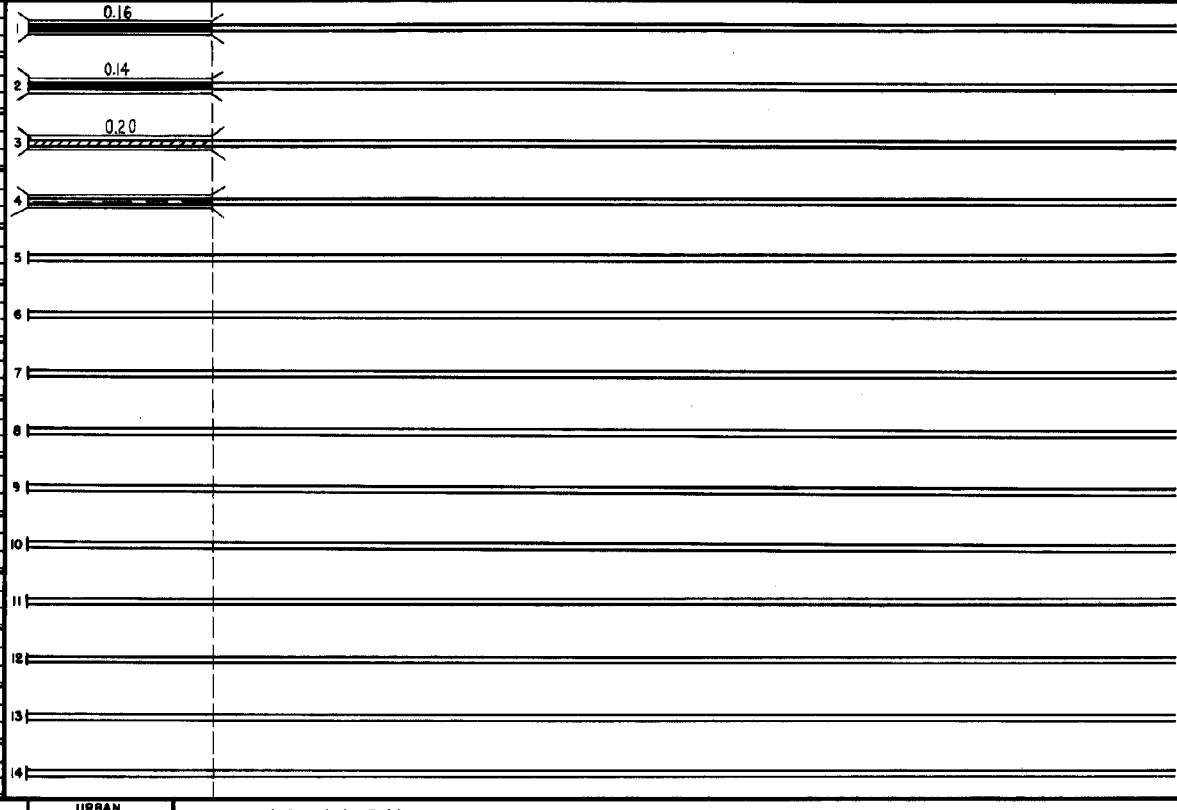

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1938	0.16	0.00	0.16	0.00	0.00	0.00	0.16	0.00	0.00
1939	1953	0.14	0.00	0.14	0.00	0.00	0.00	0.14	0.00	0.00
1954		0.20	0.00	0.20	0.00	0.00	0.00	0.20	0.00	0.00

REMARKS: Interstate Bridge

(1) Entered system in 1934 (2) Contract not final but contract substantially complete
