Mn/DOT 25480 (4-79)
FORM RL-7.

SHEET 1 OF 1

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG. RECORD

CONTROL SECTION 5212
TRUNK HIGHWAY 169
COUNTY NICOLLET - BLUE E.
DISTRICT 7A

LIMITS: N. END BR 9098 — JCT TH 14 EB (BR 07028)
Ref. Pt. 053+00.385 - 055+00.659

PLAN



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C					
1977	5203-66	Bit. Surfacing	Var.	3/4"	NBL only
	U005-1(48)	Ramp Widening, Lighting			
C		Grading.	30'	9"	
1976	5211-34,35	Bit. Surfacing	24'	2 1/4"	Applies NBL only
	U-RF-005-1(38)	Bit. Shoulders	10', 3'	2"	Both Lakes
M		Bit. Overlay at	12'	2"	212 Ton
1979	SF	Belgrade Av. Intrm-			
		change Br 9244	24'	1/2"	42 Ton
C					
1980	5212-07	Bituminous Overlay	24'	1 3/4"	
	FMS 0009(9)	Pavement Marking			
C					
1981	5212-06	Guardrail Improvement			
	HES 0009(47)				
M					
1983	SF	Seal Bit. Overlay	35'	1/2"	
		Grading		2"	Spec. 2331
1986	5212-13	Bit. Surfacing	24'	1 1/2"	Spec. 2341
C				3"	Spec. 2341
1989	5212-17	Bit. Overlay	24'	1 1/2"	Spec. 2361
C				7 1/2"	Spec. 2341
1992	5212-15	Grading	24'	4"	Spec. 2361
		Bit. Surfacing			
S					
2001	5212-23	NB buried with 19"	24'	11"	Spec. 2350
		Agg and 11" Bit.			
2003	5212-24	Mill & Bit Overlay	24'	4"	Spec 2360
2006	8827-68	Route & Seal			
		Grading/Agg. Base	Var.	6"	Class 6
2012	5212-26	Bit. Accel. Lane	14'	6"	Spec. 2360
		Bit. Turn Lane	12'	6"	Spec. 2360 NB
					(0.226 mi. on old
2015	5212-27	Conc. Pavement	var.	var.	MNTH-60 align.)
		Br. 07042 & 52009		Ramp	work on TH 169 NB

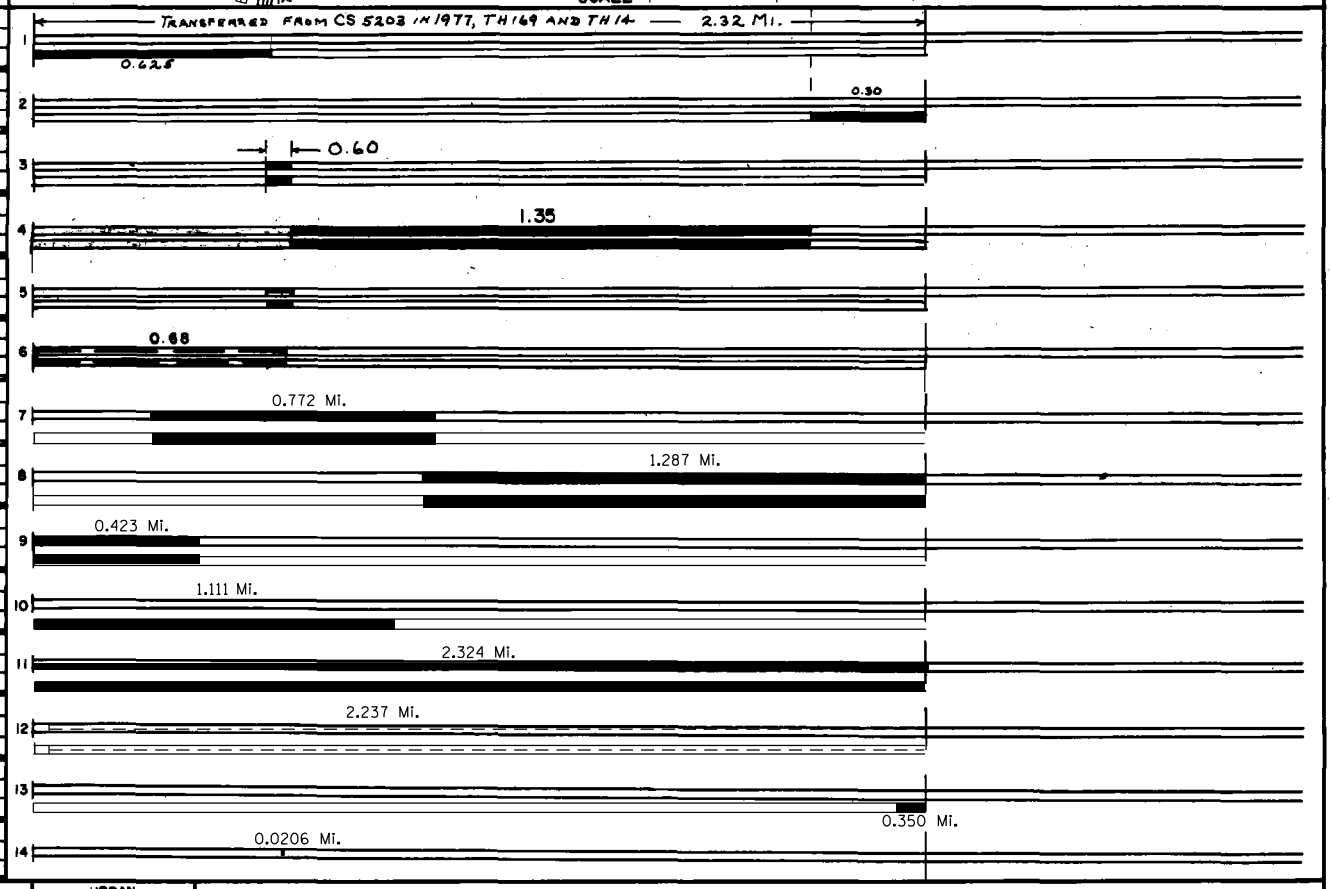

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
