FORM R.L.-7 REV. 3-58

SHEET 1 OF 1

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

# STATE OF MINNESOTA
## DEPARTMENT OF HIGHWAYS
## ROAD LIFE STUDIES
## CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6243
TRUNK HIGHWAY 10
COUNTY Ramsey
MAINTENANCE DISTRICT Metro

LIMITS: No. Co. Line - Jct. T.H. 35W

Ref. Pts. 235+00.643 - 237+00.040

| YEAR BUILT | PROJECT NO | DESCRIPTION: TYPE | WIDTH | THICKNESS | REMARKS |
|---|---|---|---|---|---|
| C | 6243-05 | Grade, Gravel Base | | | Divided Highway |
| 1972 | 6243-66 | Bit. Base* Asph. Conc** | 2@24 | 3½" | *Base 7" ** 1.14 mi. |
| | | P.C. Concrete*** | 2@24 | 9" | *** 0.48 mi. |
| | | Control Section | | | USTH-10 routed onto |
| 1999 | 6243 | Revision | | | new alignment. |
| | | | MN-118 | route | number is eliminated. |
| | | Milling | | | |
| 2010 | 6243-12 | Bit. Overlay | var. | 4" | Spec. 2360 |
| | | | | | Mi. based on WB |
| | | Grading | | | |
| 2015 | 6243-16 | Tension Cable | | | |
| | | Guardrail | | | Mi. based on EB |

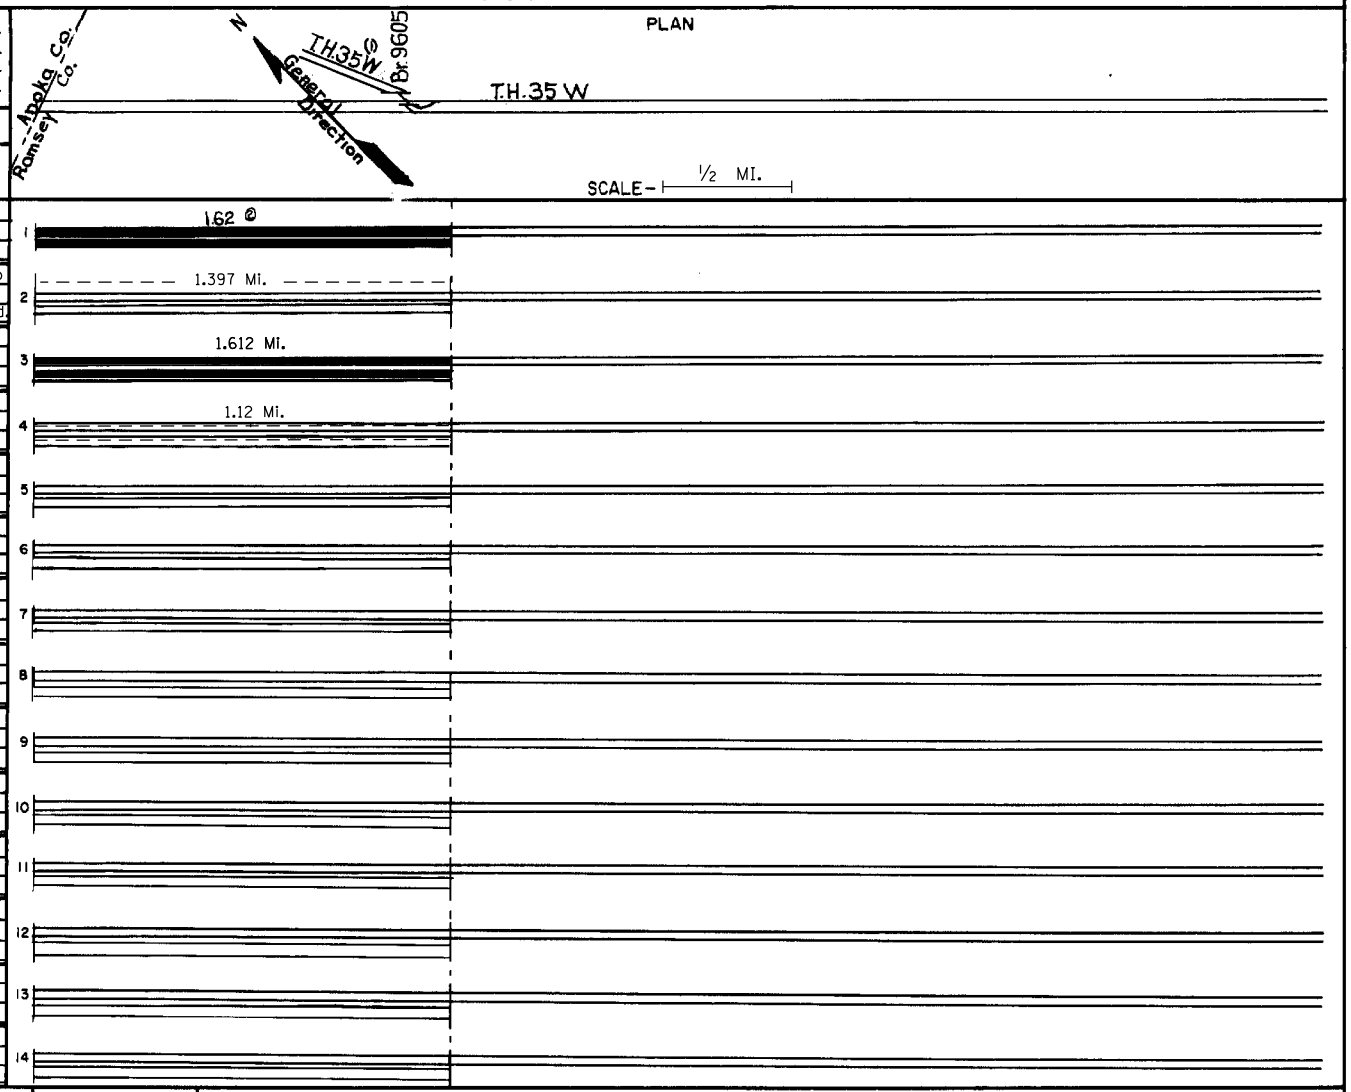


| YEARS FROM | YEARS TO | TOTAL MILES | UNINCORPORATED RDWY. MI. | UNINCORPORATED BR. MI. | INCORPORATED RDWY. MI. | INCORPORATED BR. MI. | RURAL RDWY. MI. | RURAL BR. MI. | URBAN RDWY. MI. | URBAN BR. MI. |
|---|---|---|---|---|---|---|---|---|---|---|
| 1972 | | 1.82 | 0.00 | 0.00 | 1.57 | 0.05 | 0.00 | 0.00 | 1.57 | 0.05 |

REMARKS: Layout is to scale as of 1972 (1) See 6284 Line 113 for Bridge Information. (2) In use Locally as of 1972.
